

Job Name: 25-4403 - Old Heritage Subdivision Section 6
 Job Location: Shelbyville, KY 40065
 Contractor: Filcon Construction

Plant: 100
 1/3/2026 12:54:23 PM

Tech: J. Hortsey - F
 PC: C. Goff



Structure ID: 12+70.40 LN 8

P3 GR24x24x8x3


GRADE RING F/F

- P4) 24" x 24" - CASTING HEIGHT - 3.50"
- P3) 24" x 24" - GRADE RING F/F - 3"
- P2) 48" - MH FLAT TOP w/24"x24" Hole F/G - 12"
- P1) 48" - MH BASE T/n - 42"
- 1) 48" - Conseal CS-102 1.00"
- 2) 24" x 24" - Conseal CS-102 1.00"
- 2) Hole - 30
- 3) MH Step ML-10-TDS-NCR - 10"

0 lb
 258 lb
 1500 lb
 3632 lb
 0 lb
 0 lb
 0 lb
 0 lb

 Structure Total: 5390 lb

Structure Notes:
 1. PER ASTM C-478 SPECIFICATIONS
 2. CONCRETE: 4,000 PSI AT 28 DAYS
 3. REINFORCEMENT: #3 BAR @ 4" C.C. E.W. (GRADE 60)

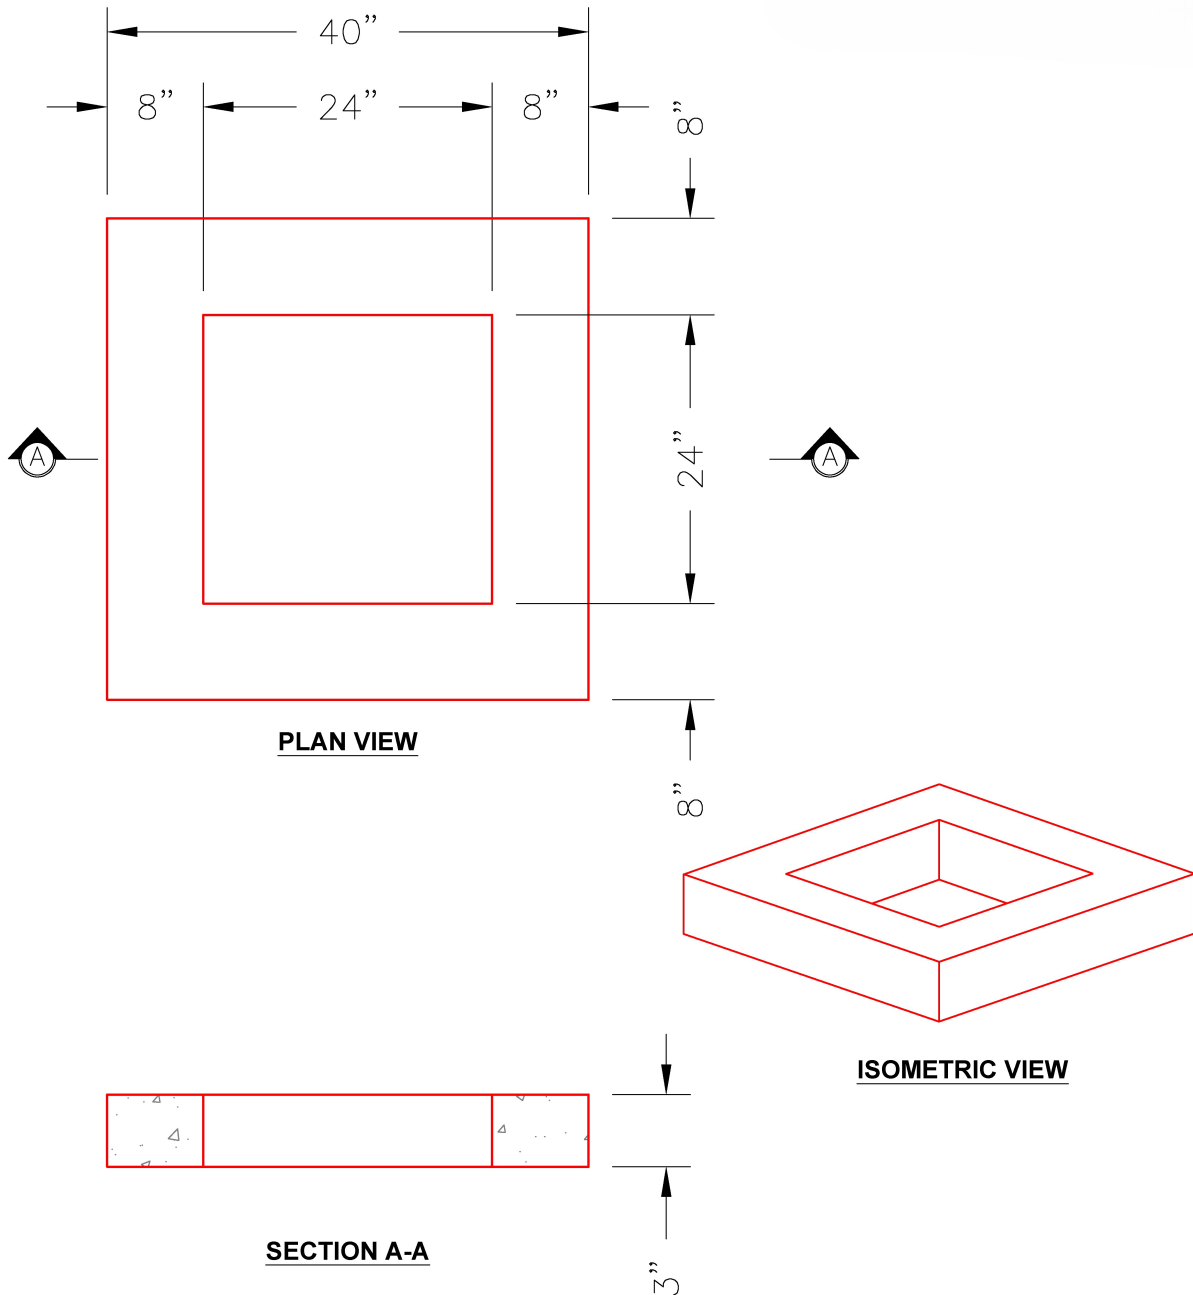

Coating (Int):
 Coating (Ext):

Seam Up: Flat
 Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 3"

Weight (Net): 258 lb
 Volume (Net): 0.07cu.yd
