

Job Name: 25-4405 Three Springs Rd Relocation  
 Job Location: Bowling Green, KY  
 Contractor: Cumberland Pipeline LLC

Plant: Beaver Dam

Tech: J. Coppage

2/2/2026 11:15:07 AM

PC: Celina Goff



**Structure ID: 3**

**P3 GR4**

**GRADE RING**

P4) 24" - CASTING HEIGHT - 7"

P3) 24" - GRADE RING - 4"

P2) 48" - ECC CONE w/ 24" HOLE - 42"

P1) 48" - MH BASE w/DROP - 42"

1) JOINT WRAP - 12" WD x 048" MAC WRAP

1) 48" - MH INVERT CHANNEL - FULL HEIGHT

1) 48" - Conseal CS-102 1.00" (Double)

2) A-Lok - 0285

1) Drop Tee - 8" PVC

1) Drop Elbow - 8" PVC

7) MH Step ML-10-TDS-NCR - 10"

0 lb

270 lb

3200 lb

4153 lb

0 lb

1440 lb

0 lb

2 lb

0 lb

0 lb

0 lb

-----

Structure Total: 9065 lb

Structure Notes:

1. JR HOE MC-375 SANITARY PROVIDED BY ICAST.

2. PER ASTM C478 SPECIFICATIONS.


3. CONCRETE = 4,000 PSI AT 28 DAYS.

4. REINFORCING PER ASTM A615 (GRADE 60).

- CONE (As .12)

- RISER/WALLS (As .12)

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

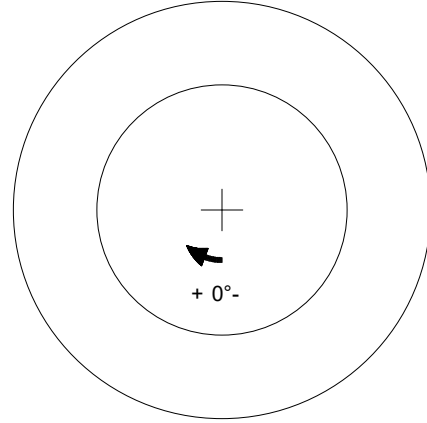

	24" - GRADE RING - 4" - (P3)	
--	------------------------------	--

Coating (Int):  
 Coating (Ext):

Seam Up: Flat  
 Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 4"

Weight (Net): 270 lb  
 Volume (Net): 0.07cu.yd
