

Job Name: 25-4419 - East Bank Reginal Pump Station Job Location: Nashville, TN 37213 Contractor: Garney Companies, Inc.	Plant: 100 1/28/2026 2:42:19 PM	Tech: J. Horsley - F PC: J. Jarvis	
---	------------------------------------	---------------------------------------	--

**Structure ID: ST106**

**P2 MH060RSVF**

**MH RISER Custom Ht T/G**



P4) 24" - CASTING HEIGHT - 7"	0 lb
P3) 60" - MH FLAT TOP w/ 24" ECC Hole F/G - 13"	2869 lb
P2) 60" - MH RISER Custom Ht T/G - 38"	3967 lb
P1) 60" - MH BASE T/n - 60"	7158 lb
1) CASTING - JBS 1150 F/C STORM	250 lb
2) 60" - Conseal CS-102 1.00"	0 lb
1) Hole - 40	0 lb
2) Hole - 34	0 lb
1) Hole - 22	0 lb
5) MH Step ML-10-TDS-NCR - 10"	0 lb
<b>Structure Total:</b>	<b>14244 lb</b>

**Structure Notes:**  
 1. PER ASTM C-478 SPECIFICATIONS  
 2. CONCRETE: 4,000 PSI AT 28 DAYS  
 3. REINFORCEMENT: PER ASTM A615  
 4. STEPS AT 235 DEGREES  
 5. JBS 1150 FRAME & COVER "STORM" SUPPLIED BY ICAST


Rim: 419.22' Rim to Invert: 9.62' Slack: 0.94" Sump: 3.5" Step Position: 235

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ( )	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

**RIGHT-SIDE UP VIEW (int. dimensions)**

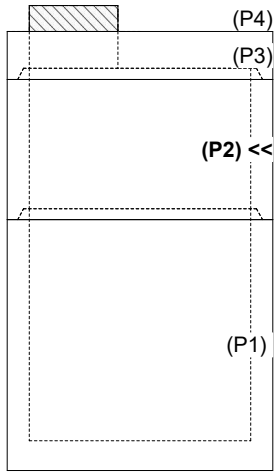

**INSIDE WALL DIMENSIONS**



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 6" Floor Height: 0"	Height (Int): 38" Height (Ext): 38"	Weight (Net): 3967 lb Volume (Net): 1.01cu.yd
----------------------------------	------------------------------------	--	--	--
