

Contractor: Kauffeld Brothers Construction

TECH: Jared - A

Plant: 100



Size: 48"

Rim to Invert: 9.4'

Floor Height: 6"


Slack: 1.8"

1. HOE MC-375 F/C "SANITARY" PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
 - CONE (As .12)
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


8) MH Step ML-10-TDS-NCR - 10"

0 lb


Structure Total: 10802 lb

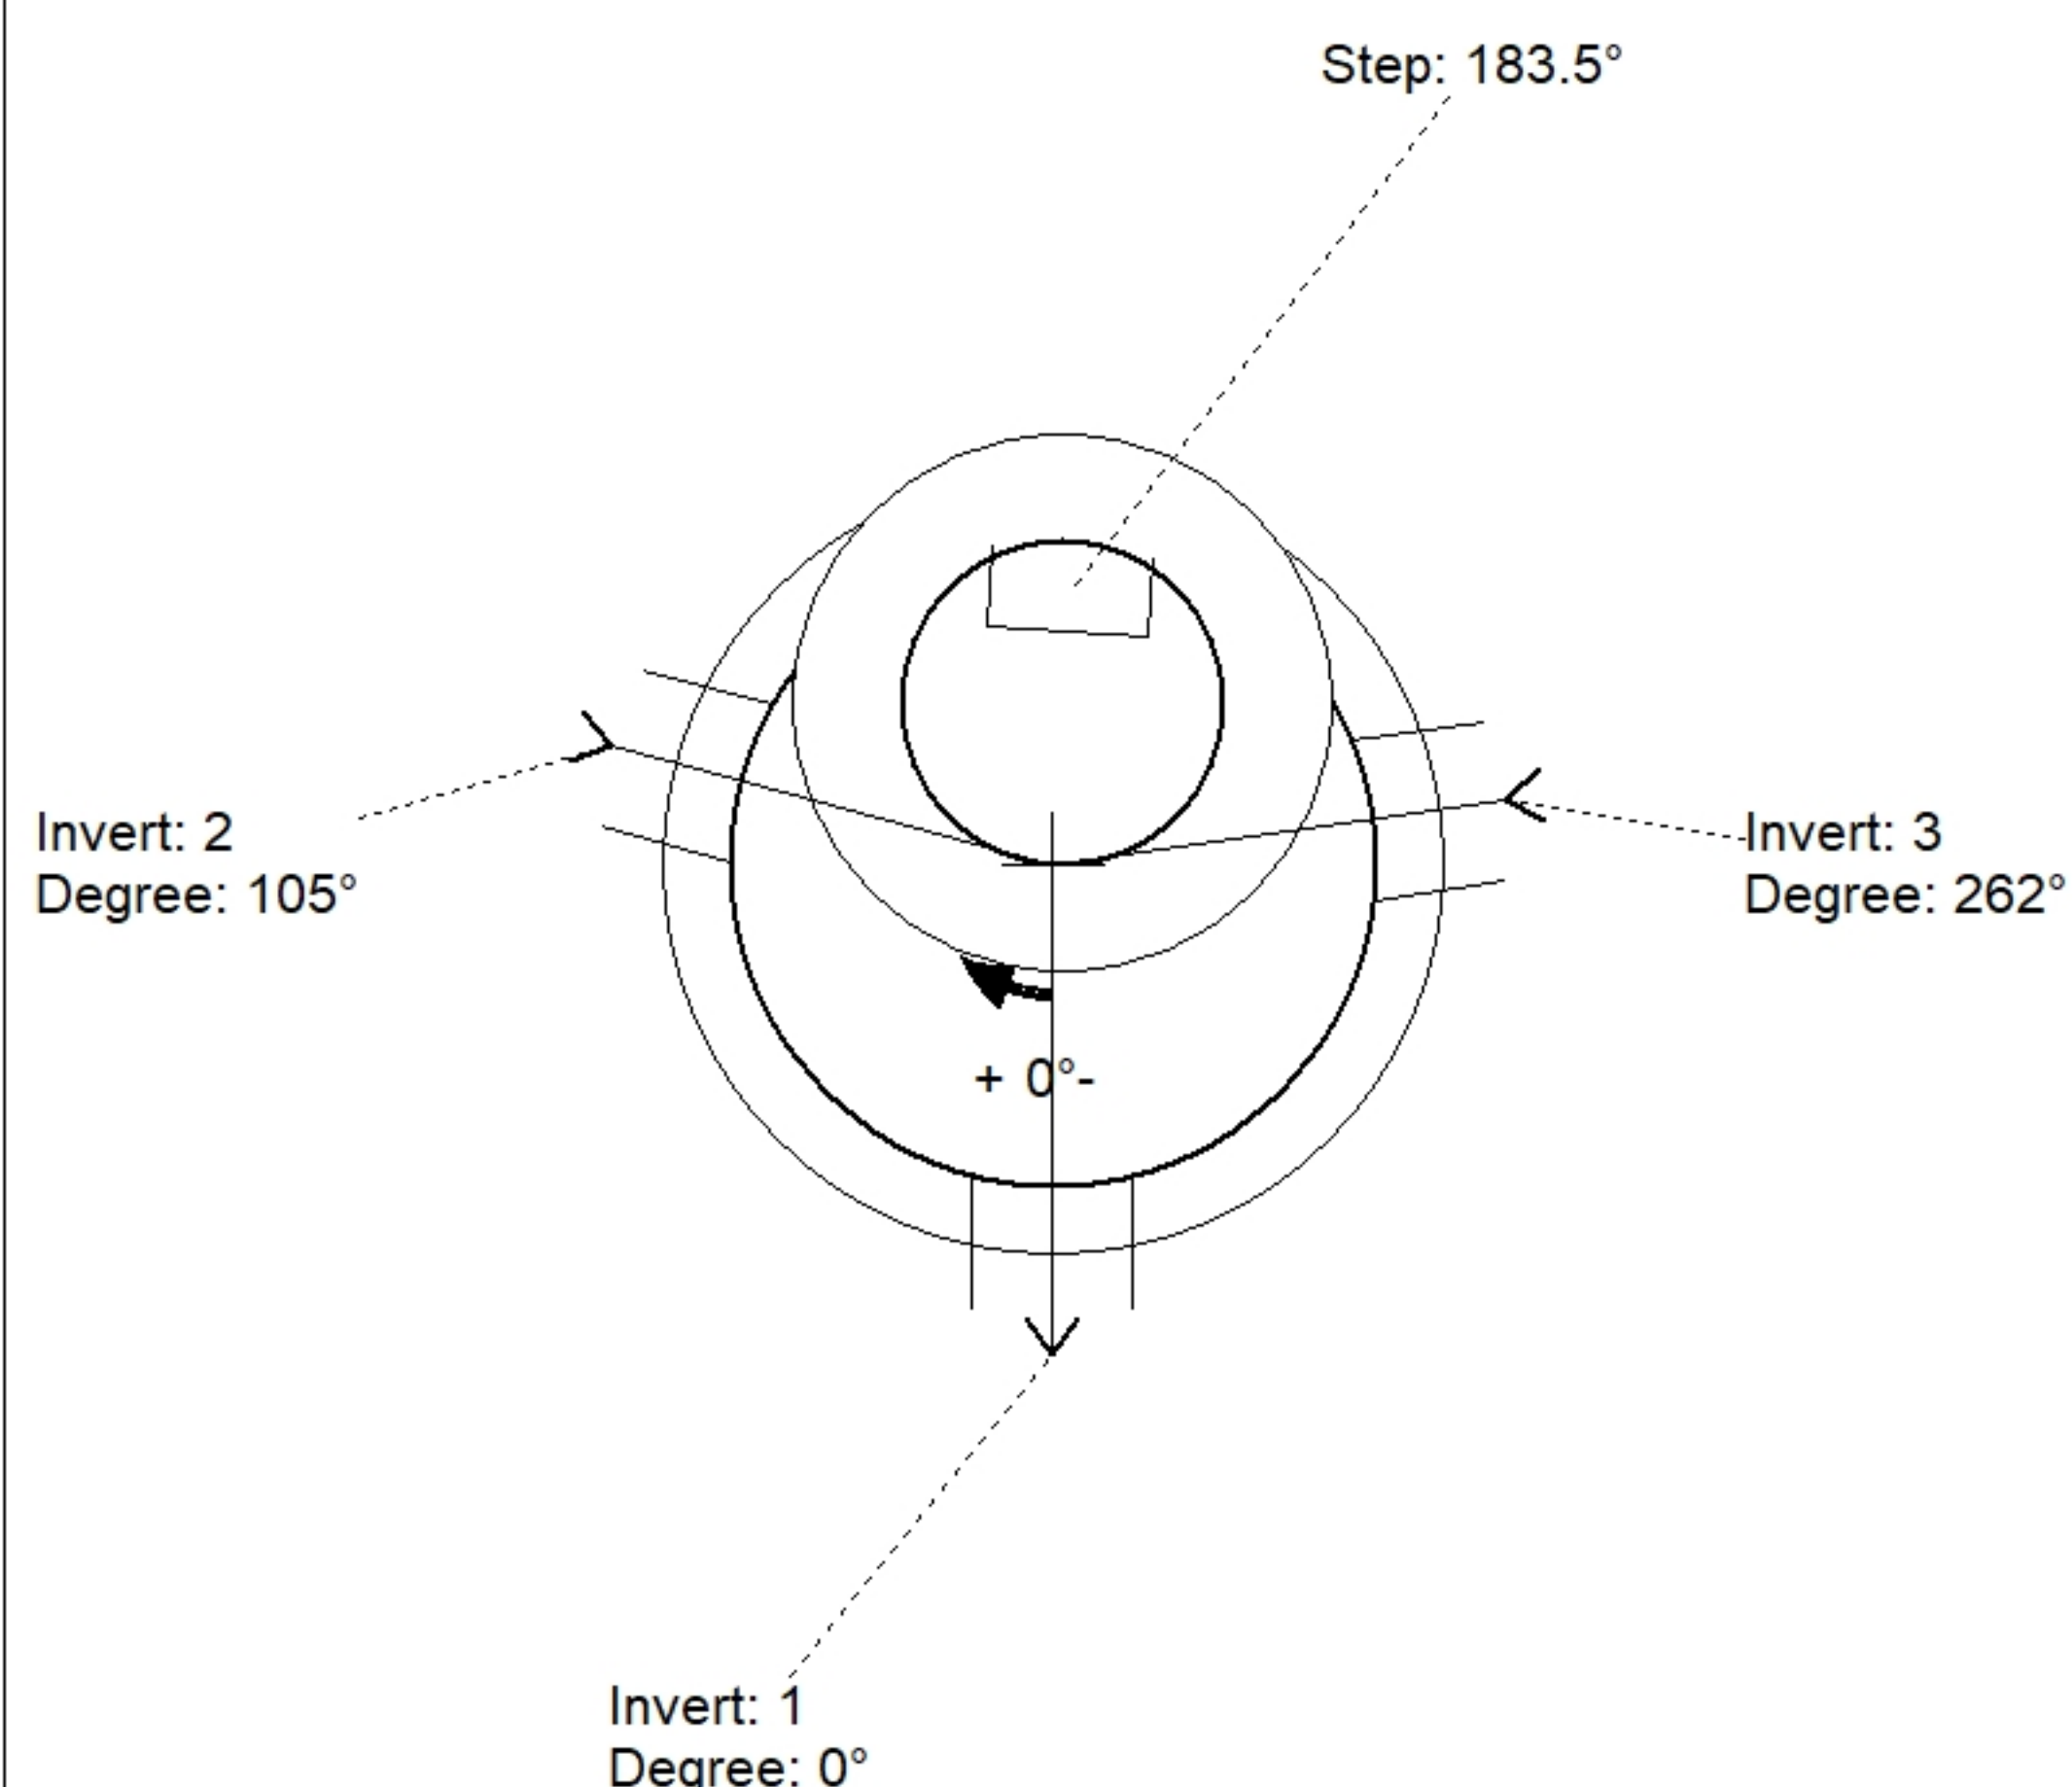

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	904.04'							
Reducer								
Invert 1	894.64'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	894.74'	105°	6" PVC SDR35	6.25"	12"	PSX 12-06 NYLO	0.2"	P1
Invert 3	894.74'	262°	6" PVC SDR35	6.25"	12"	PSX 12-06 NYLO	0.2"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

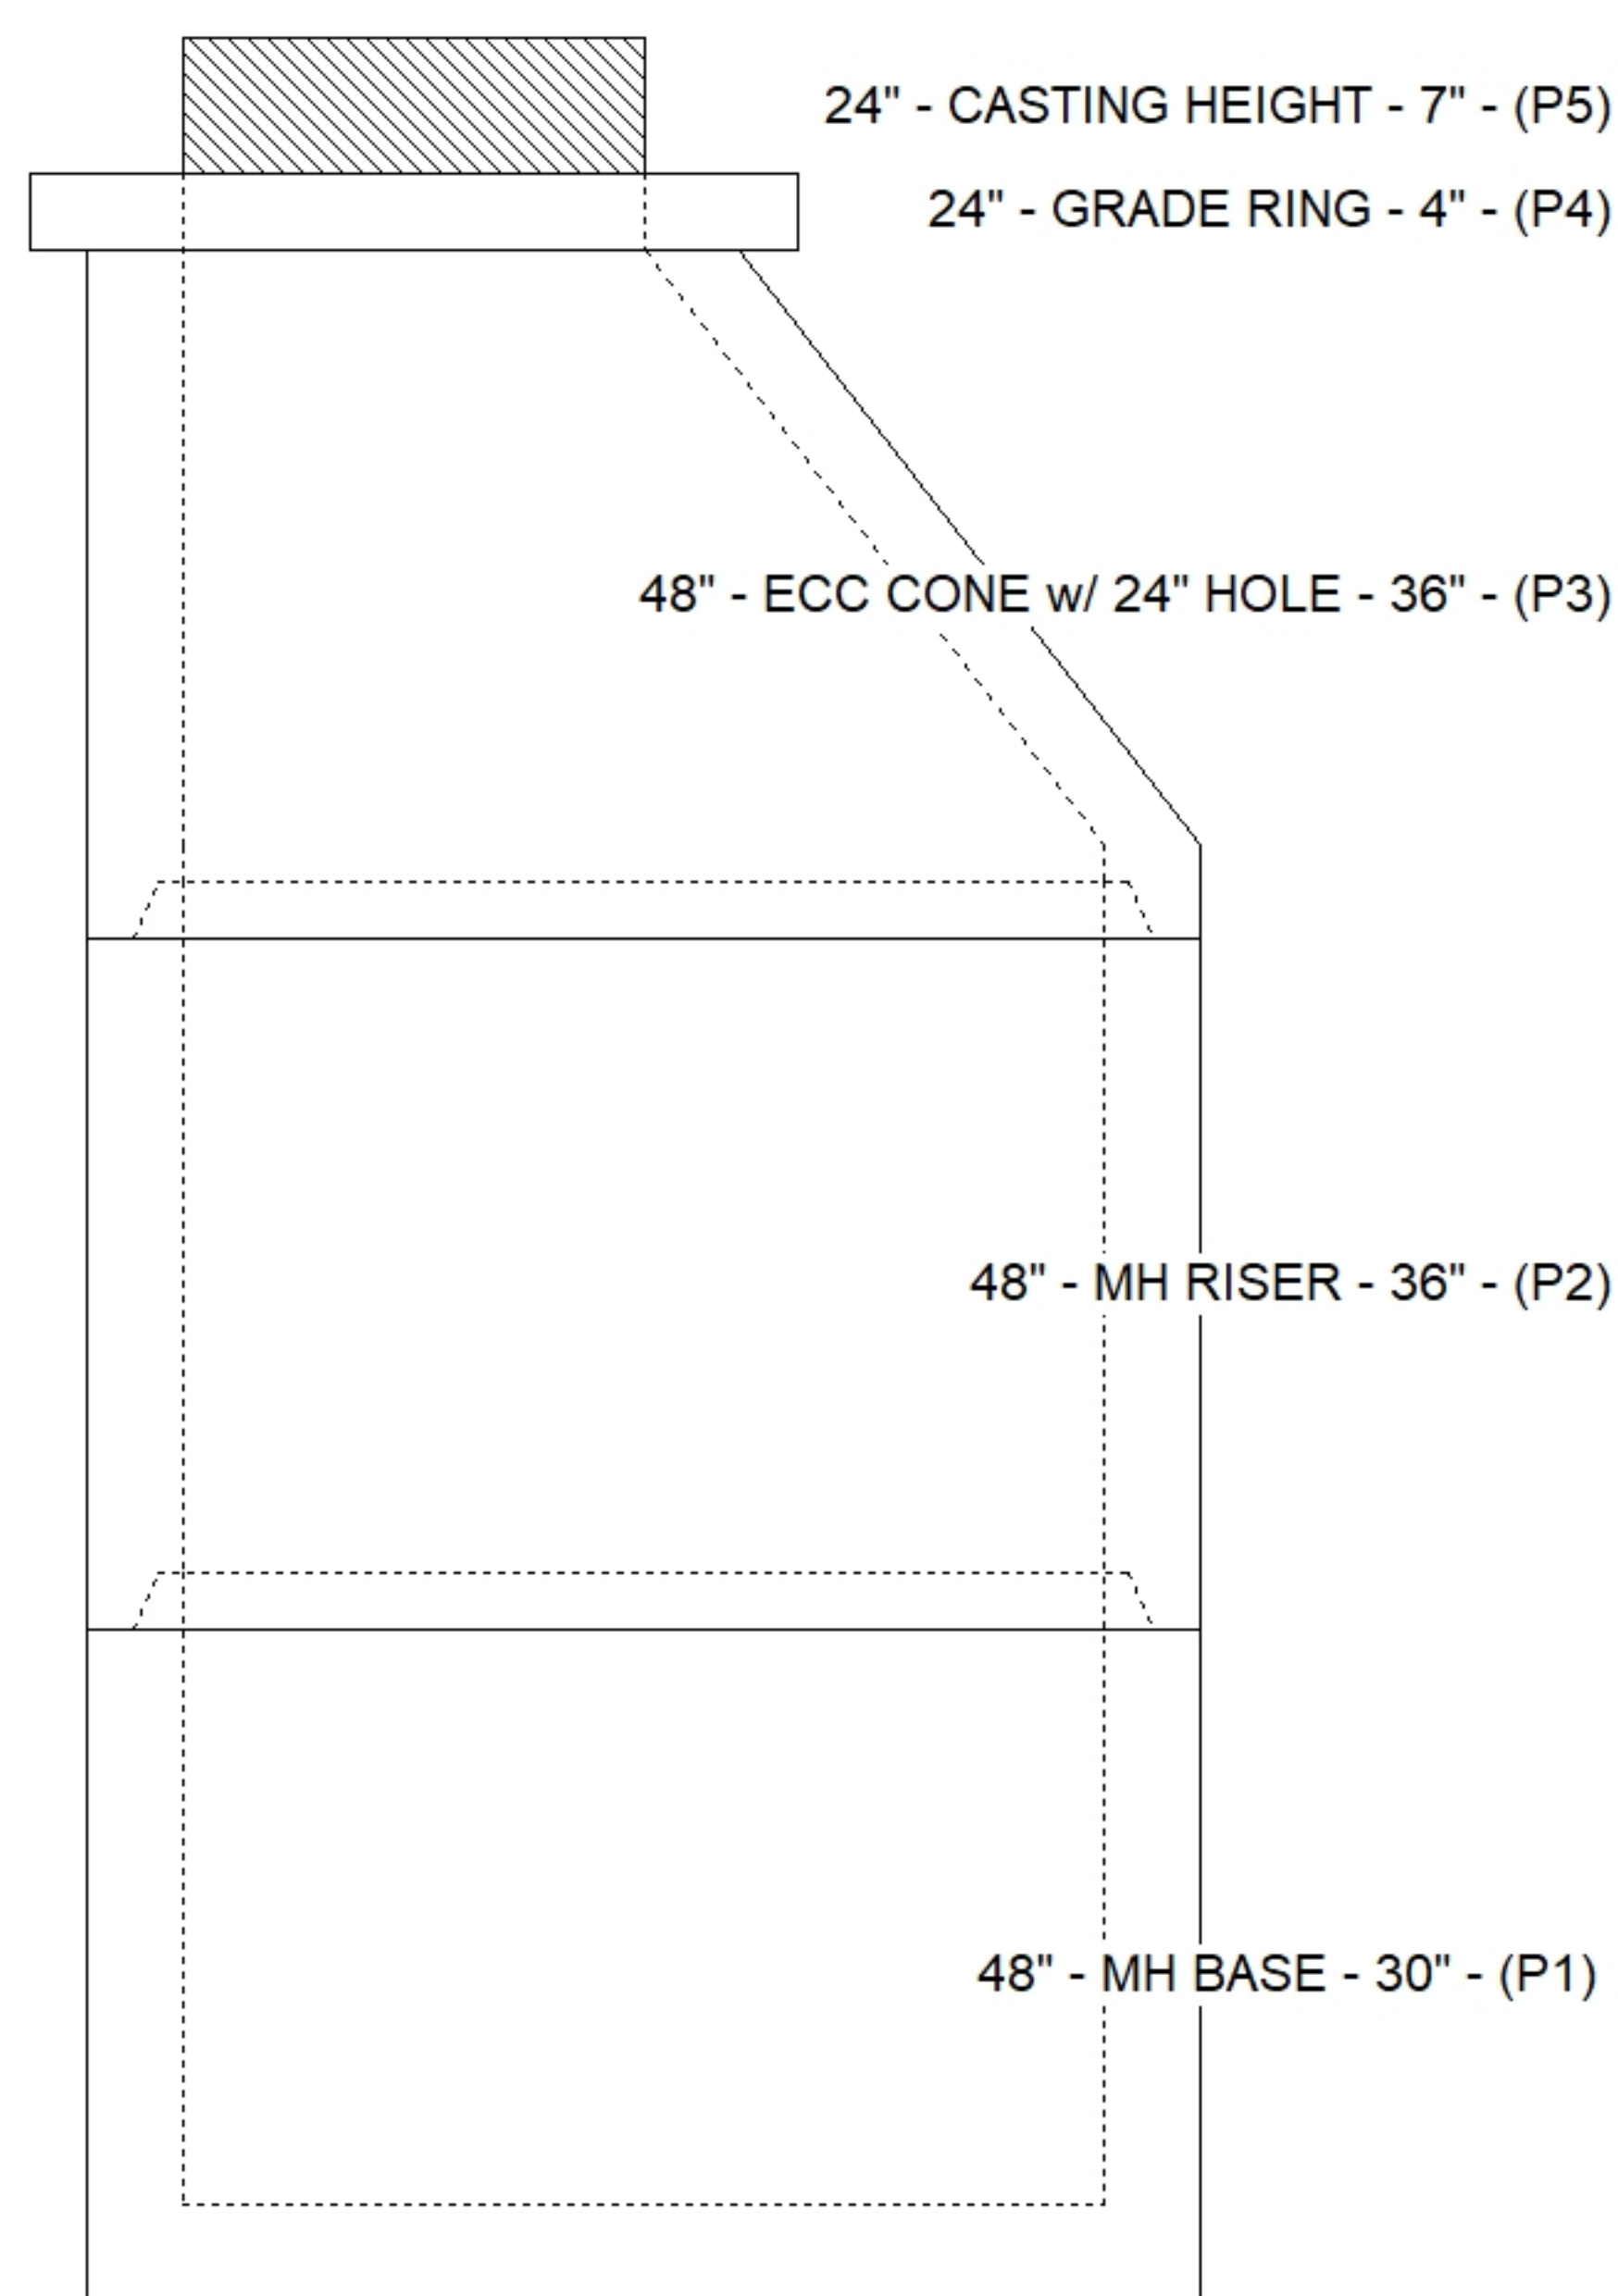

Default - Interior Dimensions

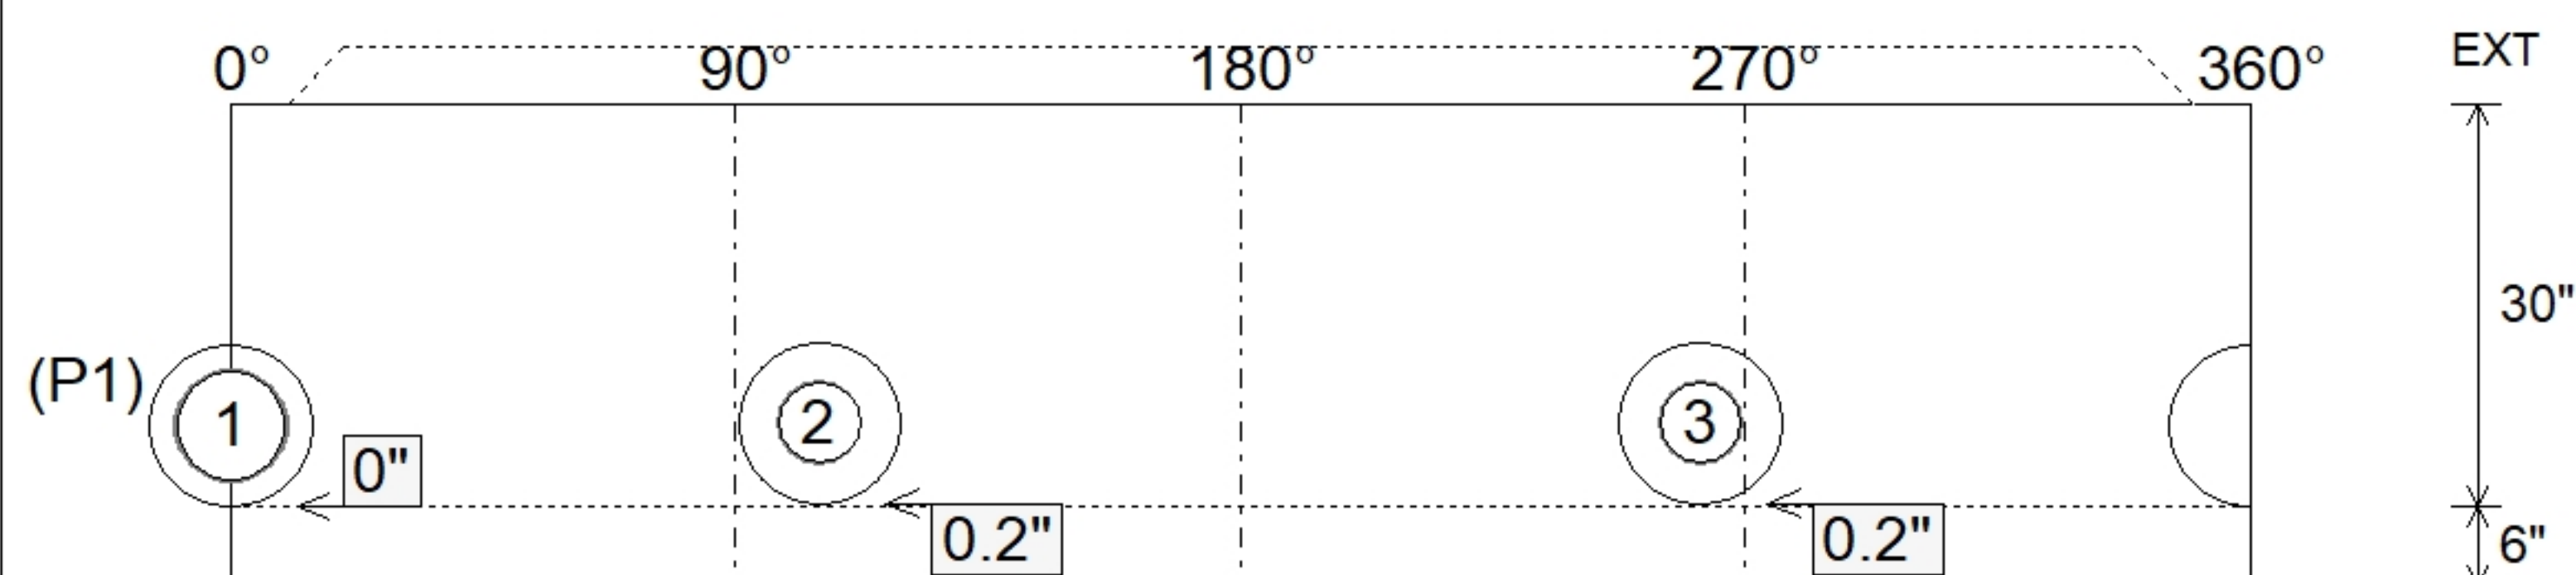

Submittal Drawing
7/27/2026 10:24:04 AM

SUBMITTAL
APPROVED BY:
