



Contractor: Kauffeld Brothers Construction

Plant: 100



Slack: 0.48"

Structure Total:	13527 lb
------------------	----------

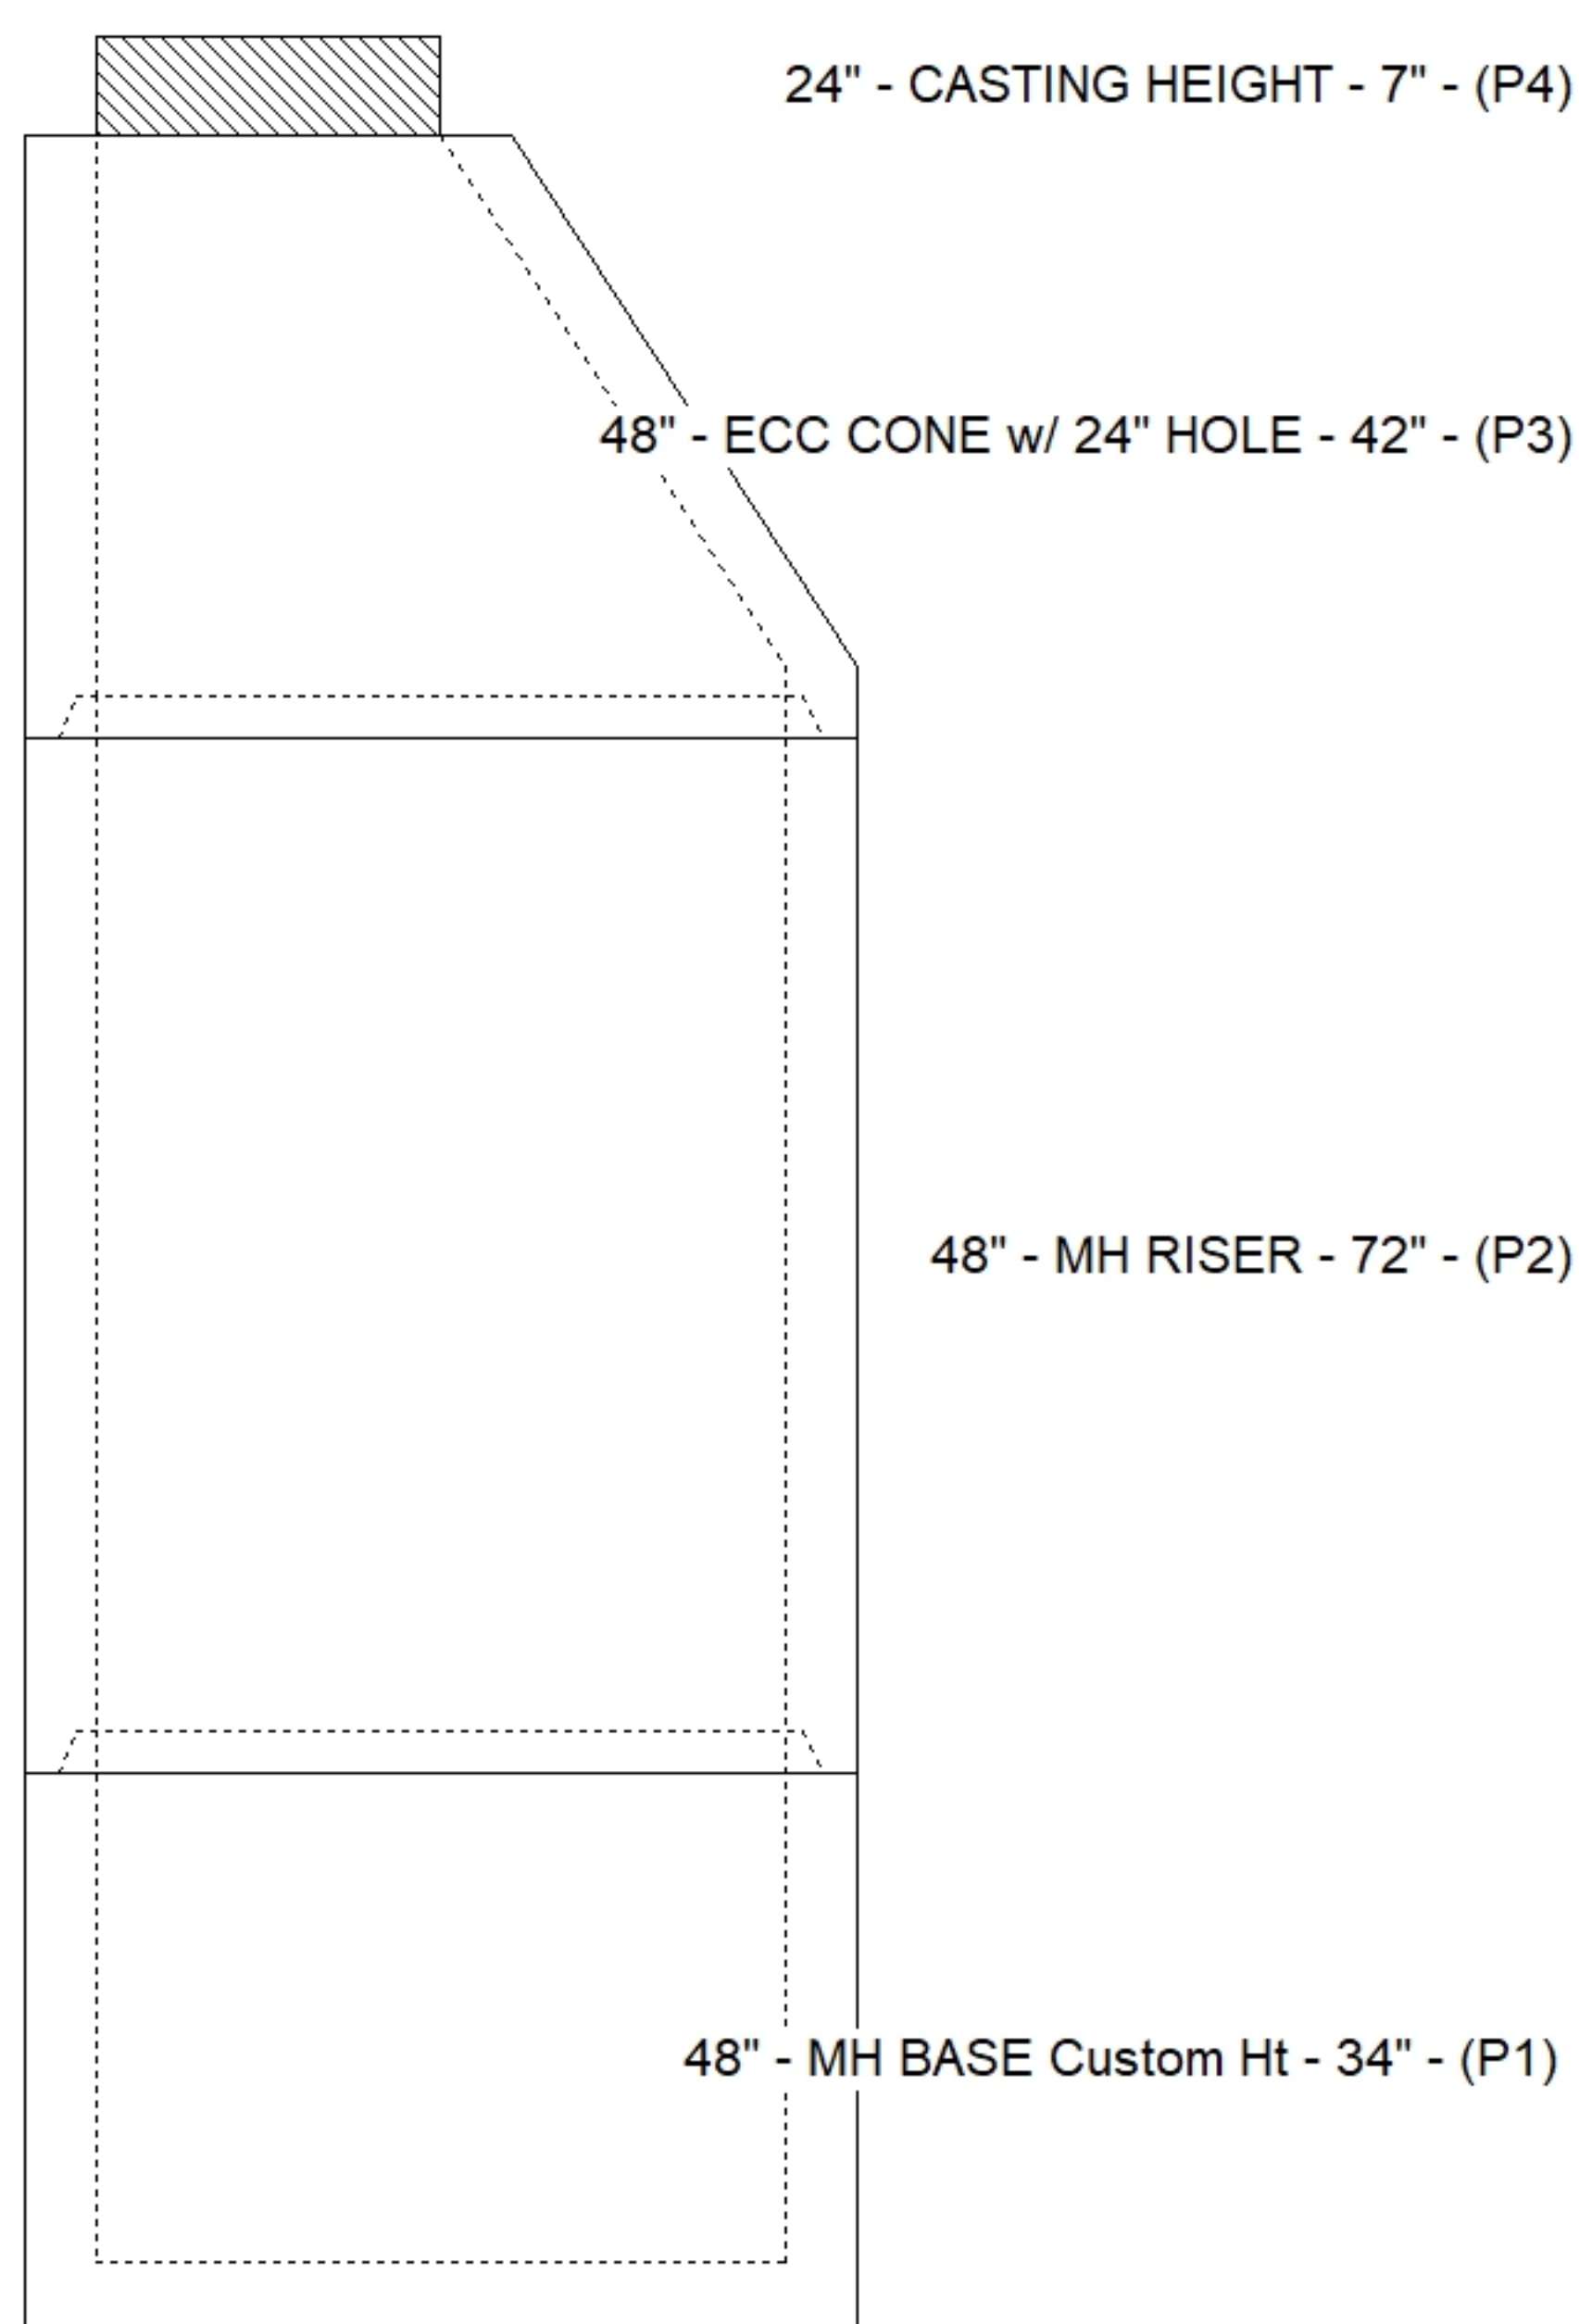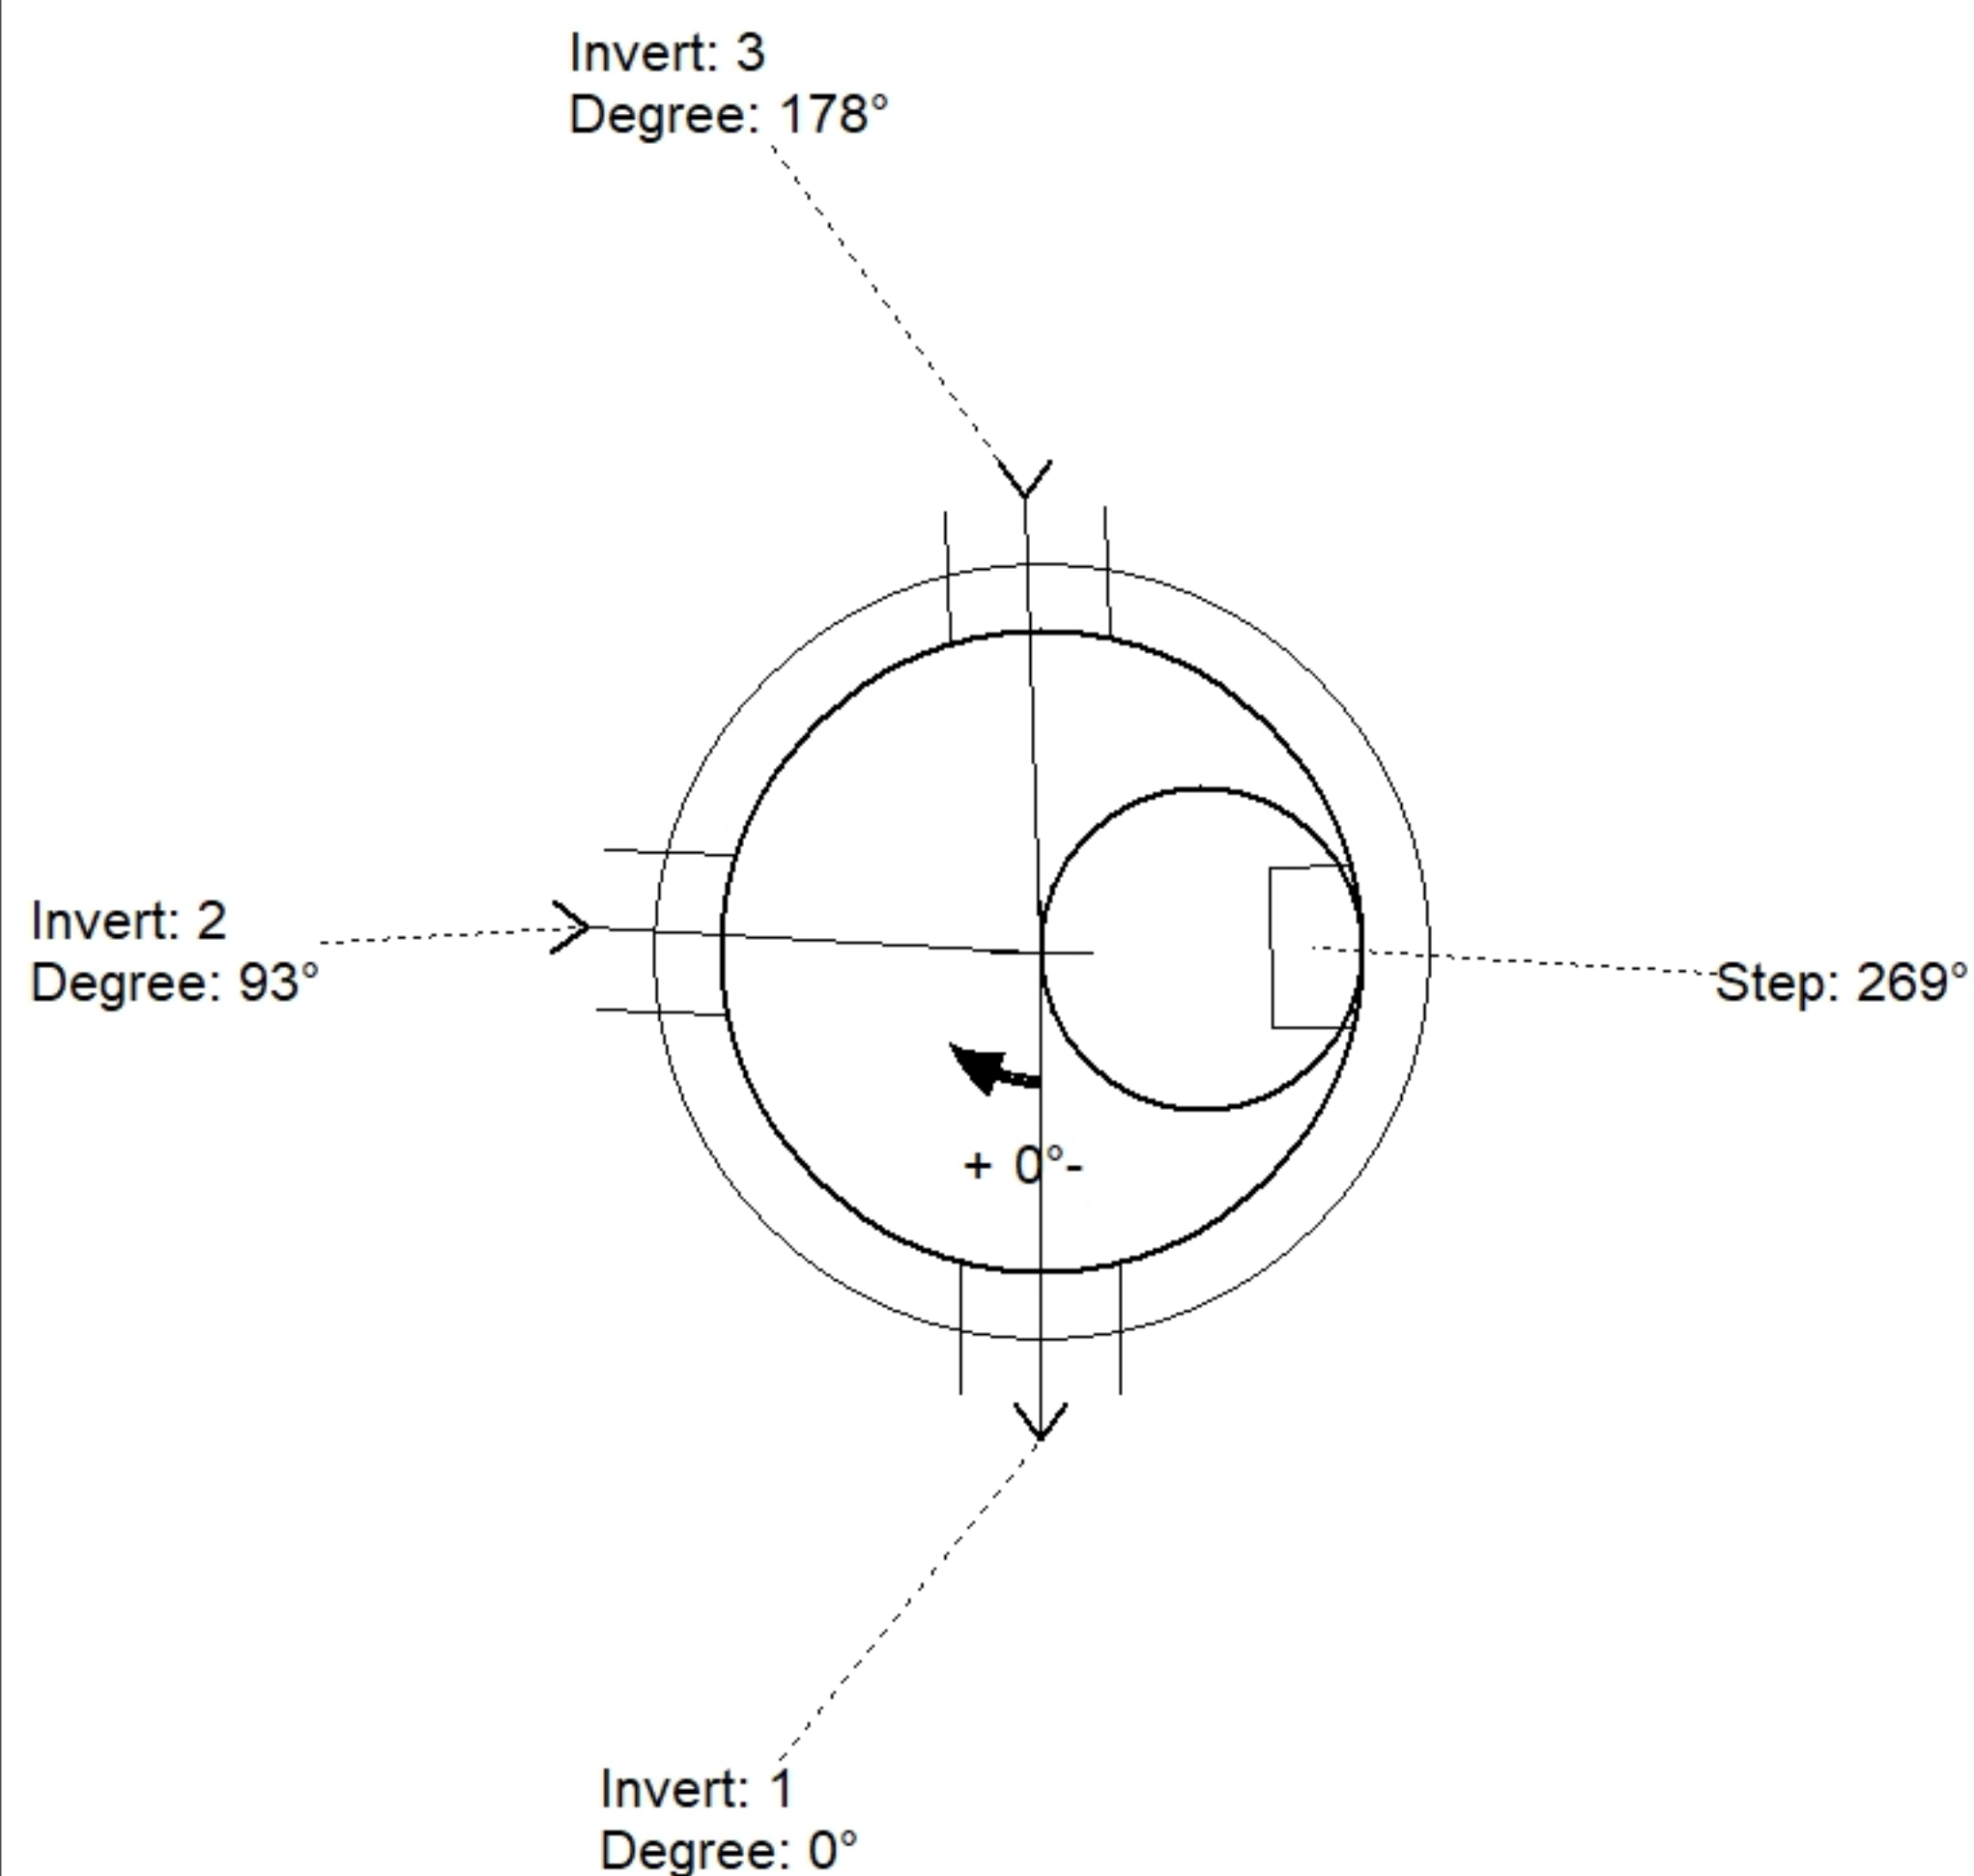

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	872.69'							
Reducer								
Invert 1	859.9'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	860'	93°	6" PVC SDR35	6.25"	12"	PSX 12-06 NYLO	0.2"	P1
Invert 3	860'	178°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	1.2"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

SUBMITTAL
APPROVED BY:
