


Contractor: Kauffeld Brothers Construction

Plant: 100




Slack: 0.52"

Structure Total:	17981 lb
------------------	----------

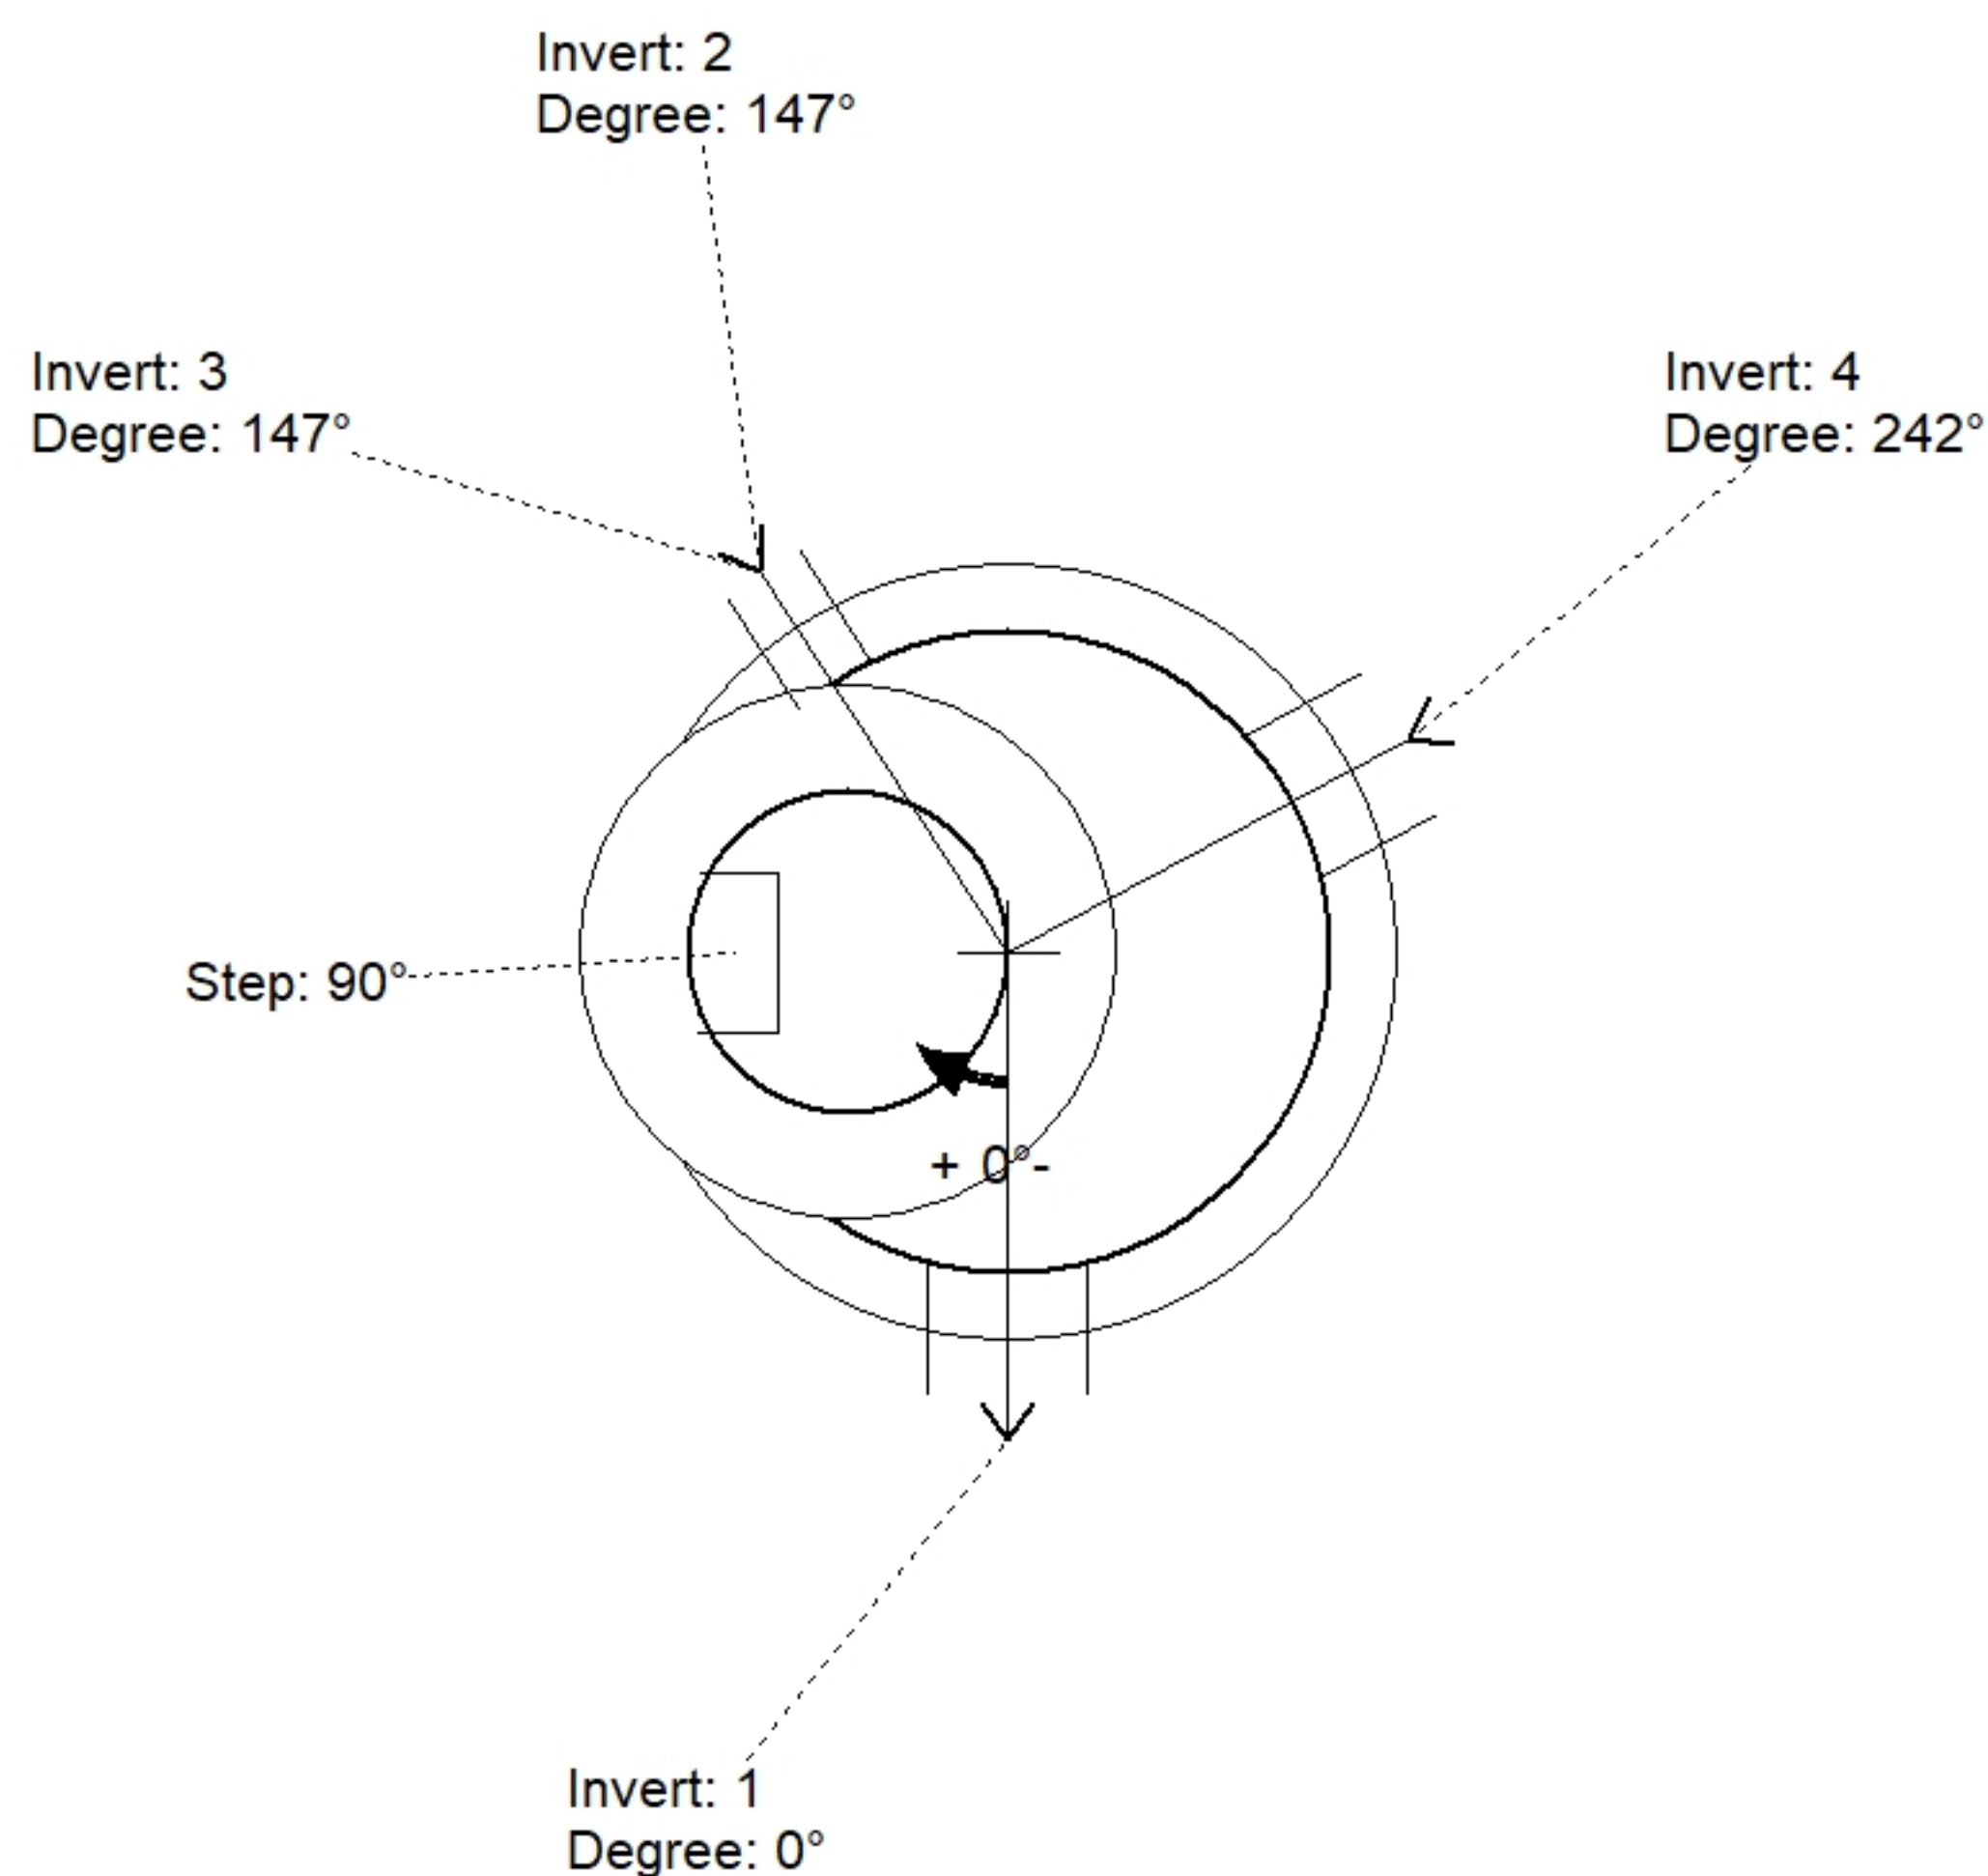

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	897.51'							
Reducer								
Invert 1	883.8'	0°	6" PVC SDR35	6.25"	12"	PSX 12-06 NYLO	0"	P1
Invert 2	883.9'	147°	6" PVC SDR35	6.25"	6.5"	Drop Elbow 6" PVC	3.95"	P1
Invert 3	888.66'	147°	6" PVC SDR35	6.25"	6.5"	Drop Tee 6" PVC	26.82"	P2
Invert 4	883.9'	242°	6" PVC SDR35	6.25"	12"	PSX 12-06 NYLO	1.2"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

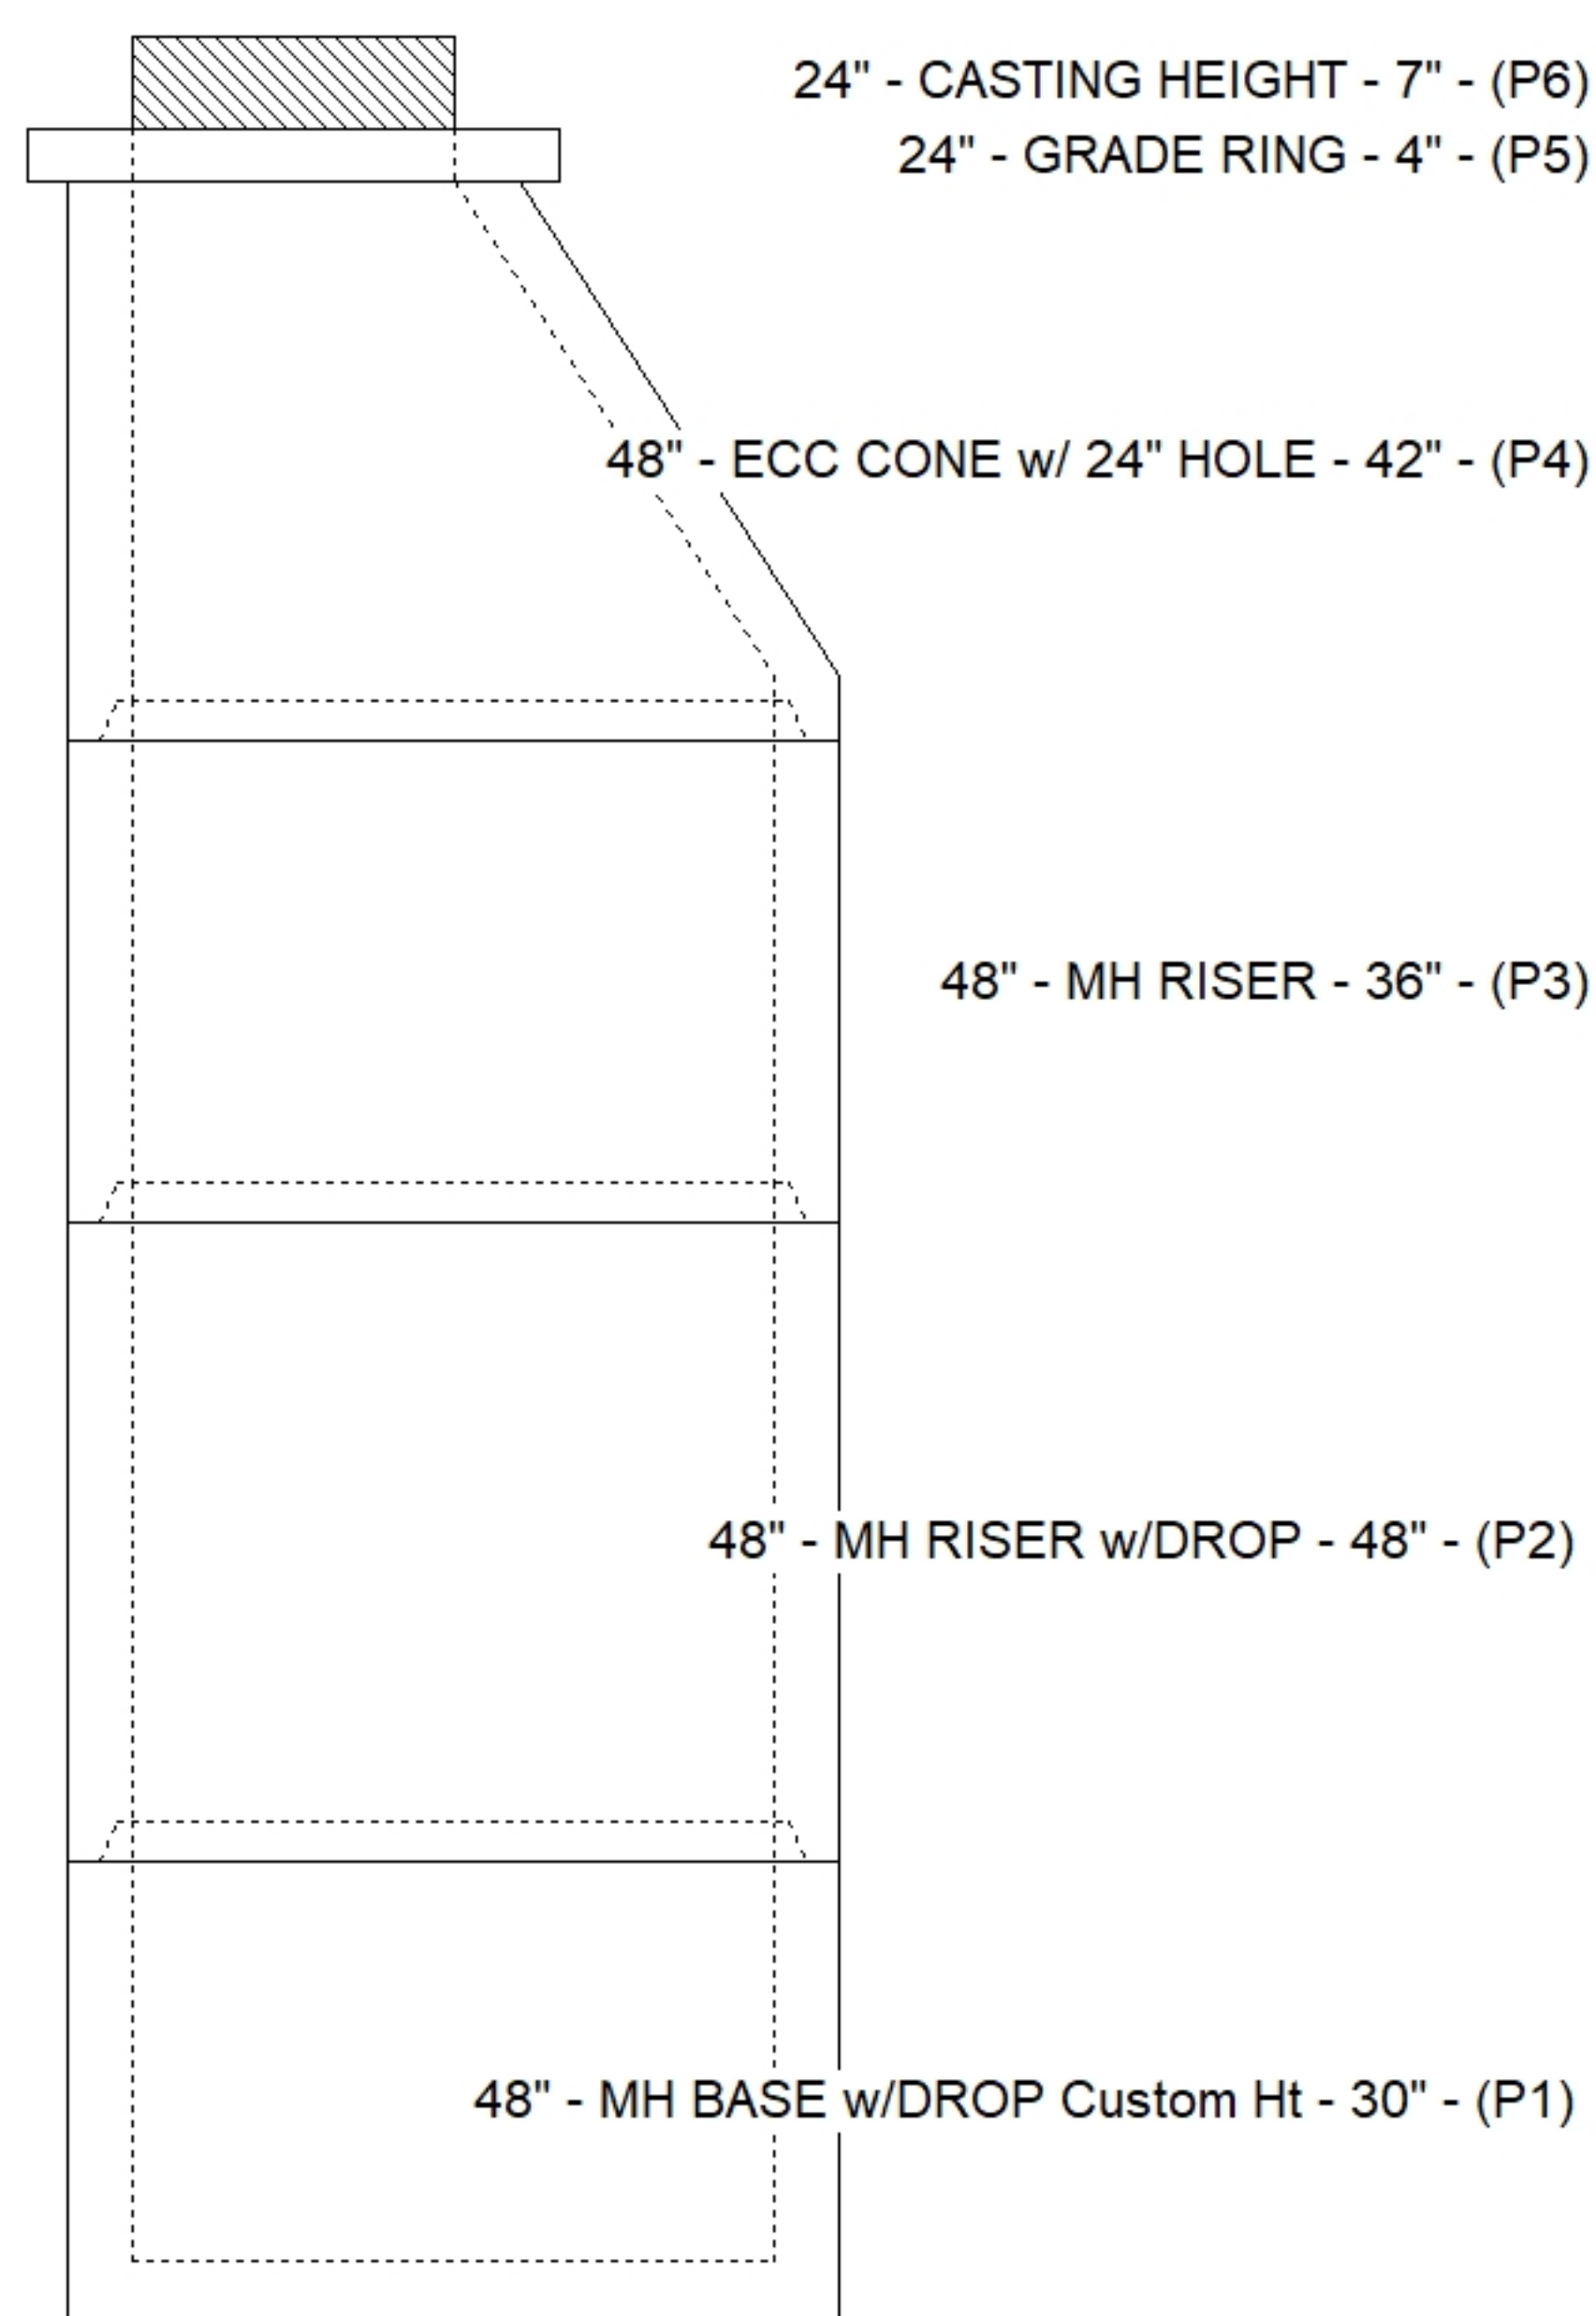

SUBMITTAL
APPROVED BY:
