

Job Name: 25-4490P1 Heartland Meadows Subdivision
Job Location: Elizabethtown, KY 40165
Contractor: Kauffeld Brothers Construction

Plant: 100

7/23/2026 12:04:58 PM

Tech: Jared - A

PC: Celina Goff



Structure ID: MH 2-9 (10)


P2 MH048LD12ECC

MH FLAT TOP w/ 24" ECC Hole

- P3) 24" - CASTING HEIGHT - 7"
P2) 48" - MH FLAT TOP w/ 24" ECC Hole - 12"
P1) 48" - MH BASE Custom Ht - 23"
- 1) 48" - MH INVERT CHANNEL - FULL HEIGHT
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) CASTING - HOE MC-375 F/C Sanitary
1) 48" - Conseal CS-102 1.00" (Double)
1) 24" - Conseal CS-102 1.00" (Double)
1) PSX - 12-08 NYLO
2) PSX - 12-06 NYLO
1) MH Step ML-10-TDS-NCR - 10"


0 lb	Structure Notes:
1561 lb	1. HOE MC-375 F/C "SANITARY" PROVIDED BY ICAST.
2793 lb	2. PER ASTM C478 SPECIFICATIONS.
1440 lb	3. CONCRETE = 4,000 PSI AT 28 DAYS.
0 lb	4. REINFORCING PER ASTM A615 (GRADE 60).
0 lb	- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
271 lb	- RISER/WALLS (As .12)
0 lb	- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
0 lb	
8 lb	
16 lb	
0 lb	

6089 lb	

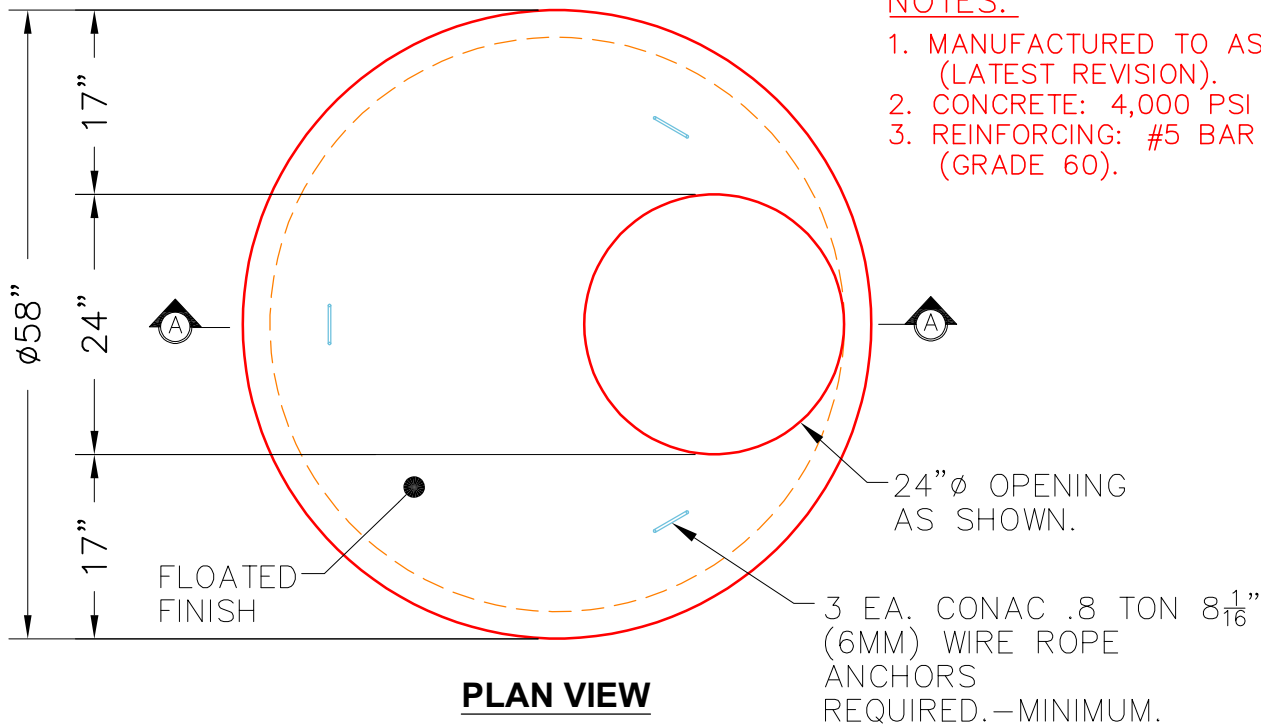

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" C.C. E.W. (GRADE 60).

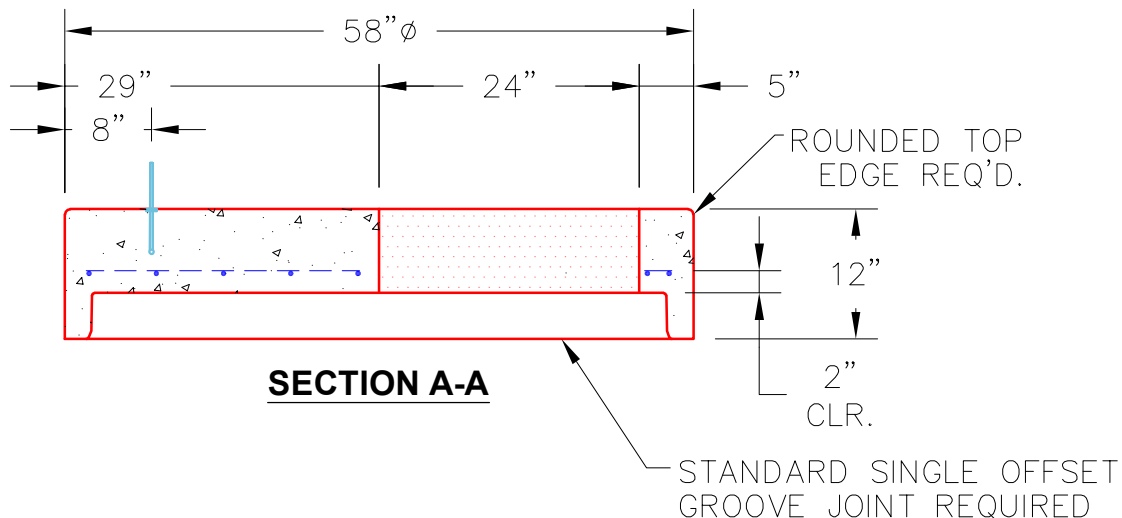

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1561 lb
Volume (Net): 0.42cu.yd
