


Job Name: 25-4490P2 Heartland Meadows Subdivision Job Location: Elizabethtown, KY 40165 Contractor: Kauffeld Brothers Construction					Plant: 100 7/30/2026 10:22:34 AM		Tech: Jared - A PC: Celina Goff				
Structure ID: CB 1-13 (25)											
P1		MH060BAVF		MH BASE Custom Ht							
P3) 34" x 34" - CASTING HEIGHT - 3" P2) 60" - MH FLAT TOP w/34"x34" Hole - 8" P1) 60" - MH BASE Custom Ht - 42" 1) CASTING - HOE 595 F/G 1) 60" - Conseal CS-102 1.00" 2) DOGHOUSE INVRTD - 40"x42"					0 lb 1957 lb 5153 lb 376 lb 0 lb 0 lb ----- Structure Total: 7486 lb		Structure Notes: 1. HOE 595 F/G PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.				
Rim: 862.34' Rim to Invert: 4.25' Slack: 0.55" Sump: 2.55" Step Position: 247.5°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	858.09'	0°	0"	30" HDPE	35.1"	DOGHOUSE INVRTD 40"x42"	40" x 42"	43.784", 26.87"	0"	0"	
Invert 2	858.09'	135°	84.823"	30" HDPE	35.1"	DOGHOUSE INVRTD 40"x42"	40" x 42"	43.784"	0"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

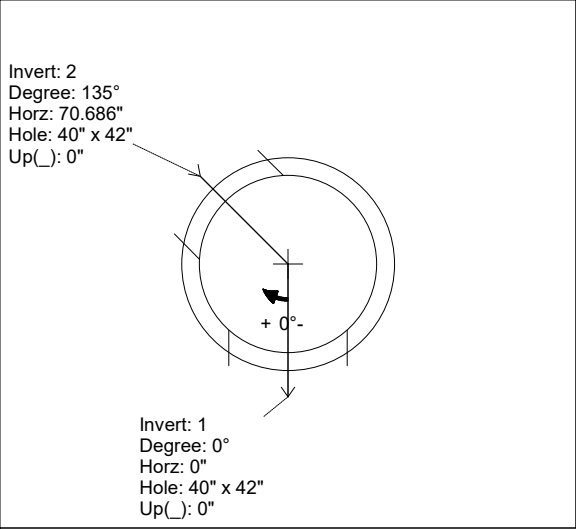

Invert: 2
Degree: 135°
Horz: 70.686"
Hole: 40" x 42"
Up(): 0"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 40" x 42"
Up(): 0"


UPSIDE-DOWN VIEW (int. dimenions)

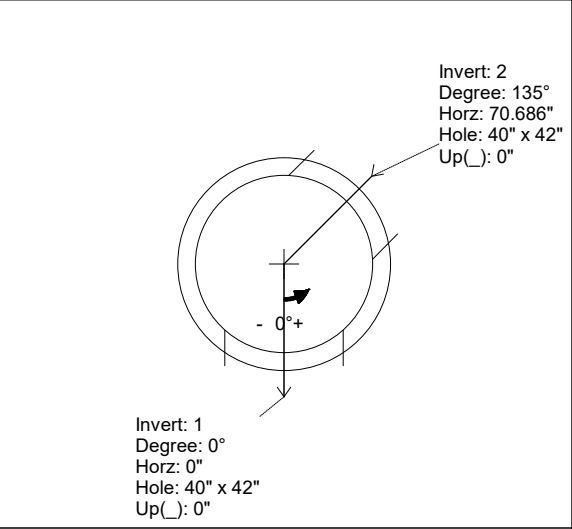

Invert: 2
Degree: 135°
Horz: 70.686"
Hole: 40" x 42"
Up(): 0"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 40" x 42"
Up(): 0"

INSIDE WALL DIMENSIONS

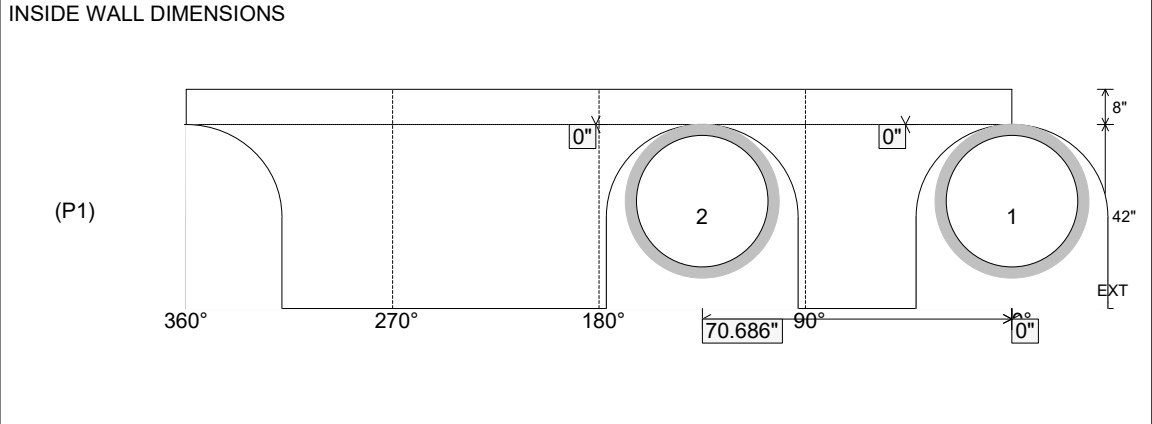

(P1)

360° 270° 180° 90°

70.686" 0"

8" 42" EXT

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 6" Floor Height: 8"	Height (Int): 42" Height (Ext): 50"	Weight (Net): 5153 lb Volume (Net): 1.32cu.yd
----------------------------------	-------------------------------	--	--	--
