

Job Name: 25-4490P2 Heartland Meadows Subdivision
Job Location: Elizabethtown, KY 40165
Contractor: Kauffeld Brothers Construction

Plant: 100

7/30/2026 10:24:41 AM

Tech: Jared - A
PC: Celina Goff



Structure ID: CB 1-13 (25)

P2 MH060LD08SP



MH FLAT TOP w/34"x34" Hole

P3) 34" x 34" - CASTING HEIGHT - 3"
P2) 60" - MH FLAT TOP w/34"x34" Hole - 8"
P1) 60" - MH BASE Custom Ht - 42"
1) CASTING - HOE 595 F/G
1) 60" - Conseal CS-102 1.00"
2) DOGHOUSE INVRTD - 40"x42"

0 lb
1957 lb
5153 lb
376 lb
0 lb
0 lb

Structure Total: 7486 lb

Structure Notes:
1. HOE 595 F/G PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

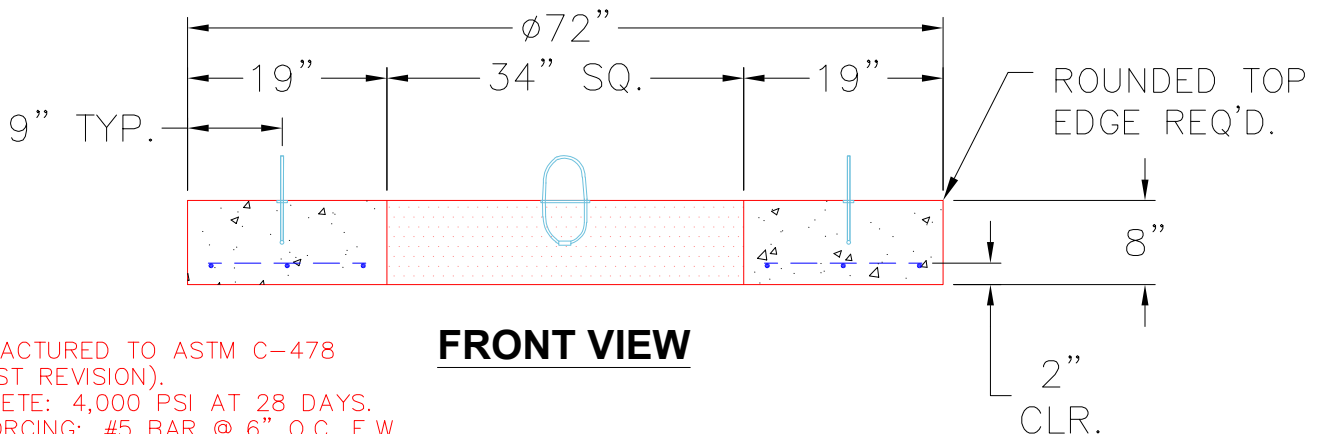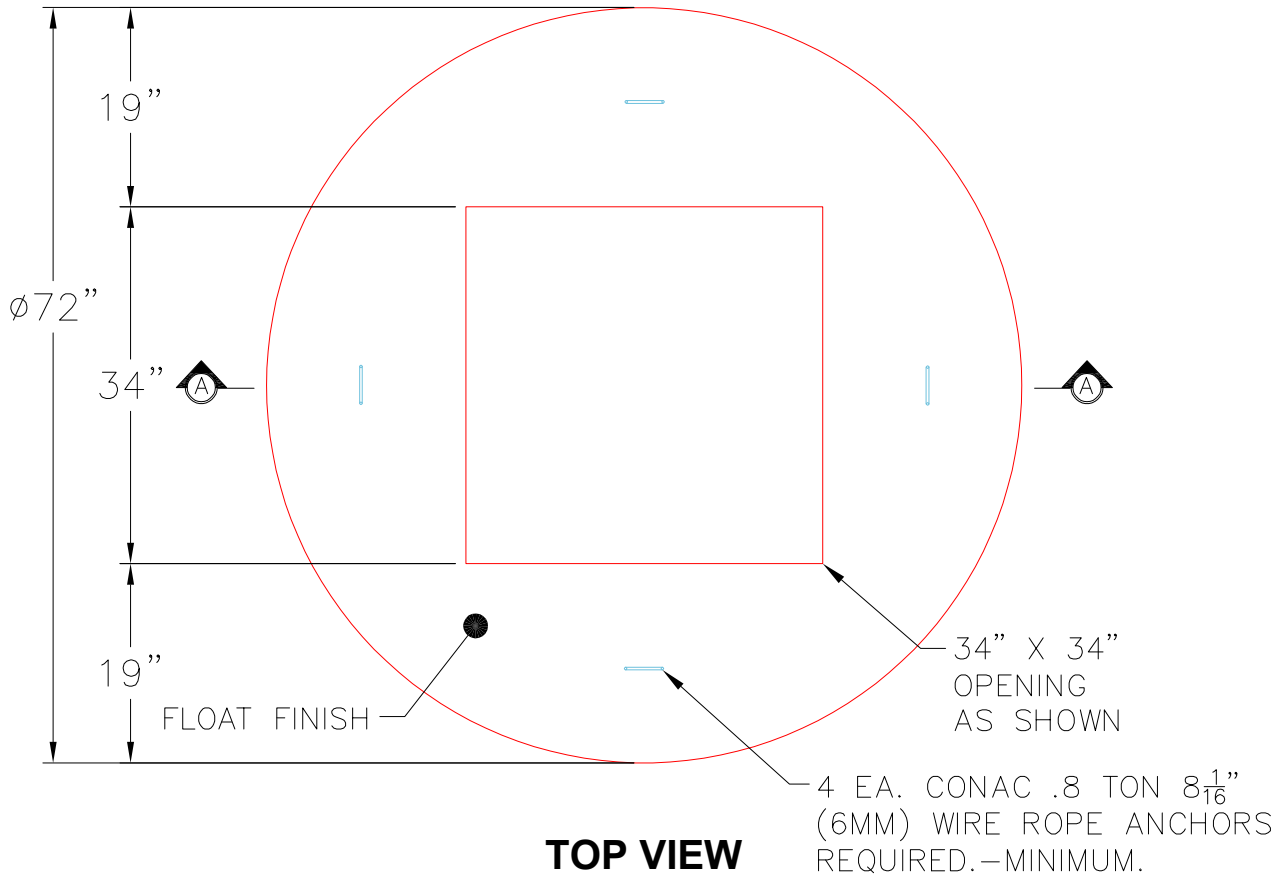

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 6"

Height (Ext): 8"

Weight (Net): 1957 lb
Volume (Net): 0.5cu.yd
