

Contractor: Kauffeld Brothers Construction

Plant: 100



Size: 24" x 36"

Rim to Invert: 3.71'

Floor Height: 8"


Slack: 0.52"

1. HOE 470 FLAT SET PROVIDED BY ICAST.
2. PER ASTM C913 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. NO INVERT CHANNEL.
5. REINFORCING PER ASTM A615 (GRADE 60).
 - WALLS (As .12) #5 BARS AT 12" C.C.E.W.
 - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

P2) 24" x 36" - CASTING HEIGHT - 6"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 38"
1) CASTING - HOE 470 SET LV (F/G/H)
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 18

0 lb
5103 lb
394 lb
0 lb
0 lb

Structure Total: 5497 lb

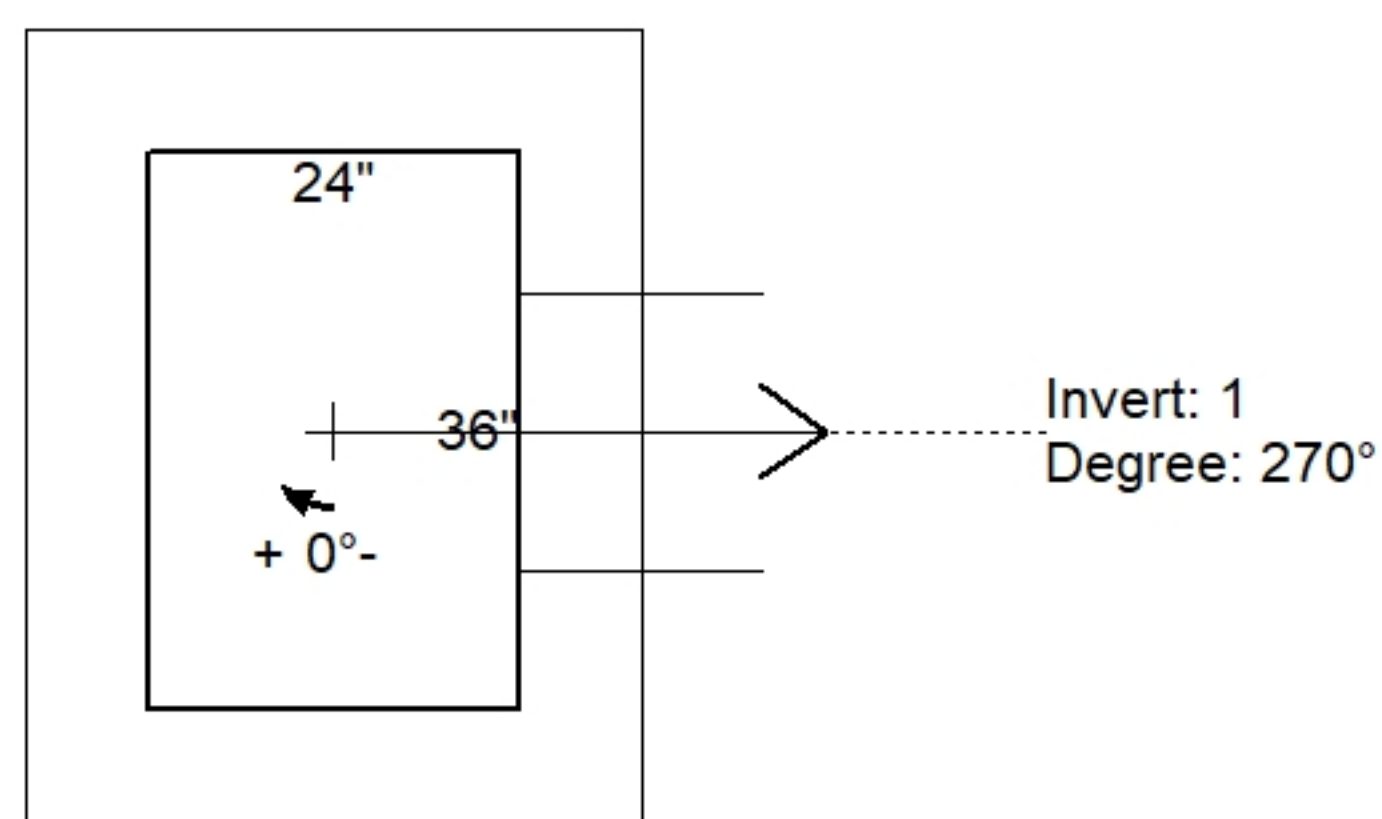


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	885.28'							
Reducer								
Invert 1	881.57'	270°	12" HDPE	14.5"	18"	Hole 18	-1.25"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 36" - CASTING HEIGHT - 6" - (P2)

24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 38" - (P1)

Default - Interior Dimensions

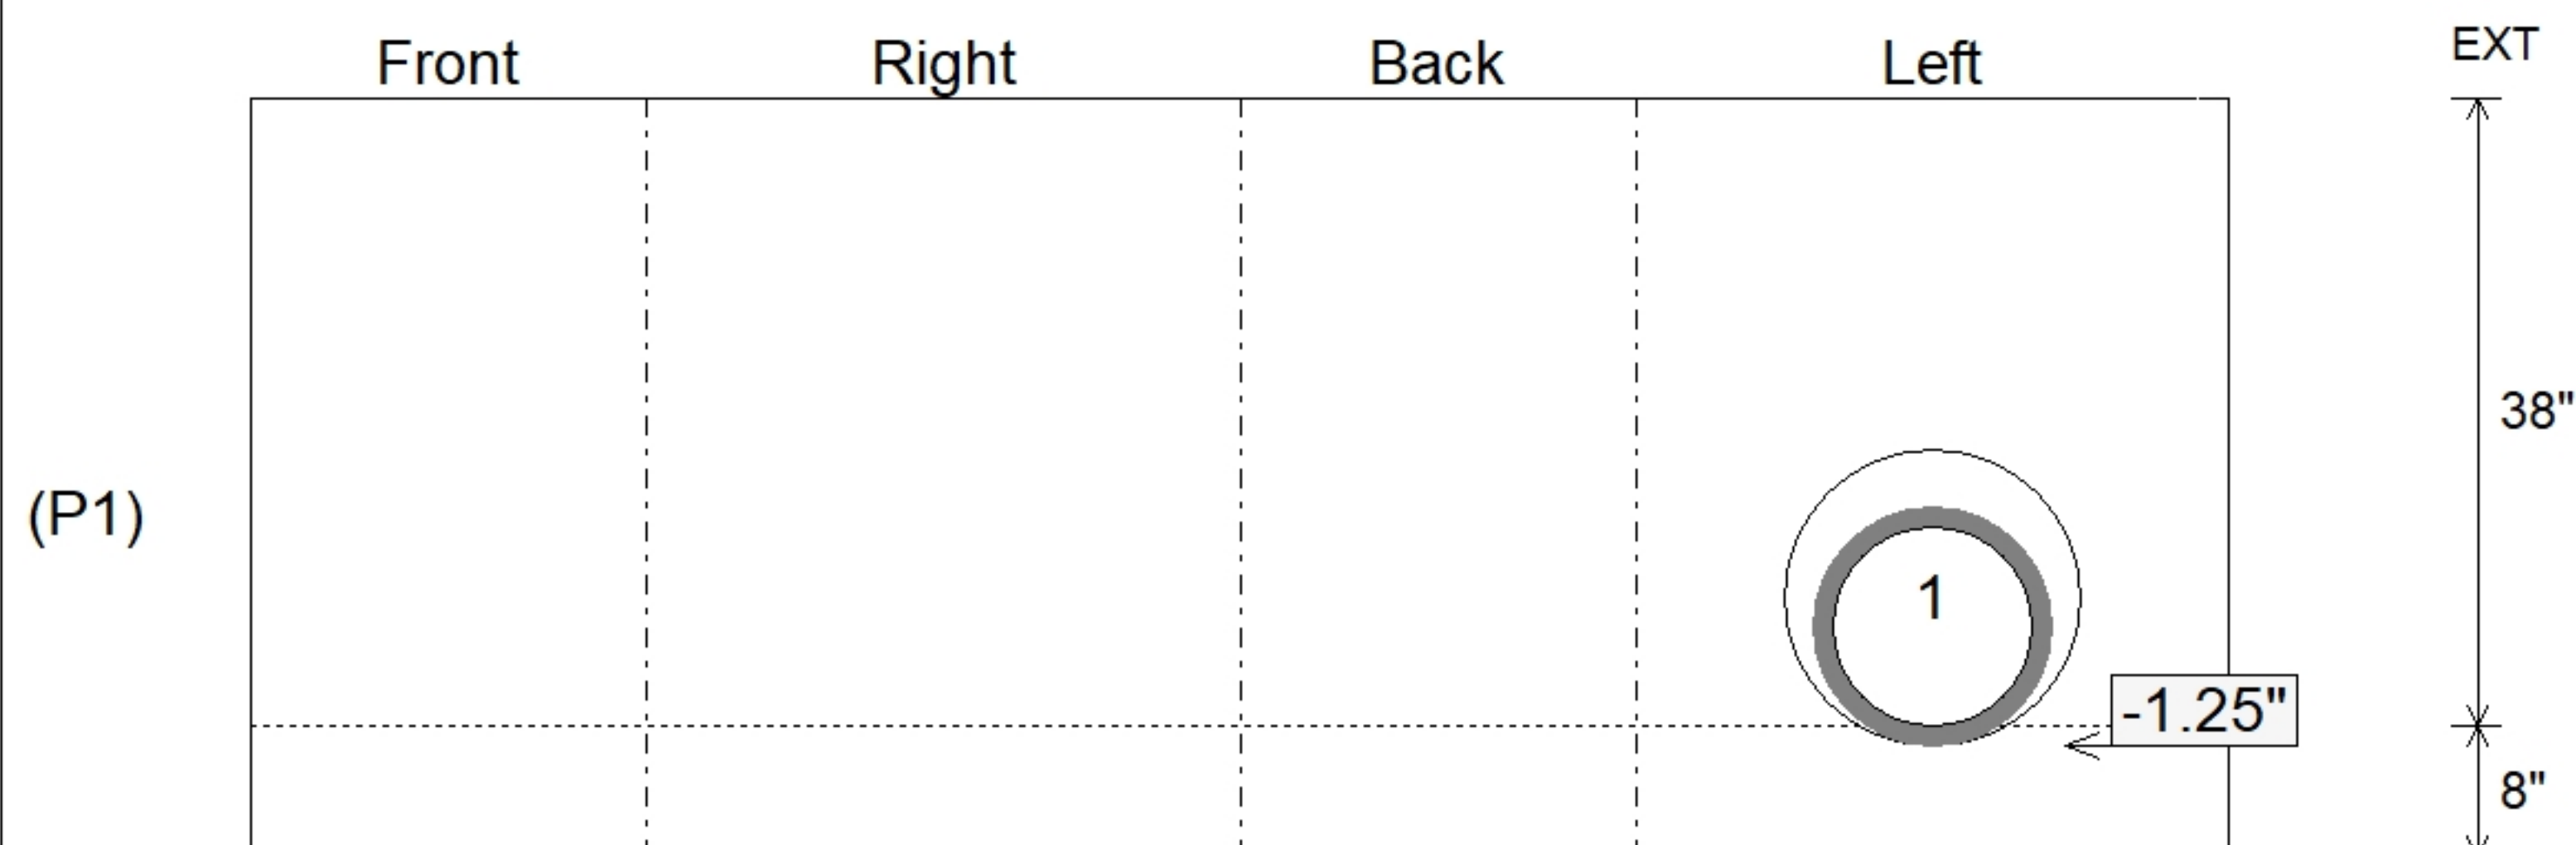

SUBMITTAL
APPROVED BY:
