




Job Name: 25-4490P2 Heartland Meadows Subdivision Job Location: Elizabethtown, KY 40165 Contractor: Kauffeld Brothers Construction					Plant: 100 7/30/2026 10:23:01 AM		Tech: Jared - A PC: Celina Goff			
Structure ID: CB 2-29 (82)										
P1 BX2436-08BA36 BOX BASE 8inW, 8inF										
P2) 24" x 36" - CASTING HEIGHT - 6" P1) 24" x 36" - BOX BASE 8inW, 8inF - 36" 1) CASTING - HOE 470 SET LV (F/G/H) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 18					0 lb 4899 lb 394 lb 0 lb 0 lb ----- 5293 lb		Structure Notes: 1. HOE 470 FLAT SET PROVIDED BY ICAST. 2. PER ASTM C913 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.			
Rim: 866.5'					Rim to Invert: 3.55'		Slack: 0.6"		Sump: 0" Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	862.95'	270°	26"	12" HDPE	14.5"	Hole 18	18"	18"	-1.25"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										



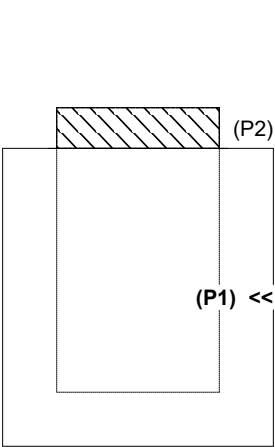



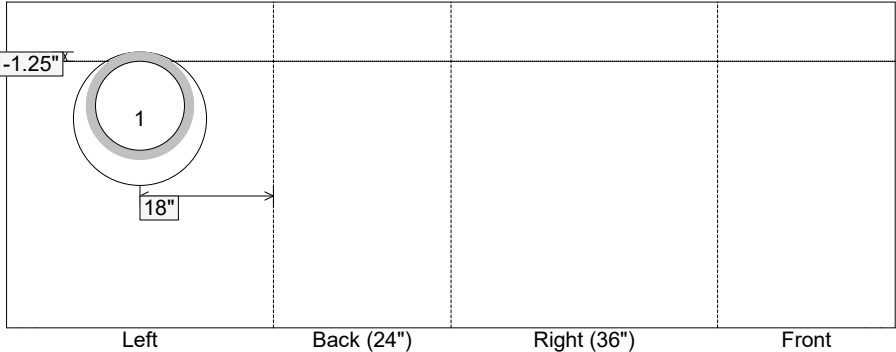

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 36" Height (Ext): 44"	Weight (Net): 4899 lb Volume (Net): 1.25cu.yd
----------------------------------	-------------------------------	--	--	--
