




Job Name: 25-4490P2 Heartland Meadows Subdivision Job Location: Elizabethtown, KY 40165 Contractor: Kauffeld Brothers Construction					Plant: 100 7/30/2026 10:20:25 AM		Tech: Jared - A PC: Celina Goff				
Structure ID: CB 3-39 (43)											
P2		MH048RS60S									
MH RISER SPECIAL											
P4) 24" x 30" - CASTING HEIGHT - 6" P3) 48" - MH FLAT TOP w/24"x30" Hole - 12" P2) 48" - MH RISER SPECIAL - 60" P1) 48" - MH BASE Custom Ht - 39" 1) CASTING - HOE 360 L Vane Set (F/G/H) 2) 48" - Conseal CS-102 1.00" 1) 24" x 30" - Conseal CS-102 1.00" 2) Hole - 30						0 lb 1935 lb 3875 lb 3739 lb 362 lb 0 lb 0 lb 0 lb ----- Structure Total: 9912 lb		Structure Notes: . 1. HOE 360 FLAT SET PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 874.9' Rim to Invert: 9.67' Slack: 0.94" Sump: 1.9" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2	869.34'	180°	91.106"	24" HDPE	27.8"	Hole 30	30"	32.406"	6.07"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

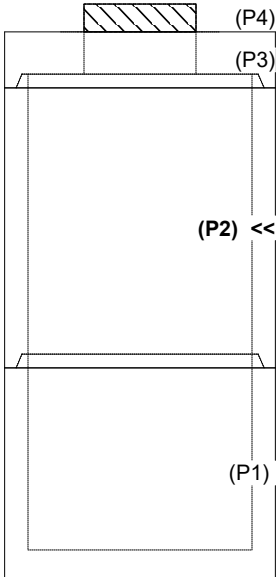

RIGHT-SIDE UP VIEW (int. dimensions)

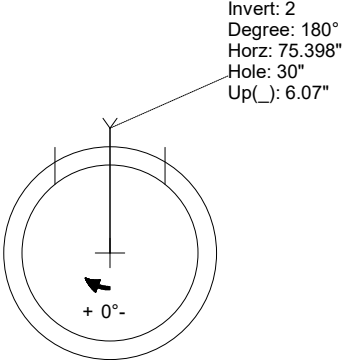

INSIDE WALL DIMENSIONS

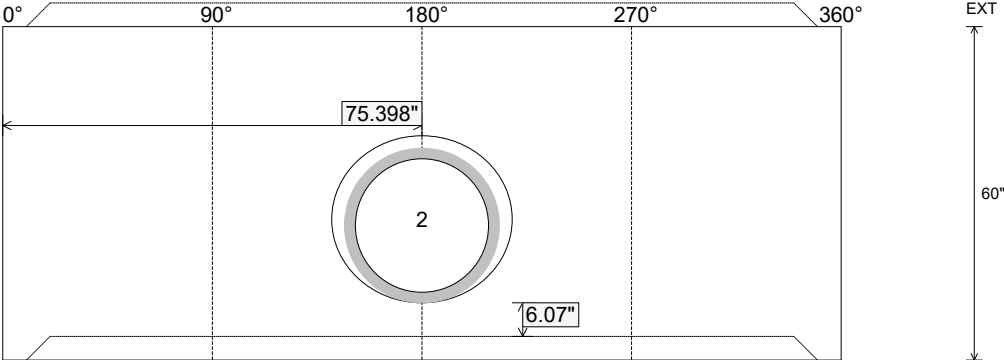

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 60" Height (Ext): 60"	Weight (Net): 3875 lb Volume (Net): 0.99cu.yd
----------------------------------	------------------------------------	--	--	--
