

Job Name: 25-4490P2 Heartland Meadows Subdivision
Job Location: Elizabethtown, KY 40165
Contractor: Kauffeld Brothers Construction

Plant: 100

7/31/2026 9:24:42 AM

Tech: Jared - A

PC: Celina Goff



Structure ID: CB 4-44 (57)



P2 MH048LD12-24X36RECT

MH FLAT TOP w/24"x36" Hole

- P4) 24" x 36" - CASTING HEIGHT - 6"
P3) 24" x 36" - GRADE RING - 3"
P2) 48" - MH FLAT TOP w/24"x36" Hole - 12"
P1) 48" - MH BASE - 60"
1) CASTING - HOE 470 SET LV (F/G/H)
1) 48" - Conseal CS-102 1.00"
2) 24" x 36" - Conseal CS-102 1.00"
3) Hole - 18

- 0 lb
306 lb
1300 lb
5195 lb
394 lb
0 lb
0 lb
0 lb

Structure Total: 7195 lb
- Structure Notes:
1. HOE 470 FLAT SET PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

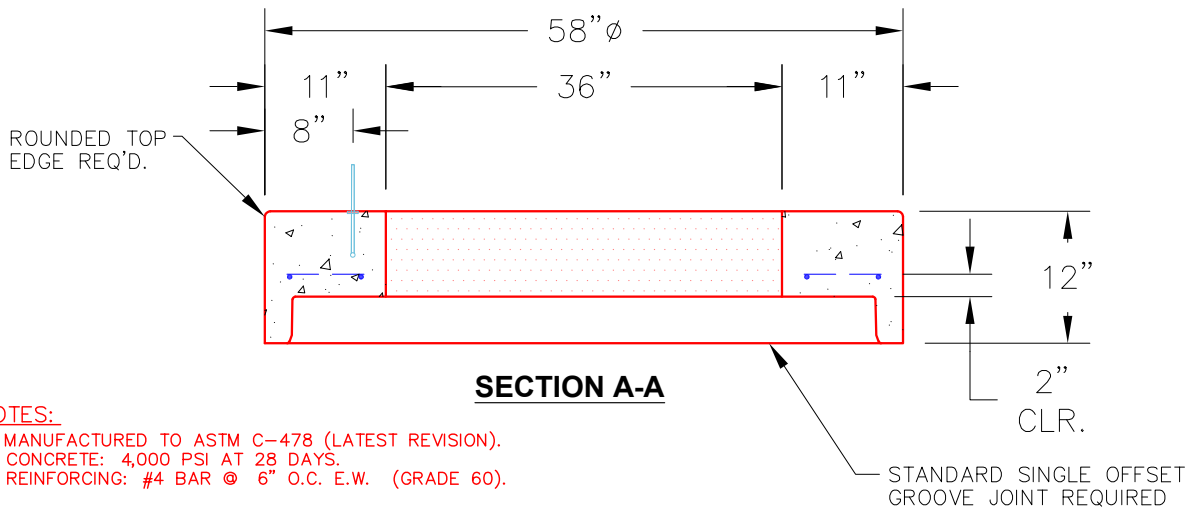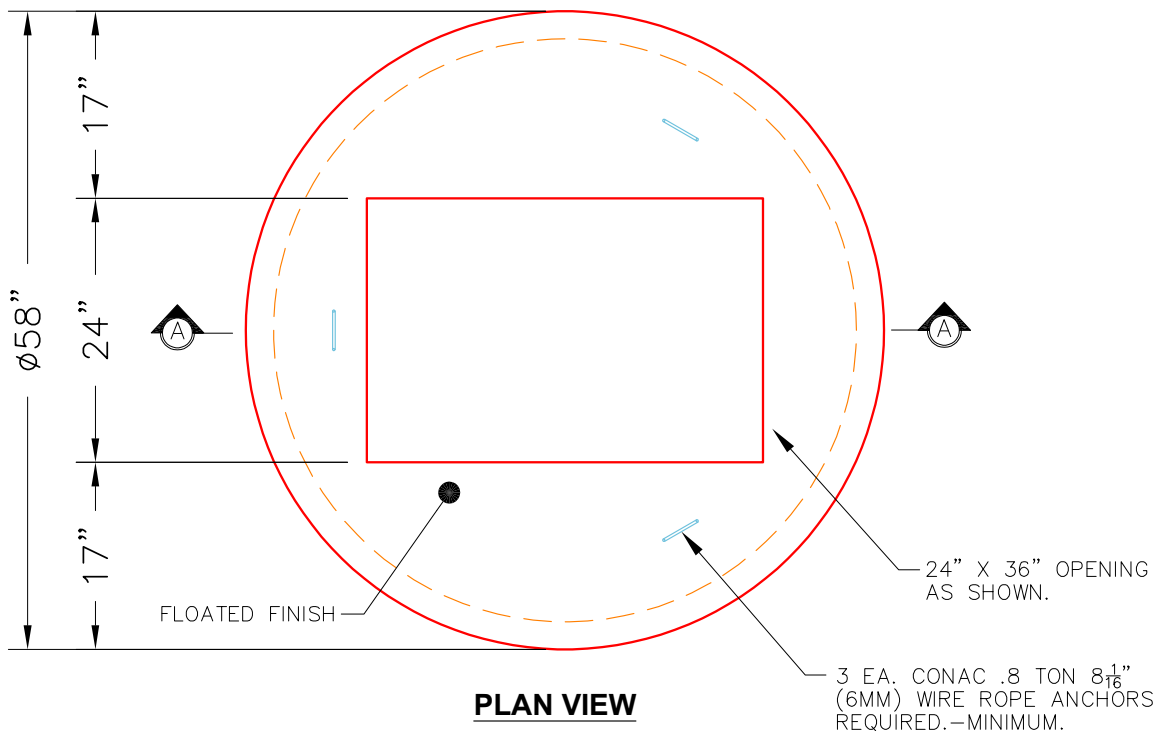

- NOTES:
1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #4 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1300 lb
Volume (Net): 0.46cu.yd
