

Job Name: 25-4490P2 Heartland Meadows Subdivision
Job Location: Elizabethtown, KY 40165
Contractor: Kauffeld Brothers Construction

Plant: 100

7/31/2026 9:24:42 AM

Tech: Jared - A

PC: Celina Goff



Structure ID: CB 4-44 (57)

P3 GR24x36x8x3

GRADE RING

- P4) 24" x 36" - CASTING HEIGHT - 6"
P3) 24" x 36" - GRADE RING - 3"
P2) 48" - MH FLAT TOP w/24"x36" Hole - 12"
P1) 48" - MH BASE - 60"
1) CASTING - HOE 470 SET LV (F/G/H)
1) 48" - Conseal CS-102 1.00"
2) 24" x 36" - Conseal CS-102 1.00"
3) Hole - 18


- 0 lb
306 lb
1300 lb
5195 lb
394 lb
0 lb
0 lb
0 lb

7195 lb
- Structure Notes:**
1. HOE 470 FLAT SET PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


Structure Total:

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. REINFORCING: #4 BAR AS SHOWN (GRADE 60 KSI).
4. LIFTS: 2 EA. CONAC .8 TON WIRE ROPE ANCHORS REQUIRED.

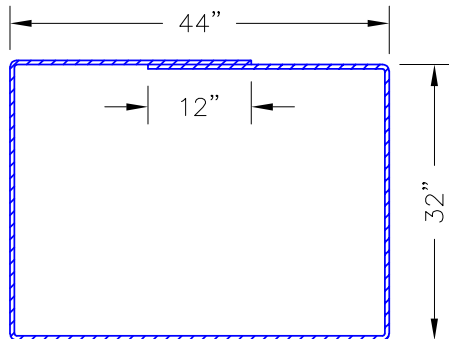


#4 BAR REINFORCING

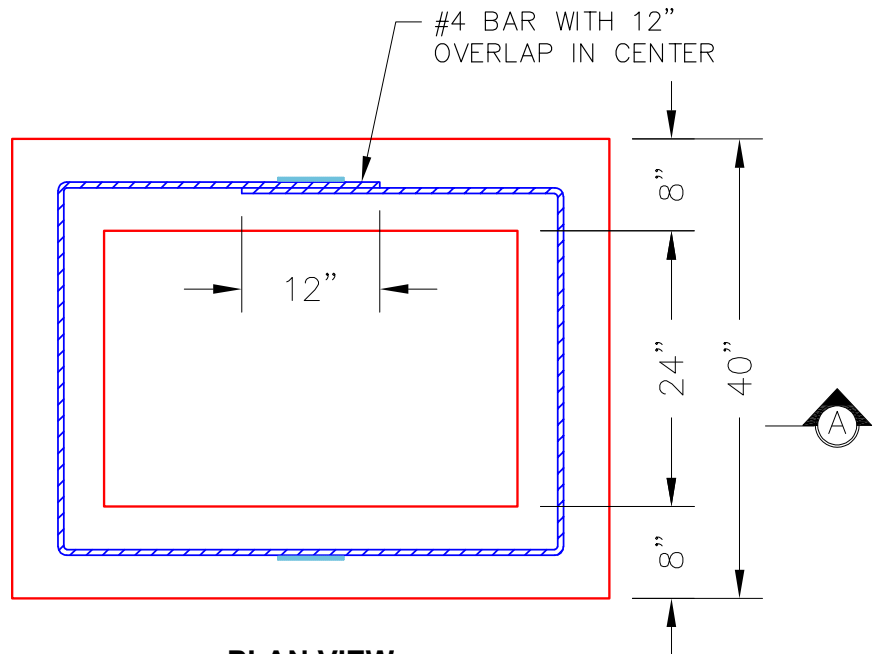

PLAN VIEW

2 EA. CONAC .8 TON $8\frac{1}{16}$ "
(6MM) WIRE ROPE ANCHORS
REQUIRED—MINIMUM.

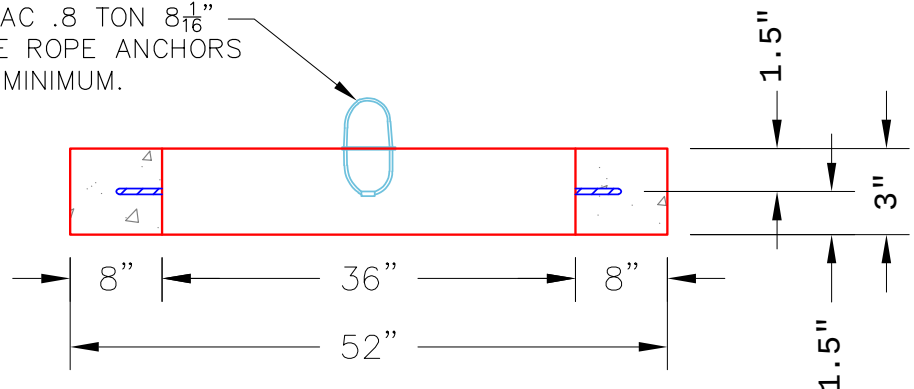

SECTION A-A

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 3"

Weight (Net): 306 lb
Volume (Net): 0.08cu.yd
