

Contractor: Kauffeld Brothers Construction

TECH: Jared - A

Plant: 100



Size: 24" x 30"

Rim to Invert: 4.98'

Floor Height: 8"


Slack: 0.76"

6. PLEASE VERIFY THE CURB LINE LOCATION AND THE ORIENTATION OF THE BOX.


2) Hole - 30

0 lb


Structure Total: 5866 lb

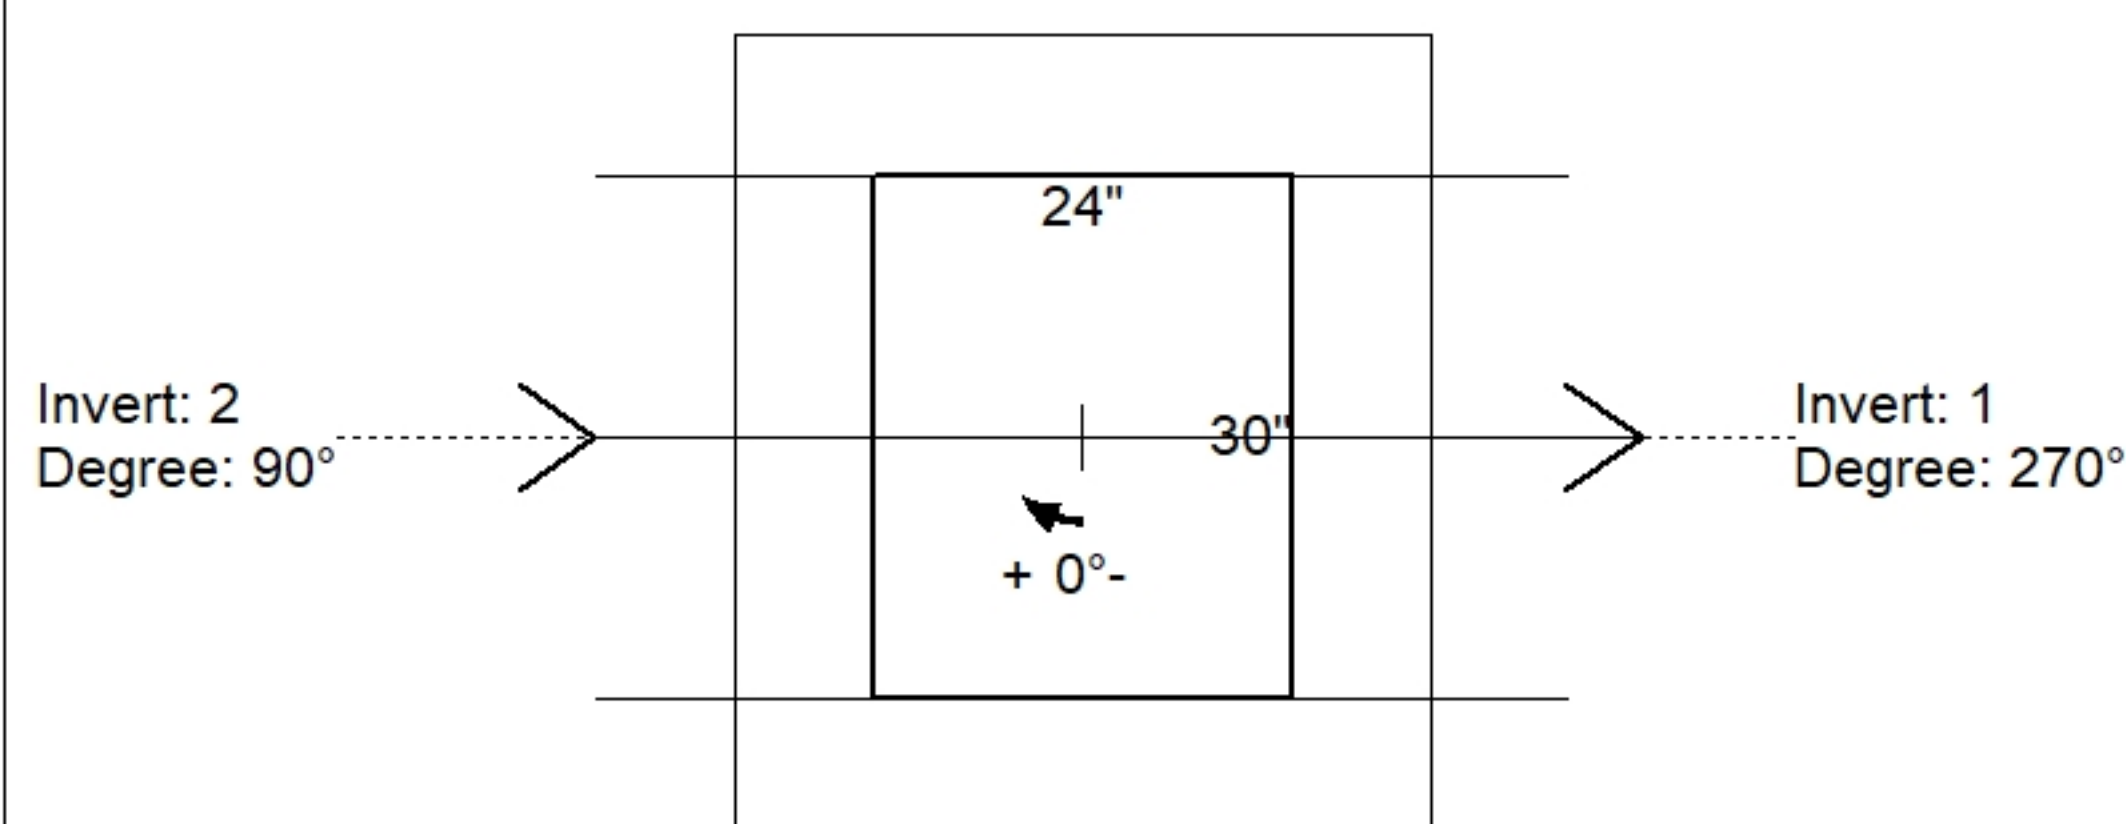

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	863.96'							
Reducer								
Invert 1	858.98'	270°	24" HDPE	27.8"	30"	Hole 30	-1.9"	P1
Invert 2	858.98'	90°	24" HDPE	27.8"	30"	Hole 30	-1.9"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

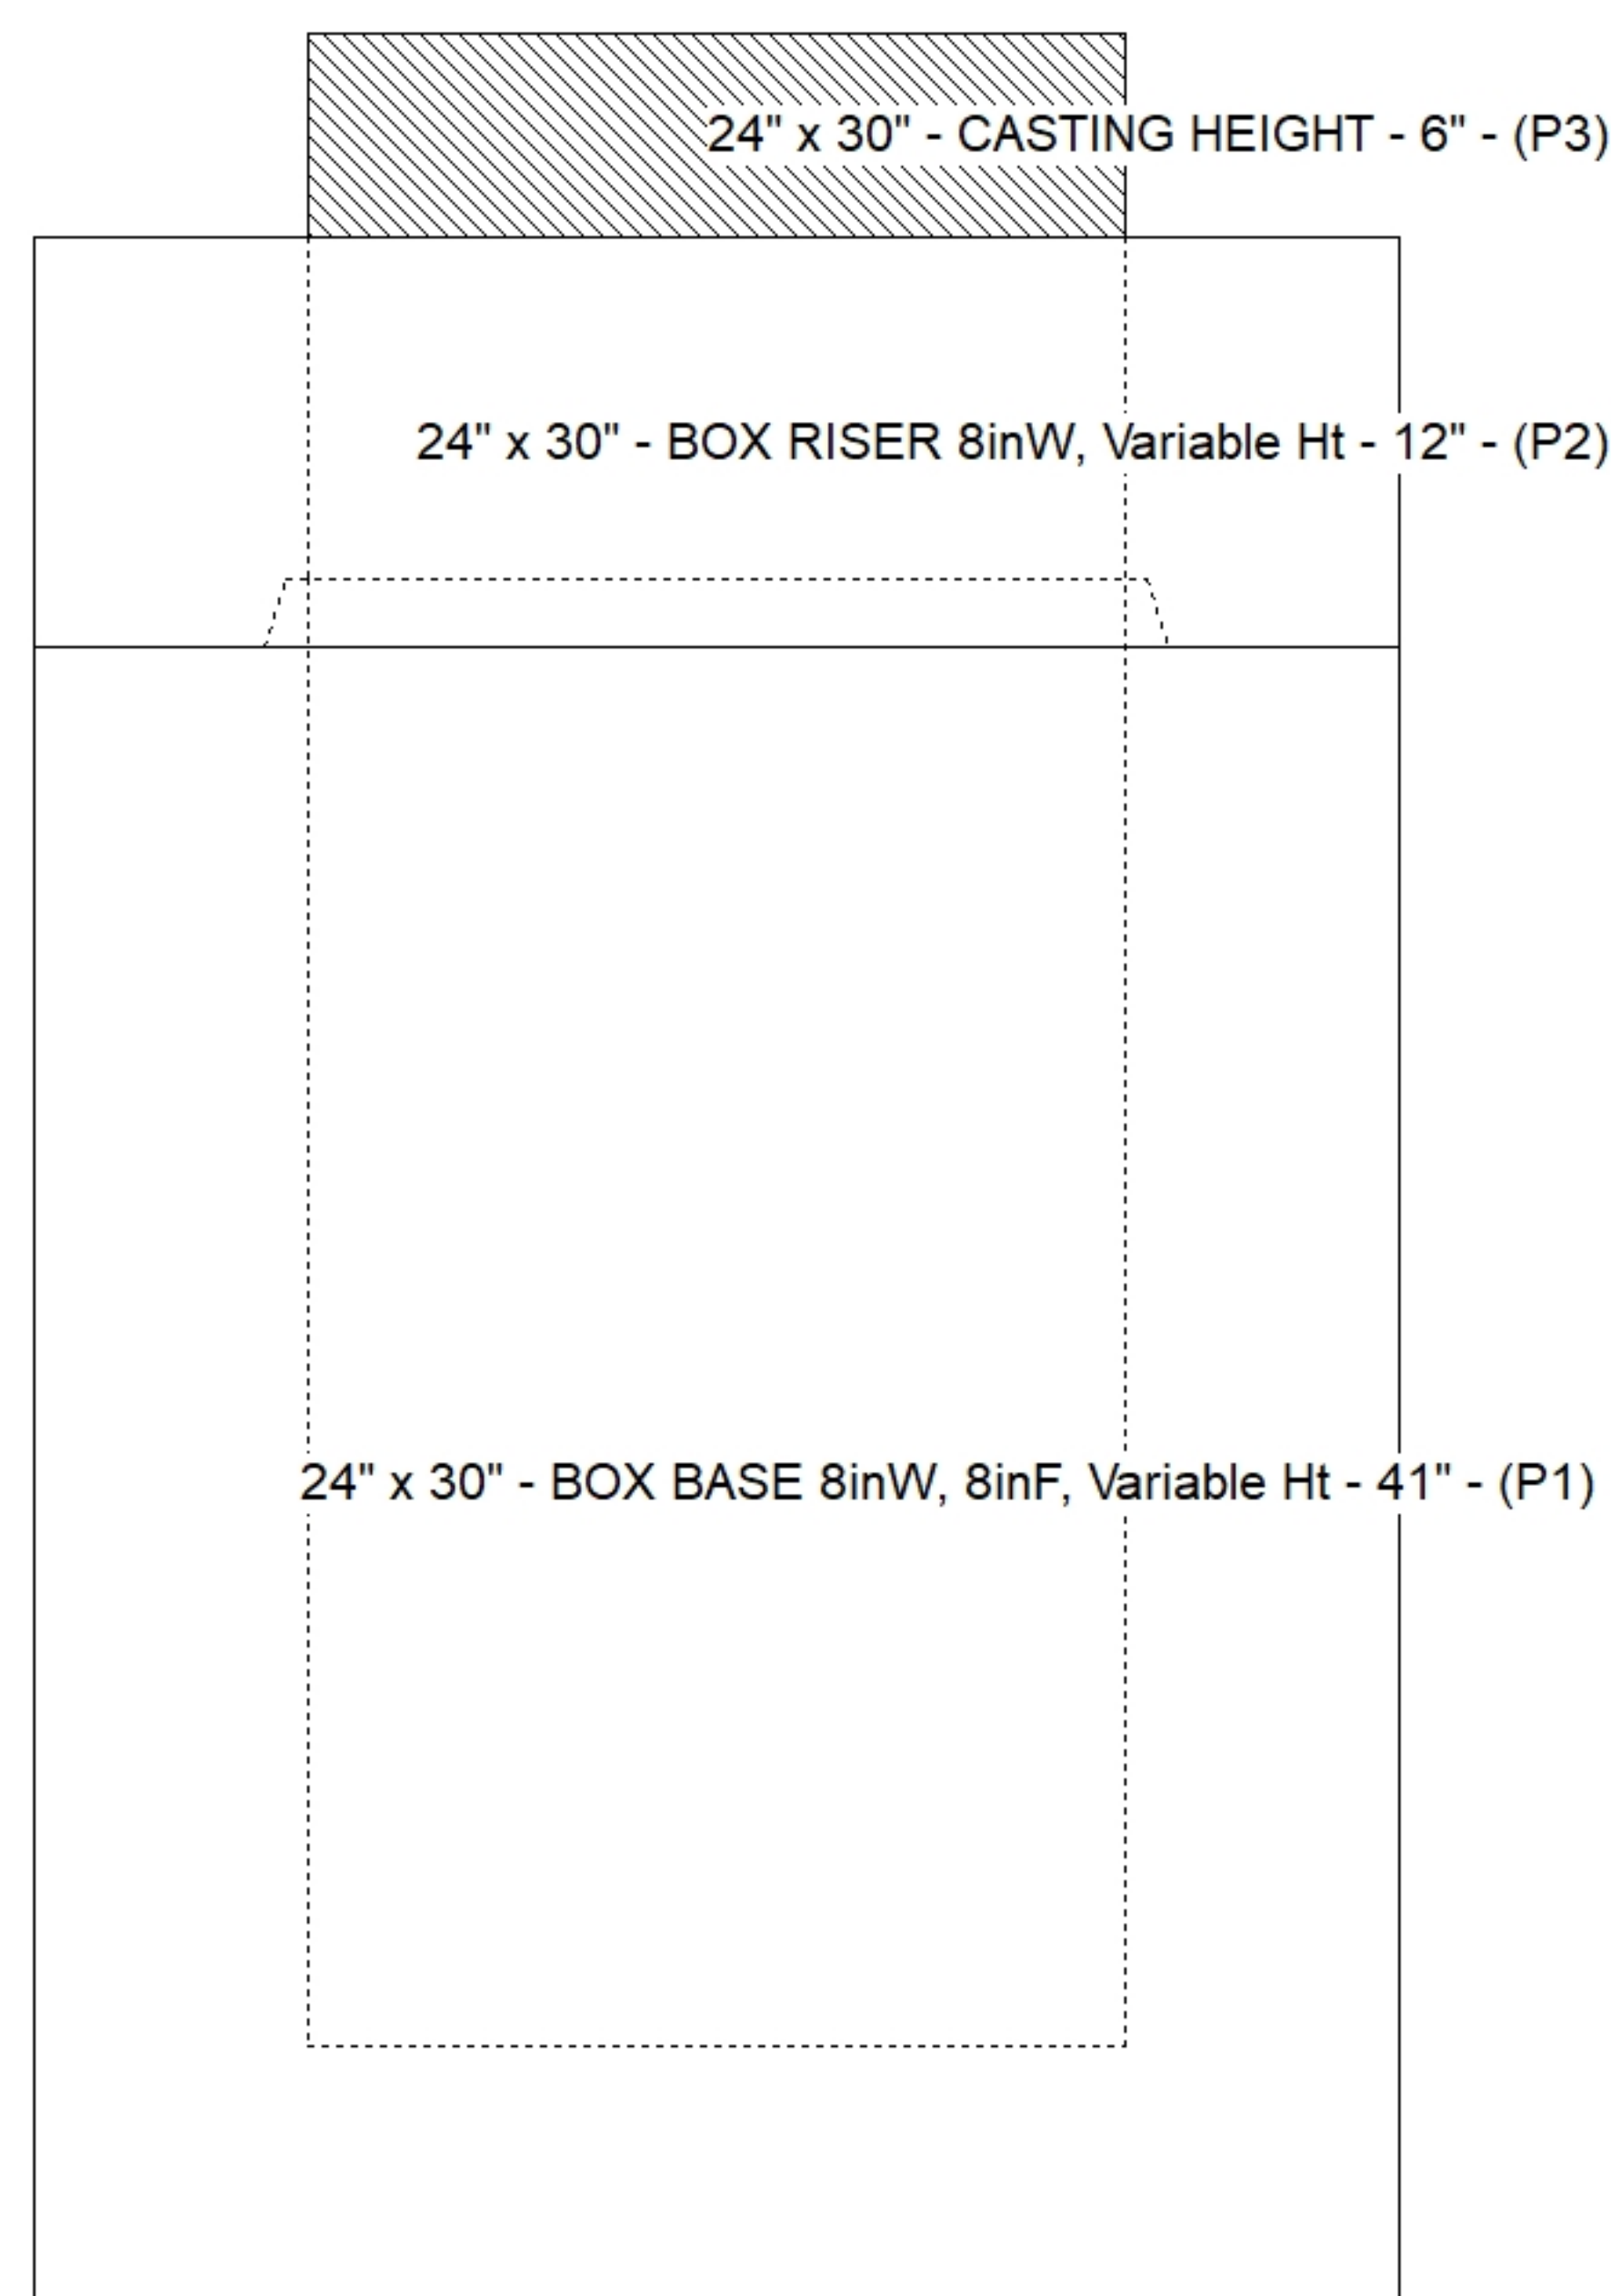

Default - Interior Dimensions

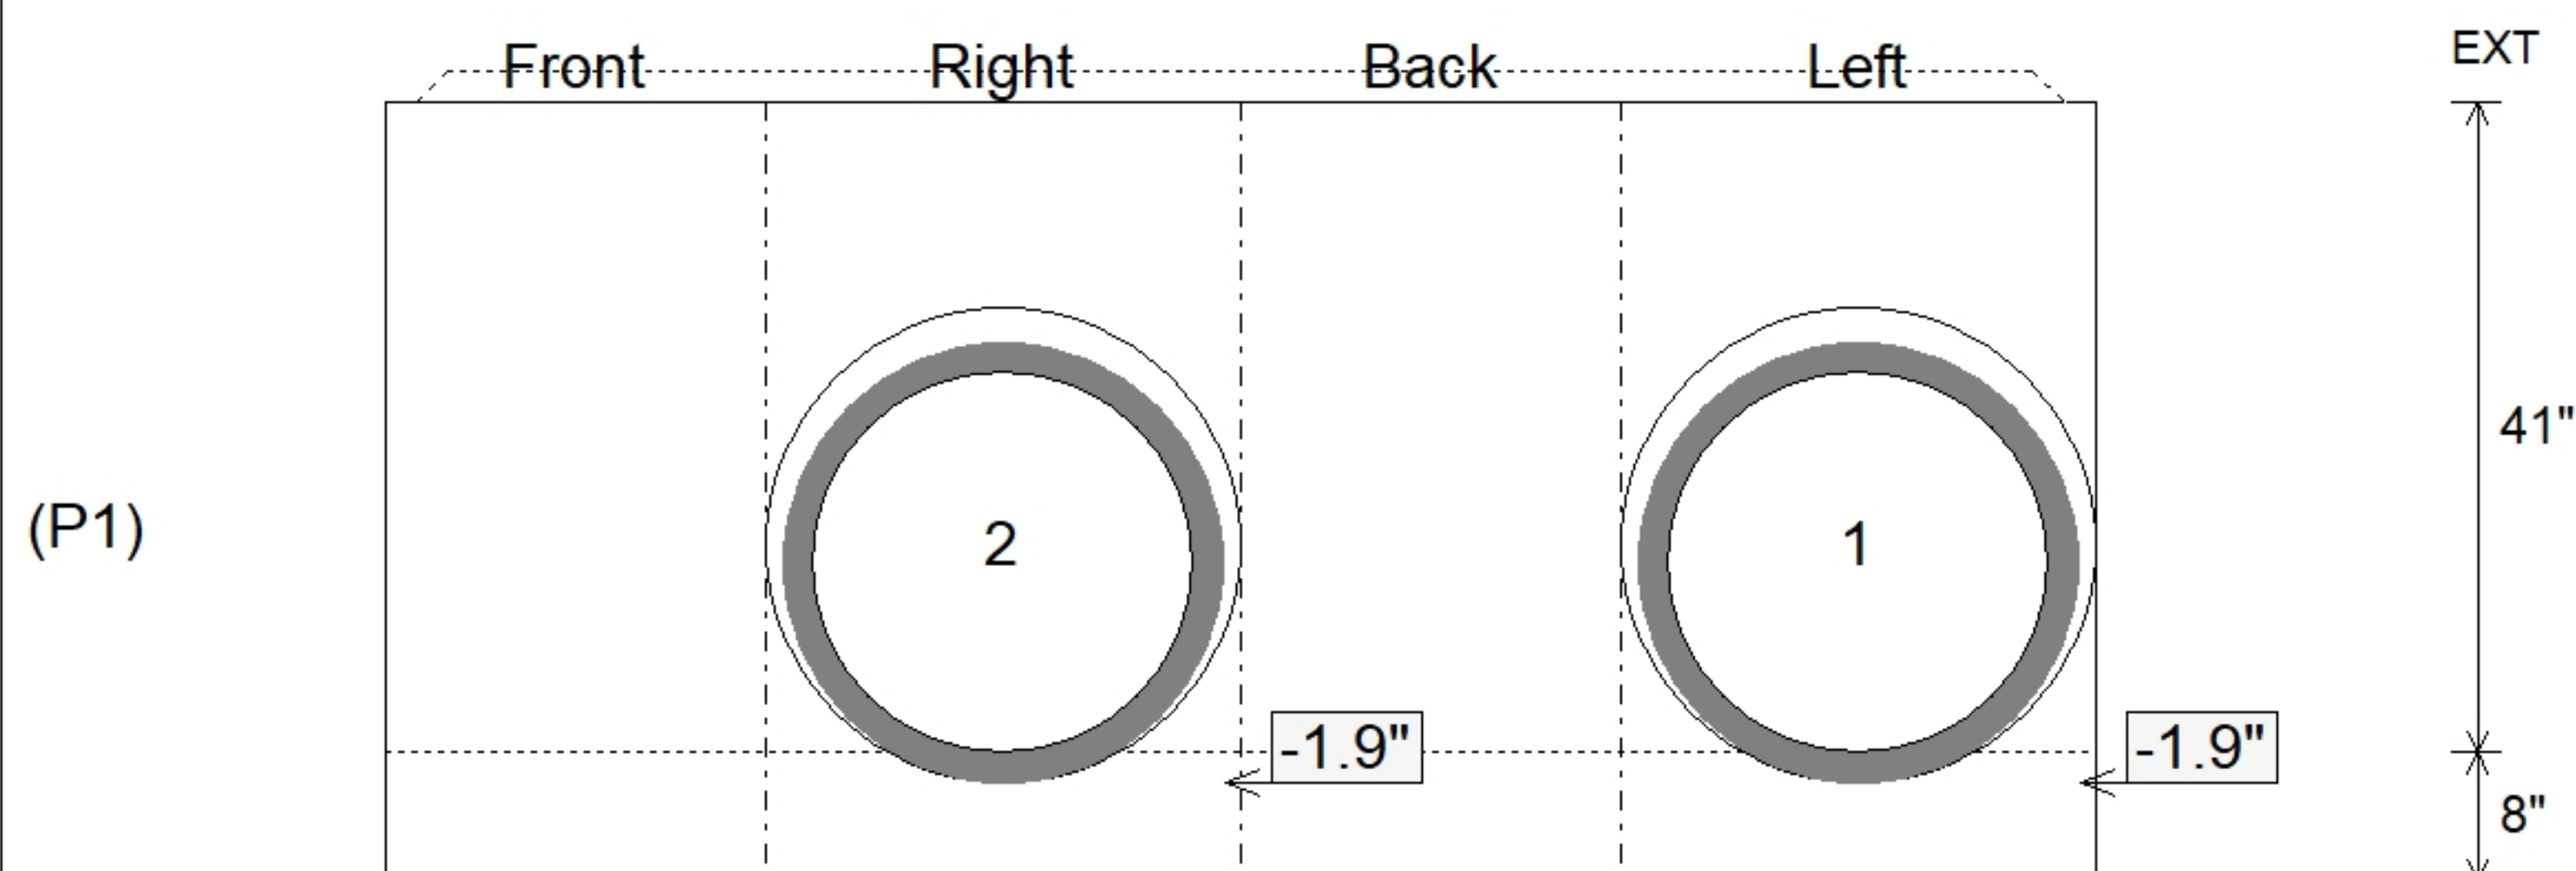

Submittal Drawing
8/3/2026 9:27:50 AM

SUBMITTAL
APPROVED BY:
