


Contractor: Kauffeld Brothers Construction

Plant: 100



Slack: 0.16"

Structure Total:	4874 lb
------------------	---------

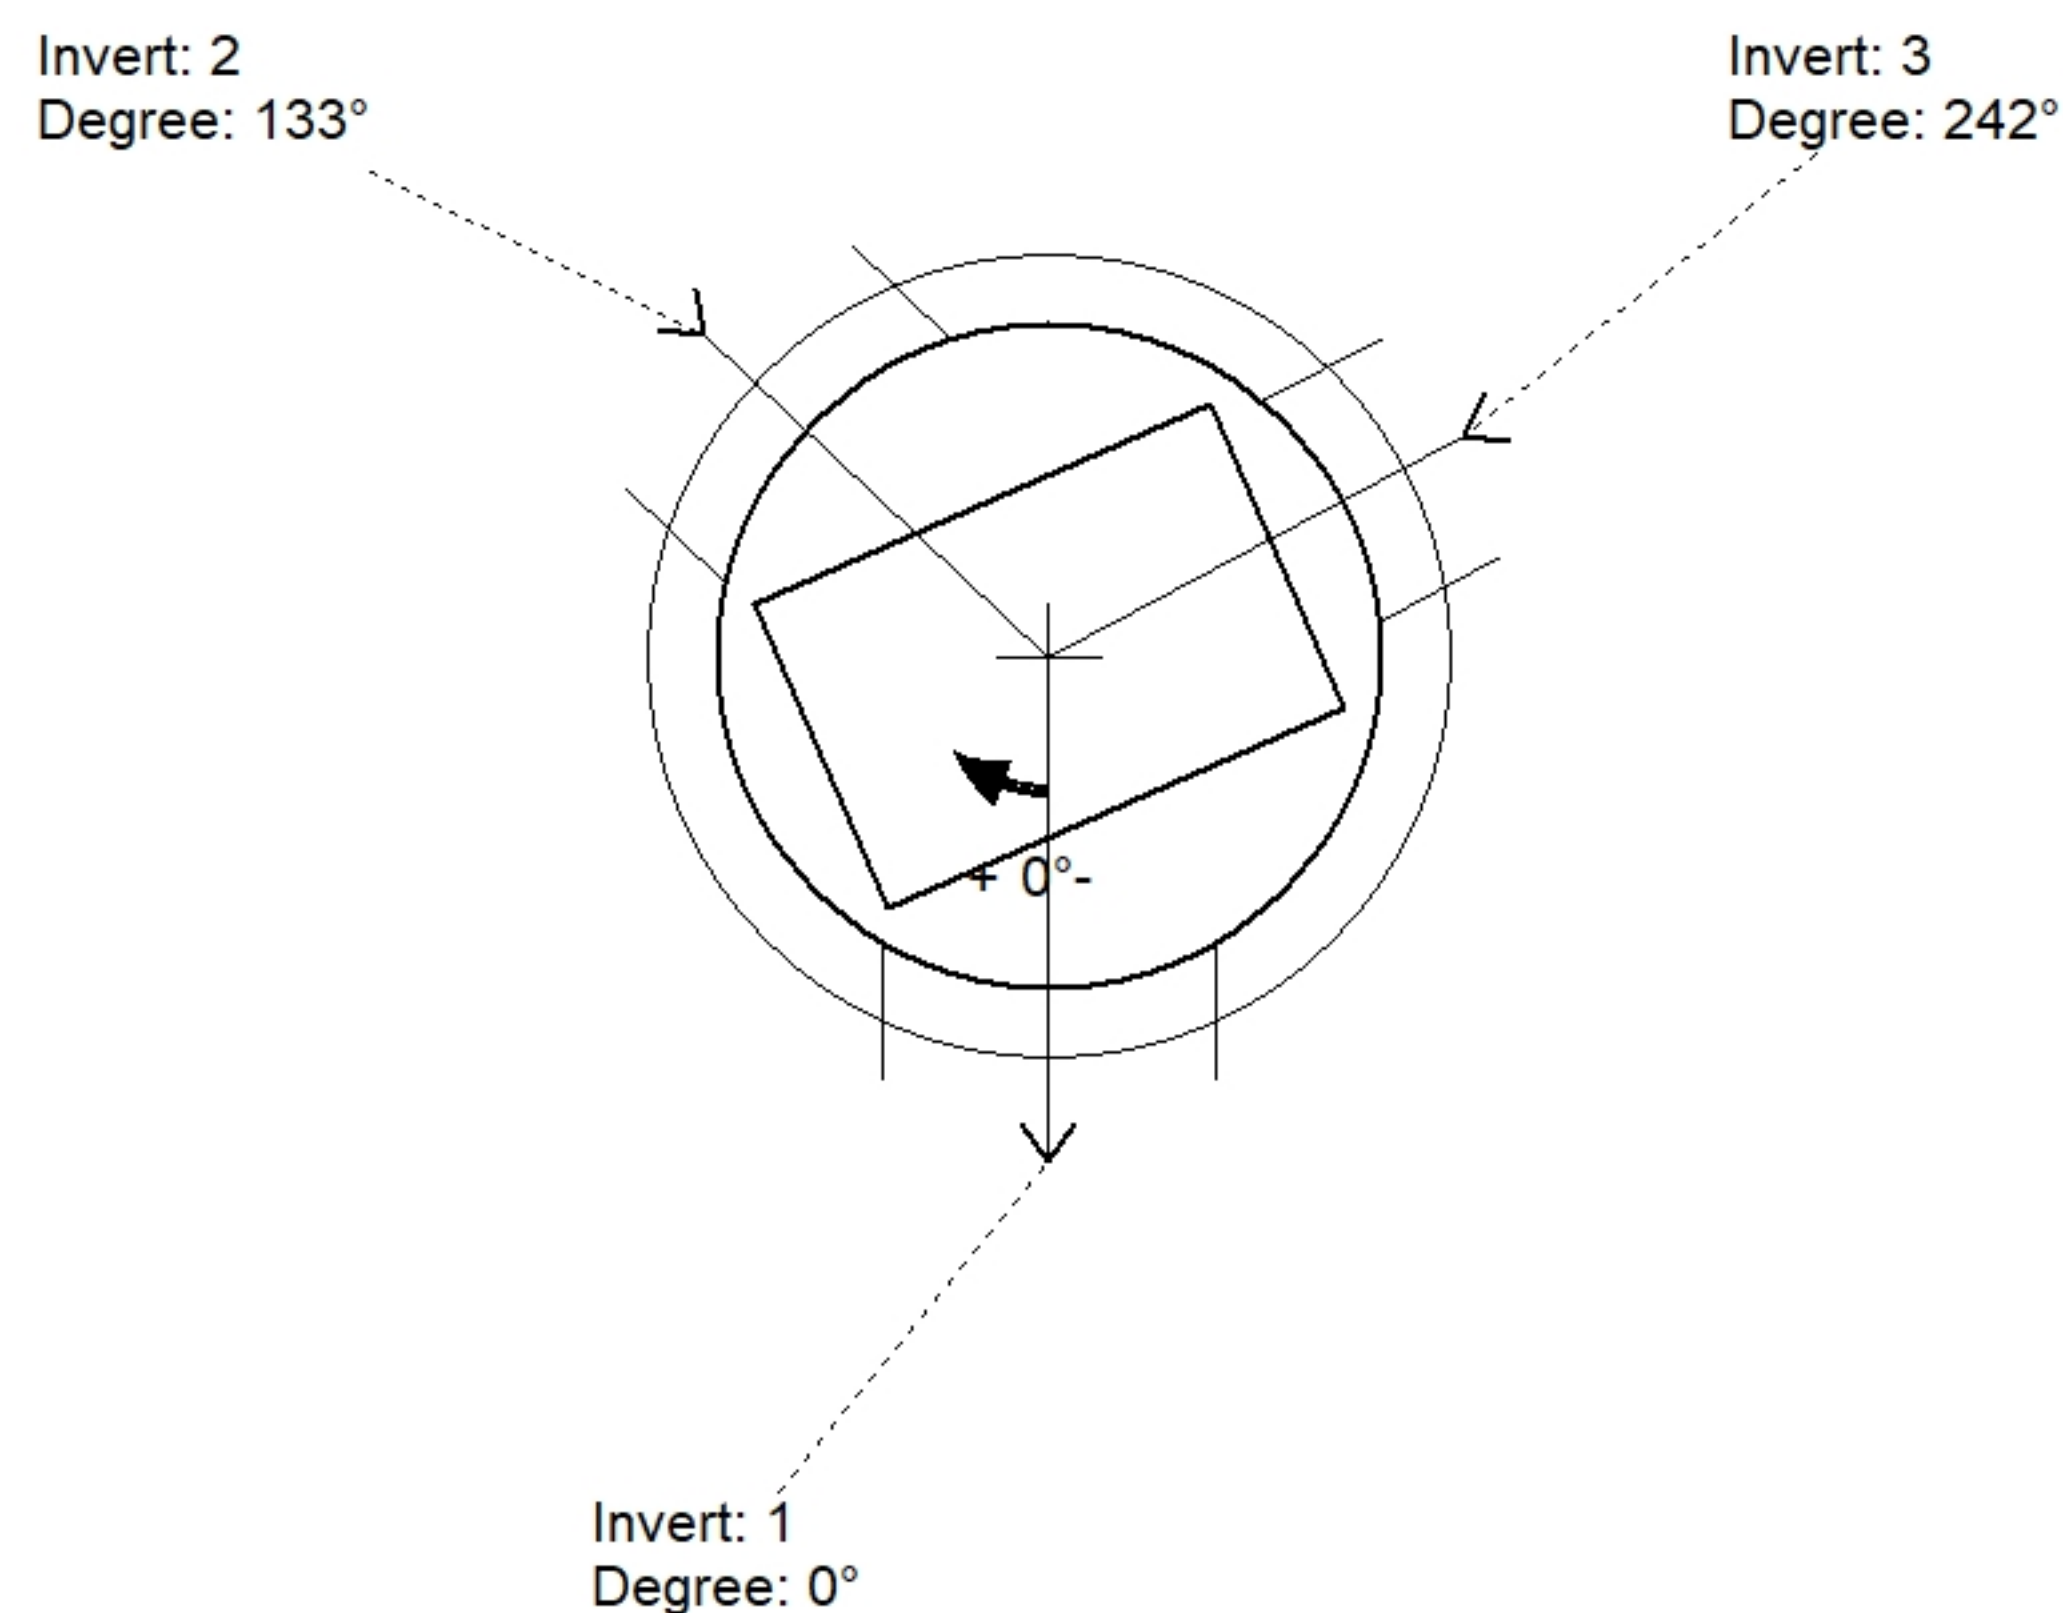


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	873.75'							
Reducer								
Invert 1	869.62'	0°	18" HDPE	21.2"	24"	Hole 24	0"	P1
Invert 2	869.63'	133°	18" HDPE	21.2"	24"	Hole 24	0.12"	P1
Invert 3	869.62'	242°	12" HDPE	14.5"	18"	Hole 18	0.35"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 36" - CASTING HEIGHT - 6" - (P3)

48" - MH FLAT TOP w/24"x36" Hole - 12" - (P2)

48" - MH BASE Custom Ht - 33" - (P1)

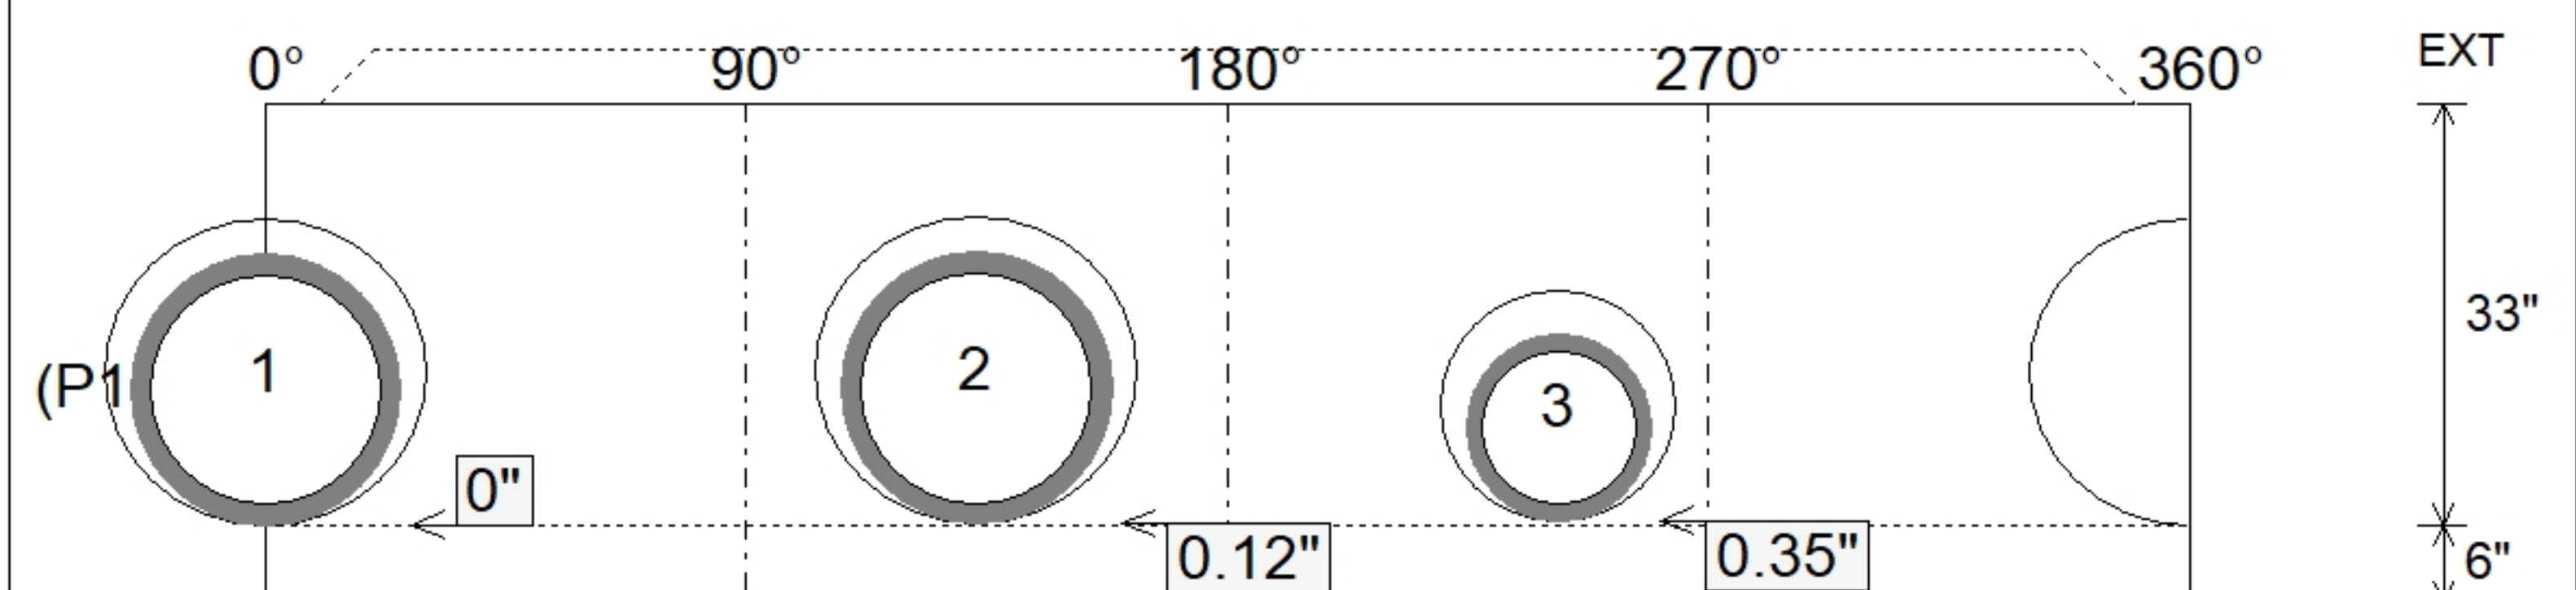

SUBMITTAL
APPROVED BY:
