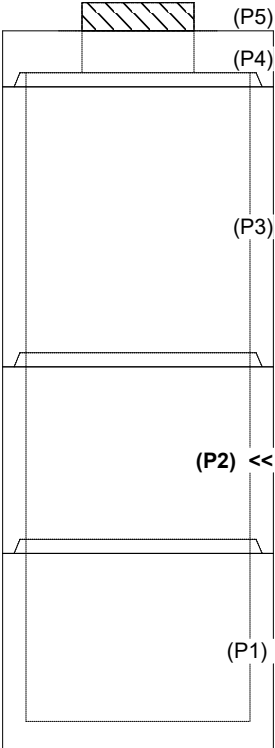
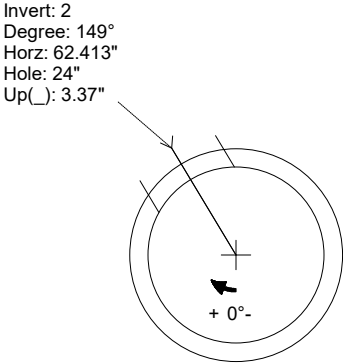
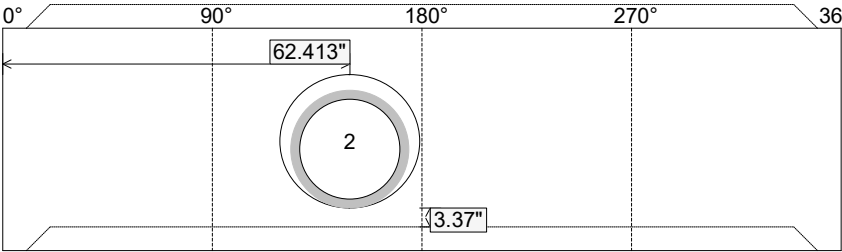



Job Name: 25-4490P2 Heartland Meadows Subdivision					Plant: 100		Tech: Jared - A					
Job Location: Elizabethtown, KY 40165					7/30/2026 10:20:23 AM		PC: Celina Goff					
Contractor: Kauffeld Brothers Construction												
Structure ID: CI 2-26 (35)												
P2		MH048RSVF		MH RISER Custom Ht								
P5) 24" x 30" - CASTING HEIGHT - 6" P4) 48" - MH FLAT TOP w/24"x30" Hole - 12" P3) 48" - MH RISER SPECIAL - 60" P2) 48" - MH RISER Custom Ht - 40" P1) 48" - MH BASE - 36" 1) CASTING - HOE 360 L Vane Set (F/G/H) 3) 48" - Conseal CS-102 1.00" 1) 24" x 30" - Conseal CS-102 1.00" 1) Hole - 30 1) Hole - 24					0 lb 1935 lb 4192 lb 2645 lb 3319 lb 362 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 12452 lb		Structure Notes: 1. HOE 360 FLAT SET PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 872.98'					Rim to Invert: 12.72'		Slack: 0.54"		Sump: 1.9"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1												
Invert 2	863.87'	149°	75.416"	18" HDPE	21.2"	Hole 24	24"	25.133"	3.37"	0"		
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												
RIGHT-SIDE UP VIEW (int. dimensions)												
												
INSIDE WALL DIMENSIONS												
												
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 40" Height (Ext): 40"		Weight (Net): 2645 lb Volume (Net): 0.68cu.yd			
