


Job Name: 25-4490P2 Heartland Meadows Subdivision Job Location: Elizabethtown, KY 40165 Contractor: Kauffeld Brothers Construction					Plant: 100 7/30/2026 10:22:35 AM		Tech: Jared - A PC: Celina Goff			
Structure ID: MH 2-67 (28)										
P1 MH048BA54		MH BASE								
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE - 42" P1) 48" - MH BASE - 54" 1) CASTING - HOE MC-375 F/C Storm 1) 48" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 20 8) MH Step ML-10-TDS-NCR - 10"					0 lb 3200 lb 4832 lb 271 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 8303 lb		Structure Notes: . 1. HOE MC-375 F/C "STORM" PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 903.04'		Rim to Invert: 8.52'		Slack: 0.54"		Sump: 1.3"		Step Position: 233°		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	894.52'	0°	0"	15" HDPE	17.6"	Hole 20	20"	20.629"	0"	0"
Invert 2	894.52'	106°	53.651"	15" HDPE	17.6"	Hole 20	20"	20.629"	0"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

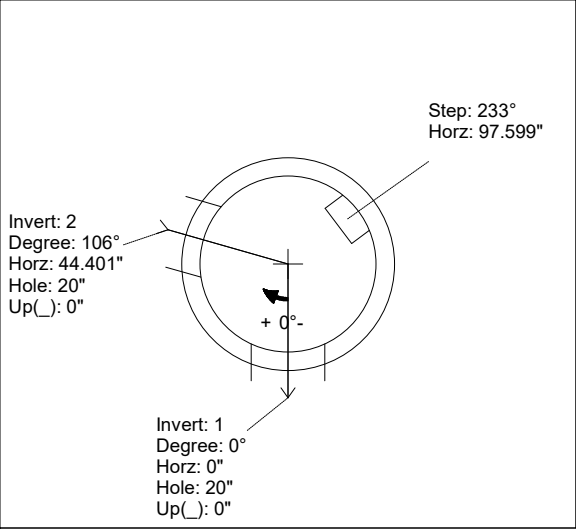


Invert: 2
Degree: 106°
Horz: 44.401"
Hole: 20"
Up(): 0"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 20"
Up(): 0"

Step: 233°
Horz: 97.599"

UPSIDE-DOWN VIEW (int. dimenions)

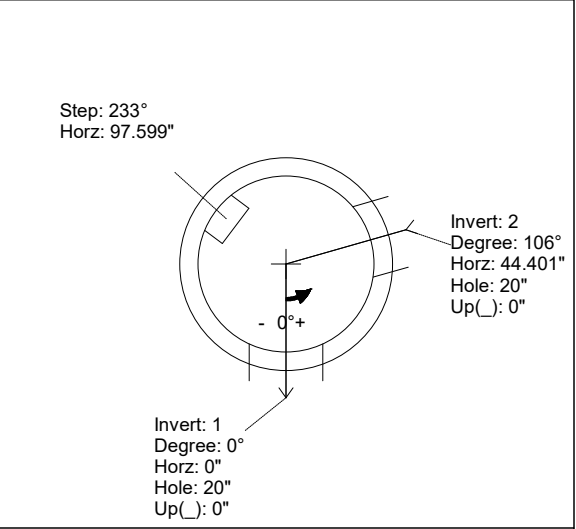


Invert: 2
Degree: 106°
Horz: 44.401"
Hole: 20"
Up(): 0"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 20"
Up(): 0"

Step: 233°
Horz: 97.599"

INSIDE WALL DIMENSIONS

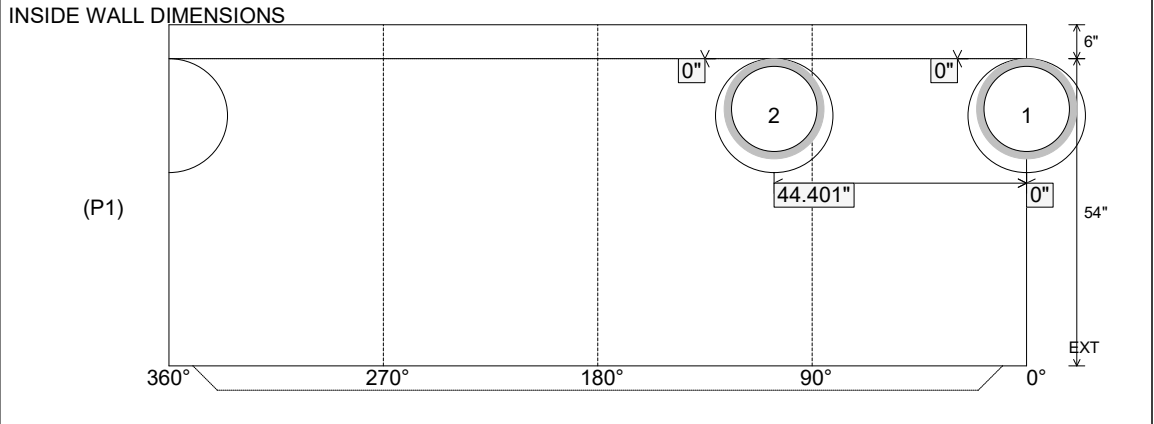

360° 270° 180° 90° 0°

EXT

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: n/a

Wall Thickness: 5"
Floor Height: 6"

Height (Int): 54"
Height (Ext): 60"

Weight (Net): 4832 lb
Volume (Net): 1.23cu.yd
