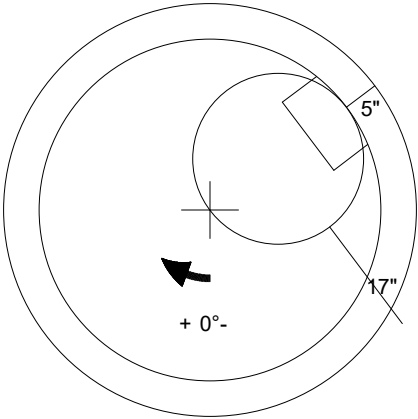



Job Name: 25-4490P2 Heartland Meadows Subdivision		Plant: 100	Tech: Jared - A	
Job Location: Elizabethtown, KY 40165		7/30/2026 10:24:42 AM	PC: Celina Goff	
Contractor: Kauffeld Brothers Construction				
Structure ID: MH 2-67 (28)				
P2 MH048CN42		ECC CONE w/ 24" HOLE		
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE - 42" P1) 48" - MH BASE - 54" 1) CASTING - HOE MC-375 F/C Storm 1) 48" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 20 8) MH Step ML-10-TDS-NCR - 10"		0 lb 3200 lb 4832 lb 271 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 8303 lb	Structure Notes: . 1. HOE MC-375 F/C "STORM" PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
 48" - ECC CONE w/ 24" HOLE - 42" - (P2)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 42"	Weight (Net): 3200 lb Volume (Net): 0.5cu.yd
