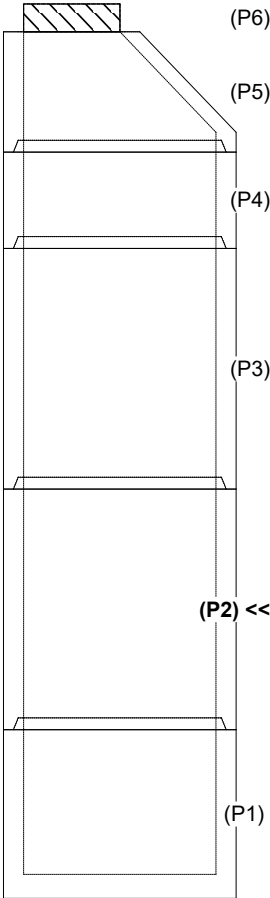
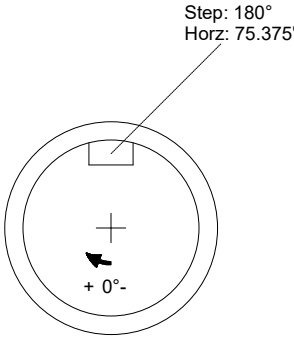
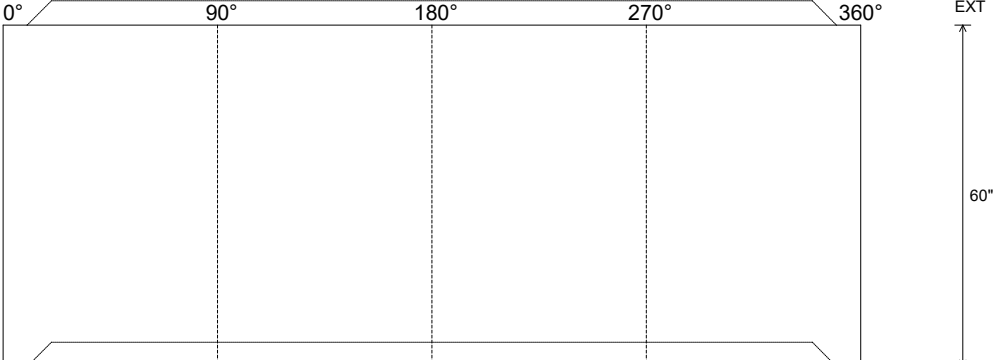


Job Name: 25-4547 - WWTP Improvements & Hydraulic Expansion Job Location: Shepherdsville, KY Contractor: Pace Contracting, LLC					Plant: 100 5/29/2026 3:22:43 PM		Tech: Jared - F PC: J Jarvis					
Structure ID: MH-39-052												
P2		MH048RS60		MH RISER T/G								
P6) 24" - CASTING HEIGHT - 7" P5) 48" - ECC CONE w/ 24" HOLE F/G - 30" P4) 48" - MH RISER T/G - 24" P3) 48" - MH RISER T/G - 60" P2) 48" - MH RISER T/G - 60" P1) 48" - MH BASE T/n - 36" 1) Chimney Seal - Cretex Chimney Seal 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 4) 48" - Conseal CS-102 1.00" (Double) 2) Kor-N-Seal2 - S206-22 16) MH Step ML-10-TDS-NCR - 10"					0 lb 2050 lb 1677 lb 4192 lb 4192 lb 3516 lb 10 lb 0 lb 0 lb 1440 lb 271 lb 0 lb 13 lb 0 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY I-CAST (HOE MC-375 F/C SANITARY). 4. 8.5" EXTERNAL CHIMNEY SEAL BY I-CAST. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 433.28'					Rim to Invert: 18.15'		Slack: 2.8"		Sump: 2"		Step Position: 180°	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1												
Invert 2												
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												
RIGHT-SIDE UP VIEW (int. dimensions)												
												
INSIDE WALL DIMENSIONS												
												
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 60" Height (Ext): 60"		Weight (Net): 4192 lb Volume (Net): 1.07cu.yd			
