



Job Name: 25-4547 - WWTP Improvements & Hydraulic Expansion Job Location: Shepherdsville, KY Contractor: Pace Contracting, LLC				Plant: 100 5/29/2026 3:22:49 PM		Tech: Jared - F PC: J Jarvis						
Structure ID: MH-9												
P3		MH048RS48		MH RISER T/G								
P5) 24" - CASTING HEIGHT - 7" P4) 48" - ECC CONE w/ 24" HOLE F/G - 24" P3) 48" - MH RISER T/G - 48" P2) 48" - MH RISER T/G - 60" P1) 48" - MH BASE T/h - 24" 1) Chimney Seal - Cretex Chimney Seal 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-375 F/C Sanitary 3) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 12M NYLO 12) MH Step ML-10-TDS-NCR - 10" Structure Total: 13743 lb						0 lb 1550 lb 3353 lb 4192 lb 2911 lb 10 lb 1440 lb 0 lb 0 lb 271 lb 0 lb 16 lb 0 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY I-CAST (HOE MC-375 F/C SANITARY). 4. 8.5" EXTERNAL CHIMNEY SEAL BY I-CAST. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 450.5'		Rim to Invert: 13.5'		Slack: 1"		Sump: 2"		Step Position: 270°				
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset		
Invert 1												
Invert 2												
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

RIGHT-SIDE UP VIEW (int. dimensions)

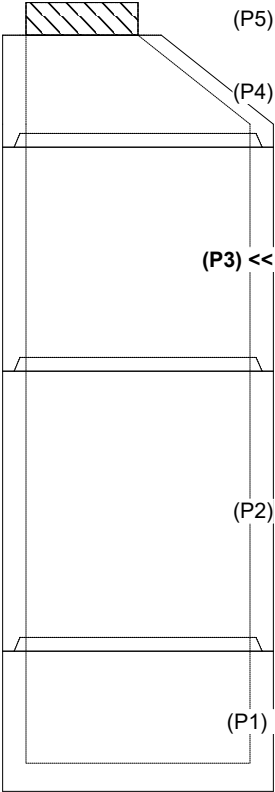

INSIDE WALL DIMENSIONS

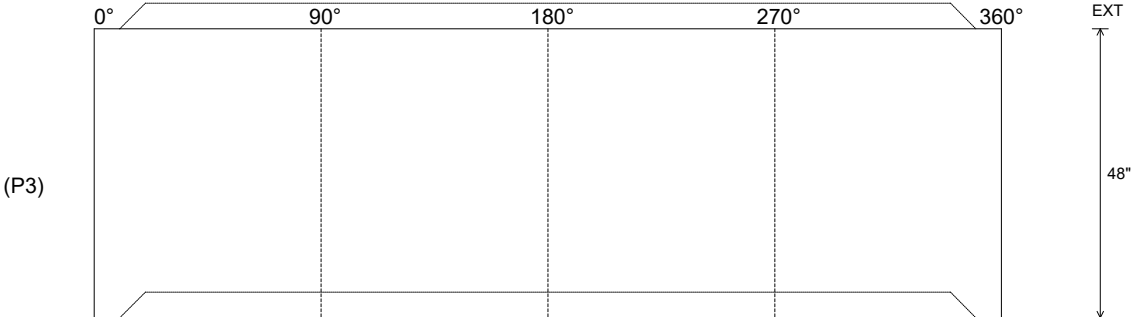

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 48" Height (Ext): 48"	Weight (Net): 3353 lb Volume (Net): 0.86cu.yd
----------------------------------	------------------------------------	--	--	--
