

Job Name: 25-4733 - The Paddock
Job Location: Springfield, KY
Contractor: Core & Main LP (Lou)

Plant: 100

Tech: Jared - F

5/14/2026 11:31:09 AM

PC: T. Lewis



Structure ID: SSWR-1

P2 MH048CN24

ECC CONE w/ 24" HOLE F/G

- P3) 24" - CASTING HEIGHT - 7"
P2) 48" - ECC CONE w/ 24" HOLE F/G - 24"
P1) 48" - MH BASE T/n - 18"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - MH INVERT CHANNEL - FULL HEIGHT
1) CASTING - HOE MC-315 F/C Sanitary
1) 48" - Conseal CS-102 1.00" (Double)
1) Quik-Lok - QL-08-C
1) PSX - 12M NYLO
3) MH Step ML-10-TDS-NCR - 10"

0 lb
1550 lb
2501 lb
0 lb
0 lb
1440 lb
258 lb
0 lb
1 lb
8 lb
0 lb



Structure Total: 5758 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HOE MC-315 F/C SANITARY).

REINFORCING PER ASTM A615 (GRADE 60).

- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

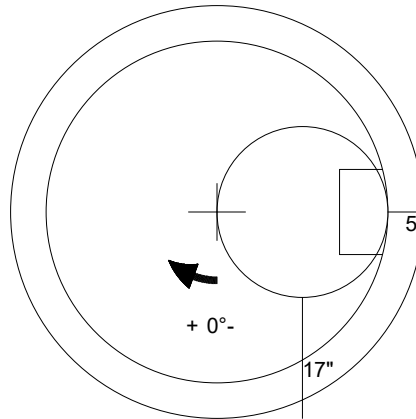

48" - ECC CONE w/ 24" HOLE F/G - 24" - (P2)

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 24"

Weight (Net): 1550 lb
Volume (Net): 0.33cu.yd
