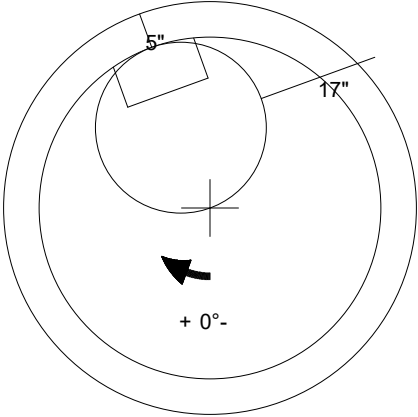



Job Name: 25-4733 - The Paddock Job Location: Springfield, KY Contractor: Core & Main LP (Lou)		Plant: 100 5/4/2026 6:49:55 PM	Tech: Jared - F PC: T. Lewis		
Structure ID: SSWR-3					
P3 MH048CN36		ECC CONE w/ 24" HOLE F/G			
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING F/F - 4" P3) 48" - ECC CONE w/ 24" HOLE F/G - 36" P2) 48" - MH RISER T/G - 48" P1) 48" - MH BASE T/h - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-315 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 12M NYLO 1) PSX - 12-06 NYLO 9) MH Step ML-10-TDS-NCR - 10"		0 lb 270 lb 3000 lb 3353 lb 3282 lb 0 lb 0 lb 1440 lb 258 lb 0 lb 16 lb 8 lb 0 lb Structure Total: 11627 lb	Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-315 F/C SANITARY). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
					
					
48" - ECC CONE w/ 24" HOLE F/G - 36" - (P3)					
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 36"	Weight (Net): 3000 lb Volume (Net): 0.5cu.yd	
