

Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam



Size: 60"

Rim to Invert: 6.42'

Floor Height: 8"

Slack: 0.54"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.


P3) 24" x 30" - CASTING HEIGHT - 3.50"
P2) 60" - MH FLAT TOP w/24"x30" Hole F/G - 13"
P1) 60" - MH BASE T/n - 60"
1) CASTING - HOE KY-460-11 F/G (DBI 11)
2) Hole - 44
5) MH Step ML-10-TDS-NCR - 10"

0 lb
2668 lb
7314 lb
421 lb
0 lb
0 lb


Structure Total: 10403 lb

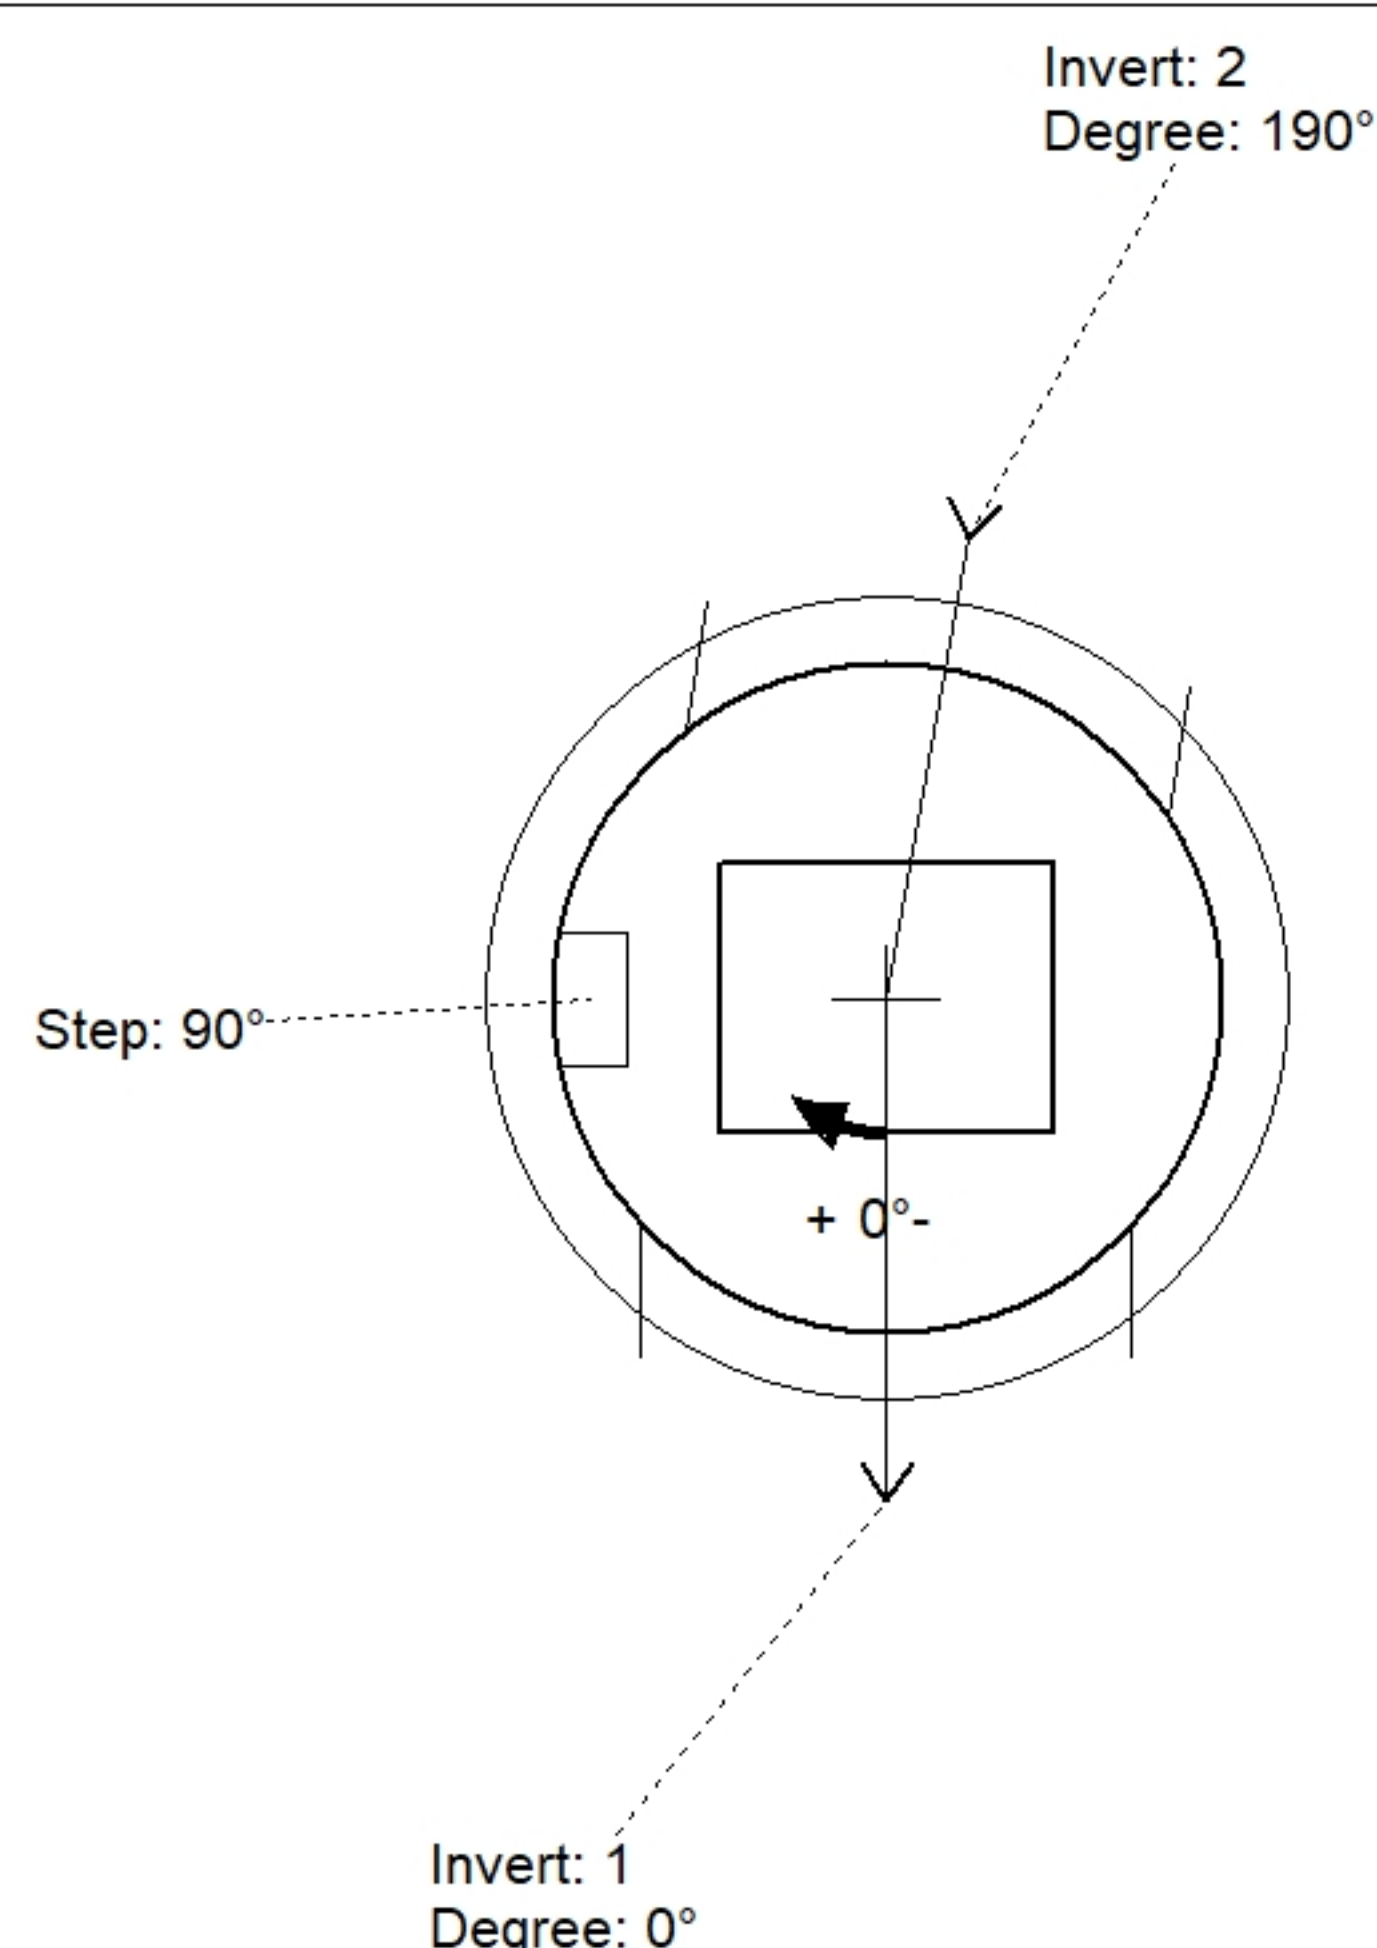

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	582.92'							
Reducer								
Invert 1	576.5'	0°	36" HDPE	41.7"	44"	Hole 44	-2.85"	P1
Invert 2	576.5'	190°	36" HDPE	41.7"	44"	Hole 44	-2.85"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

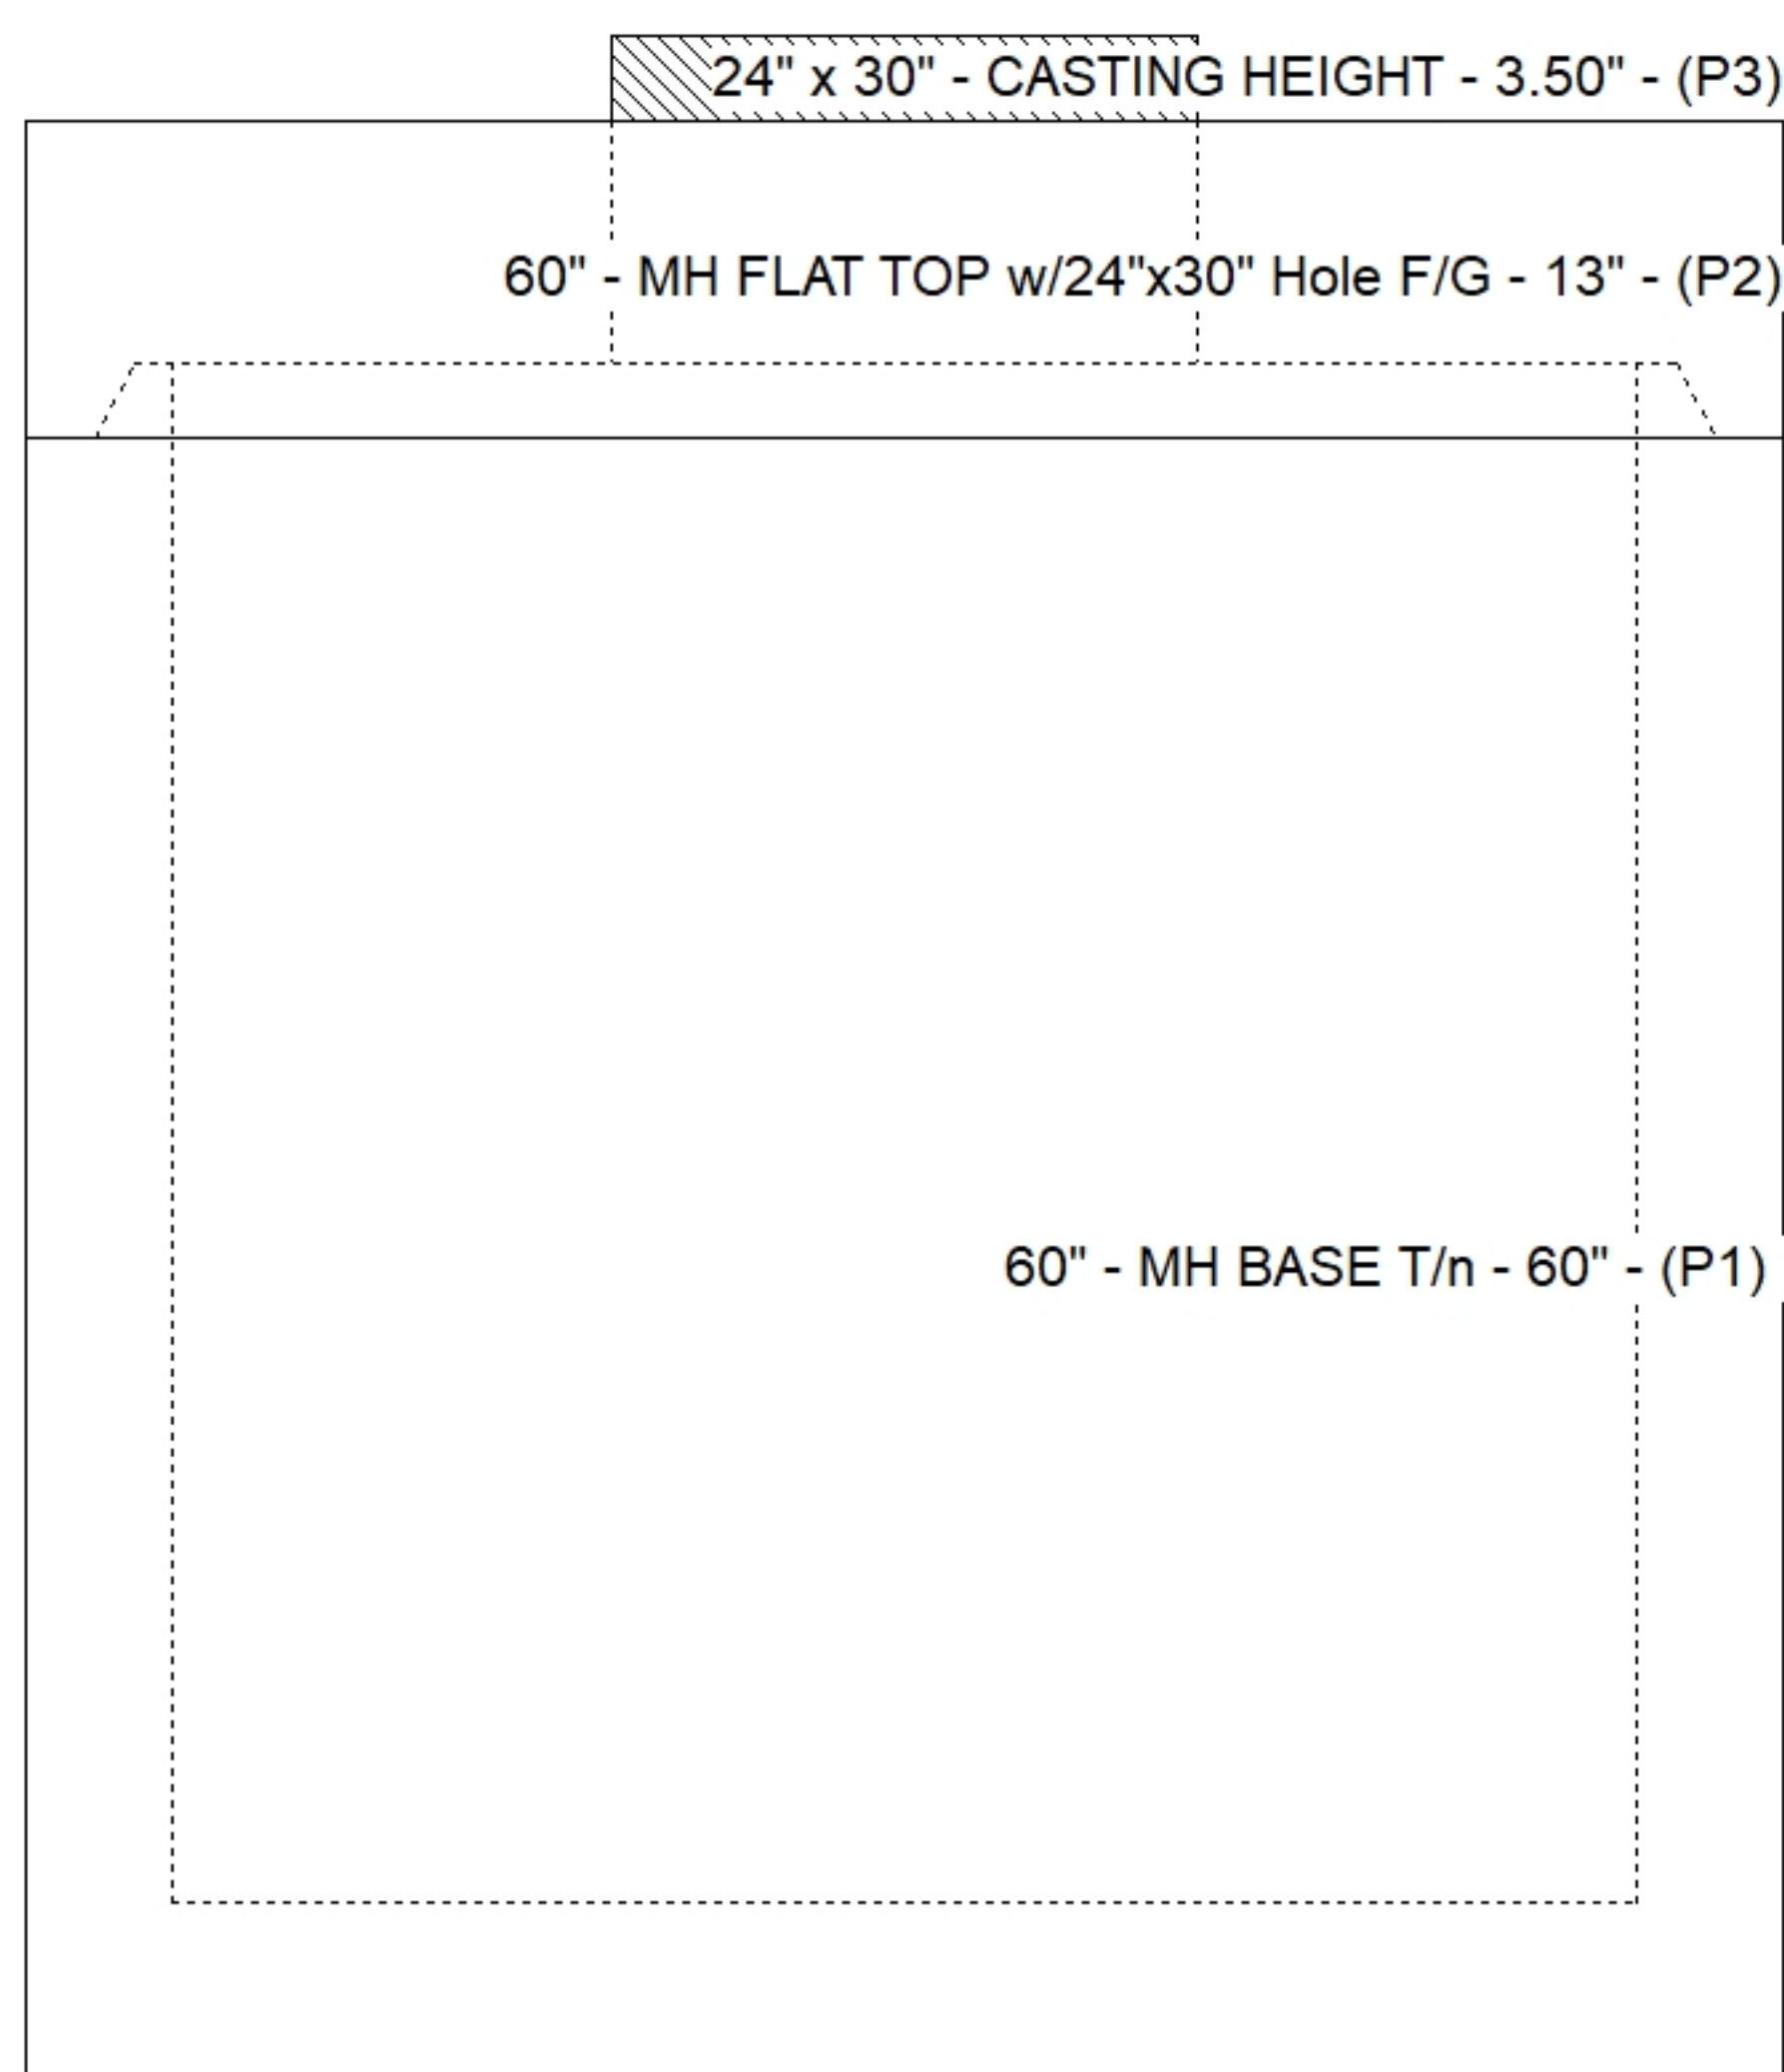

Default - Interior Dimensions

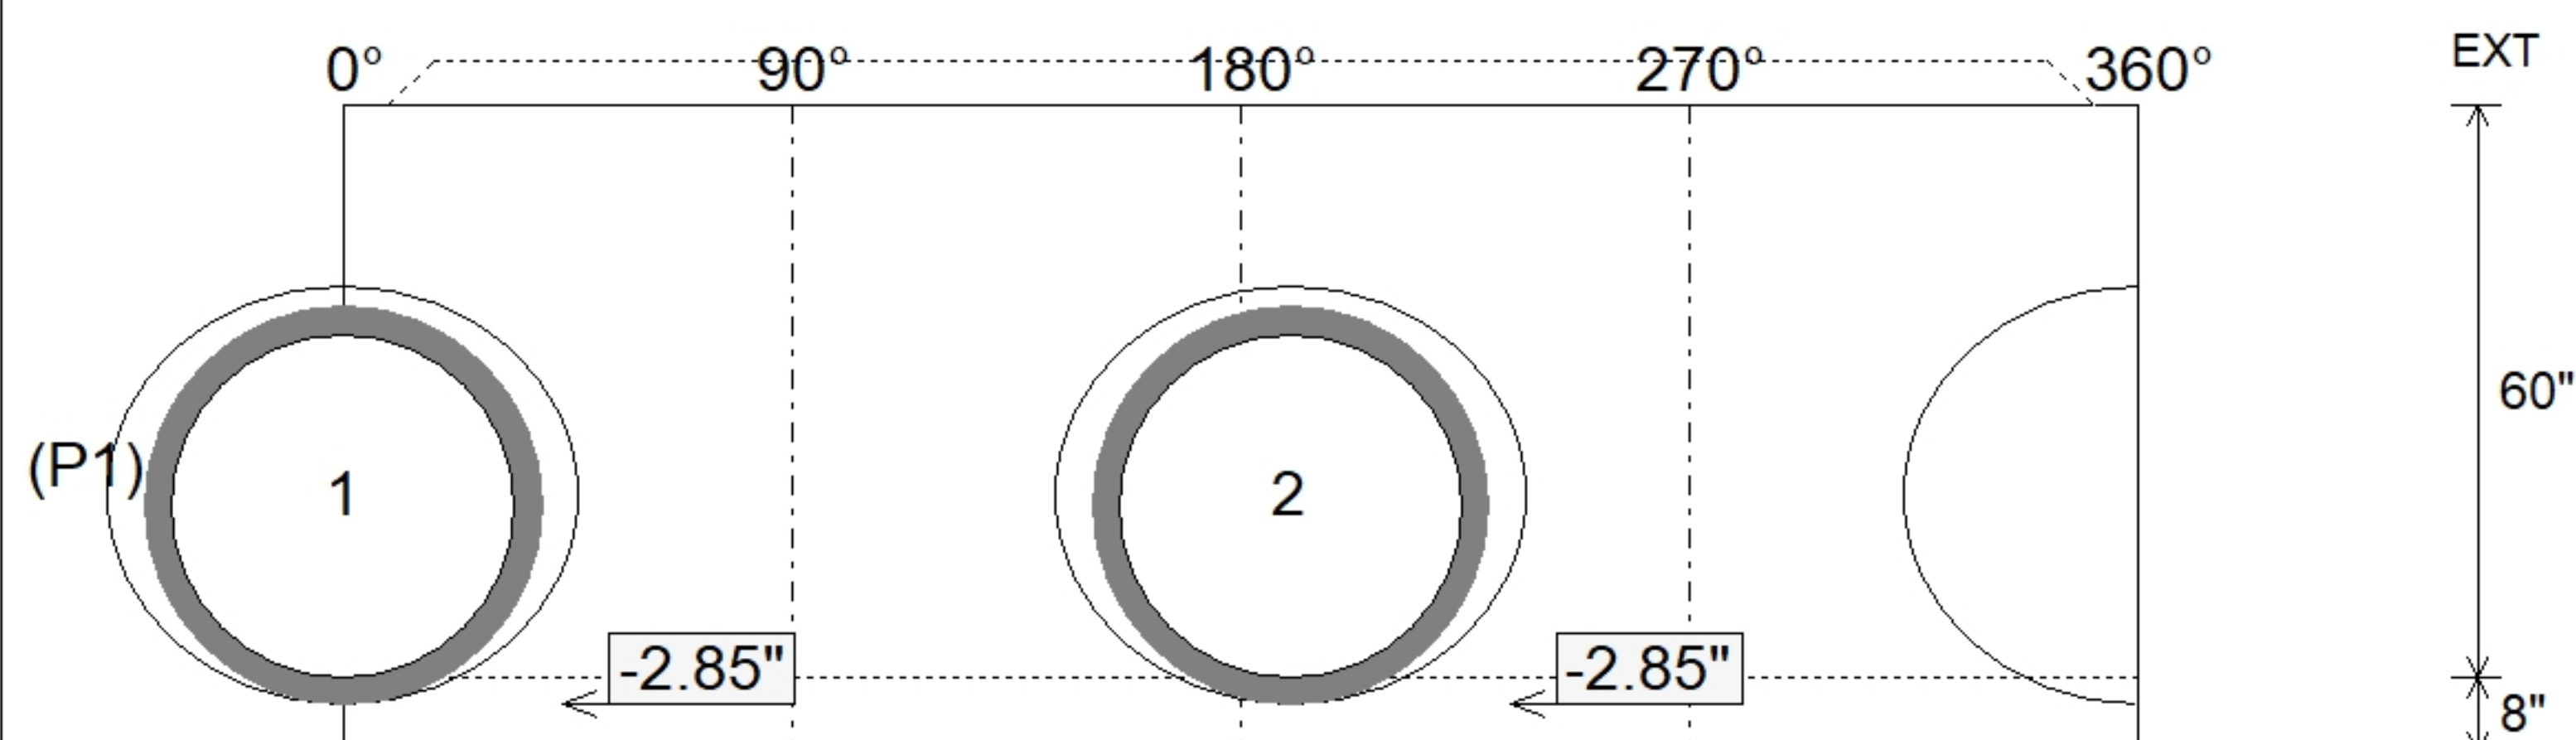

SUBMITTAL
APPROVED BY:
