

Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam



Size: 72"

Rim to Invert: 7.14'

Floor Height: 8"


Slack: 0.18"

- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.


P3) 48" x 48" - CASTING HEIGHT - 4.5"
P2) 72" - MH FLAT TOP w/48"x48" Hole F/G - 15"
P1) 72" - MH BASE T/n - 66"
1) CASTING - HOE 918 F/G
1) 72" - Conseal CS-102 1.00"
1) 48" x 48" - Conseal CS-102 1.00"
2) Hole - 44
2) Hole - 18
6) MH Step ML-10-TDS-NCR - 10"

0 lb
4411 lb
11321 lb
228 lb
0 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 15960 lb

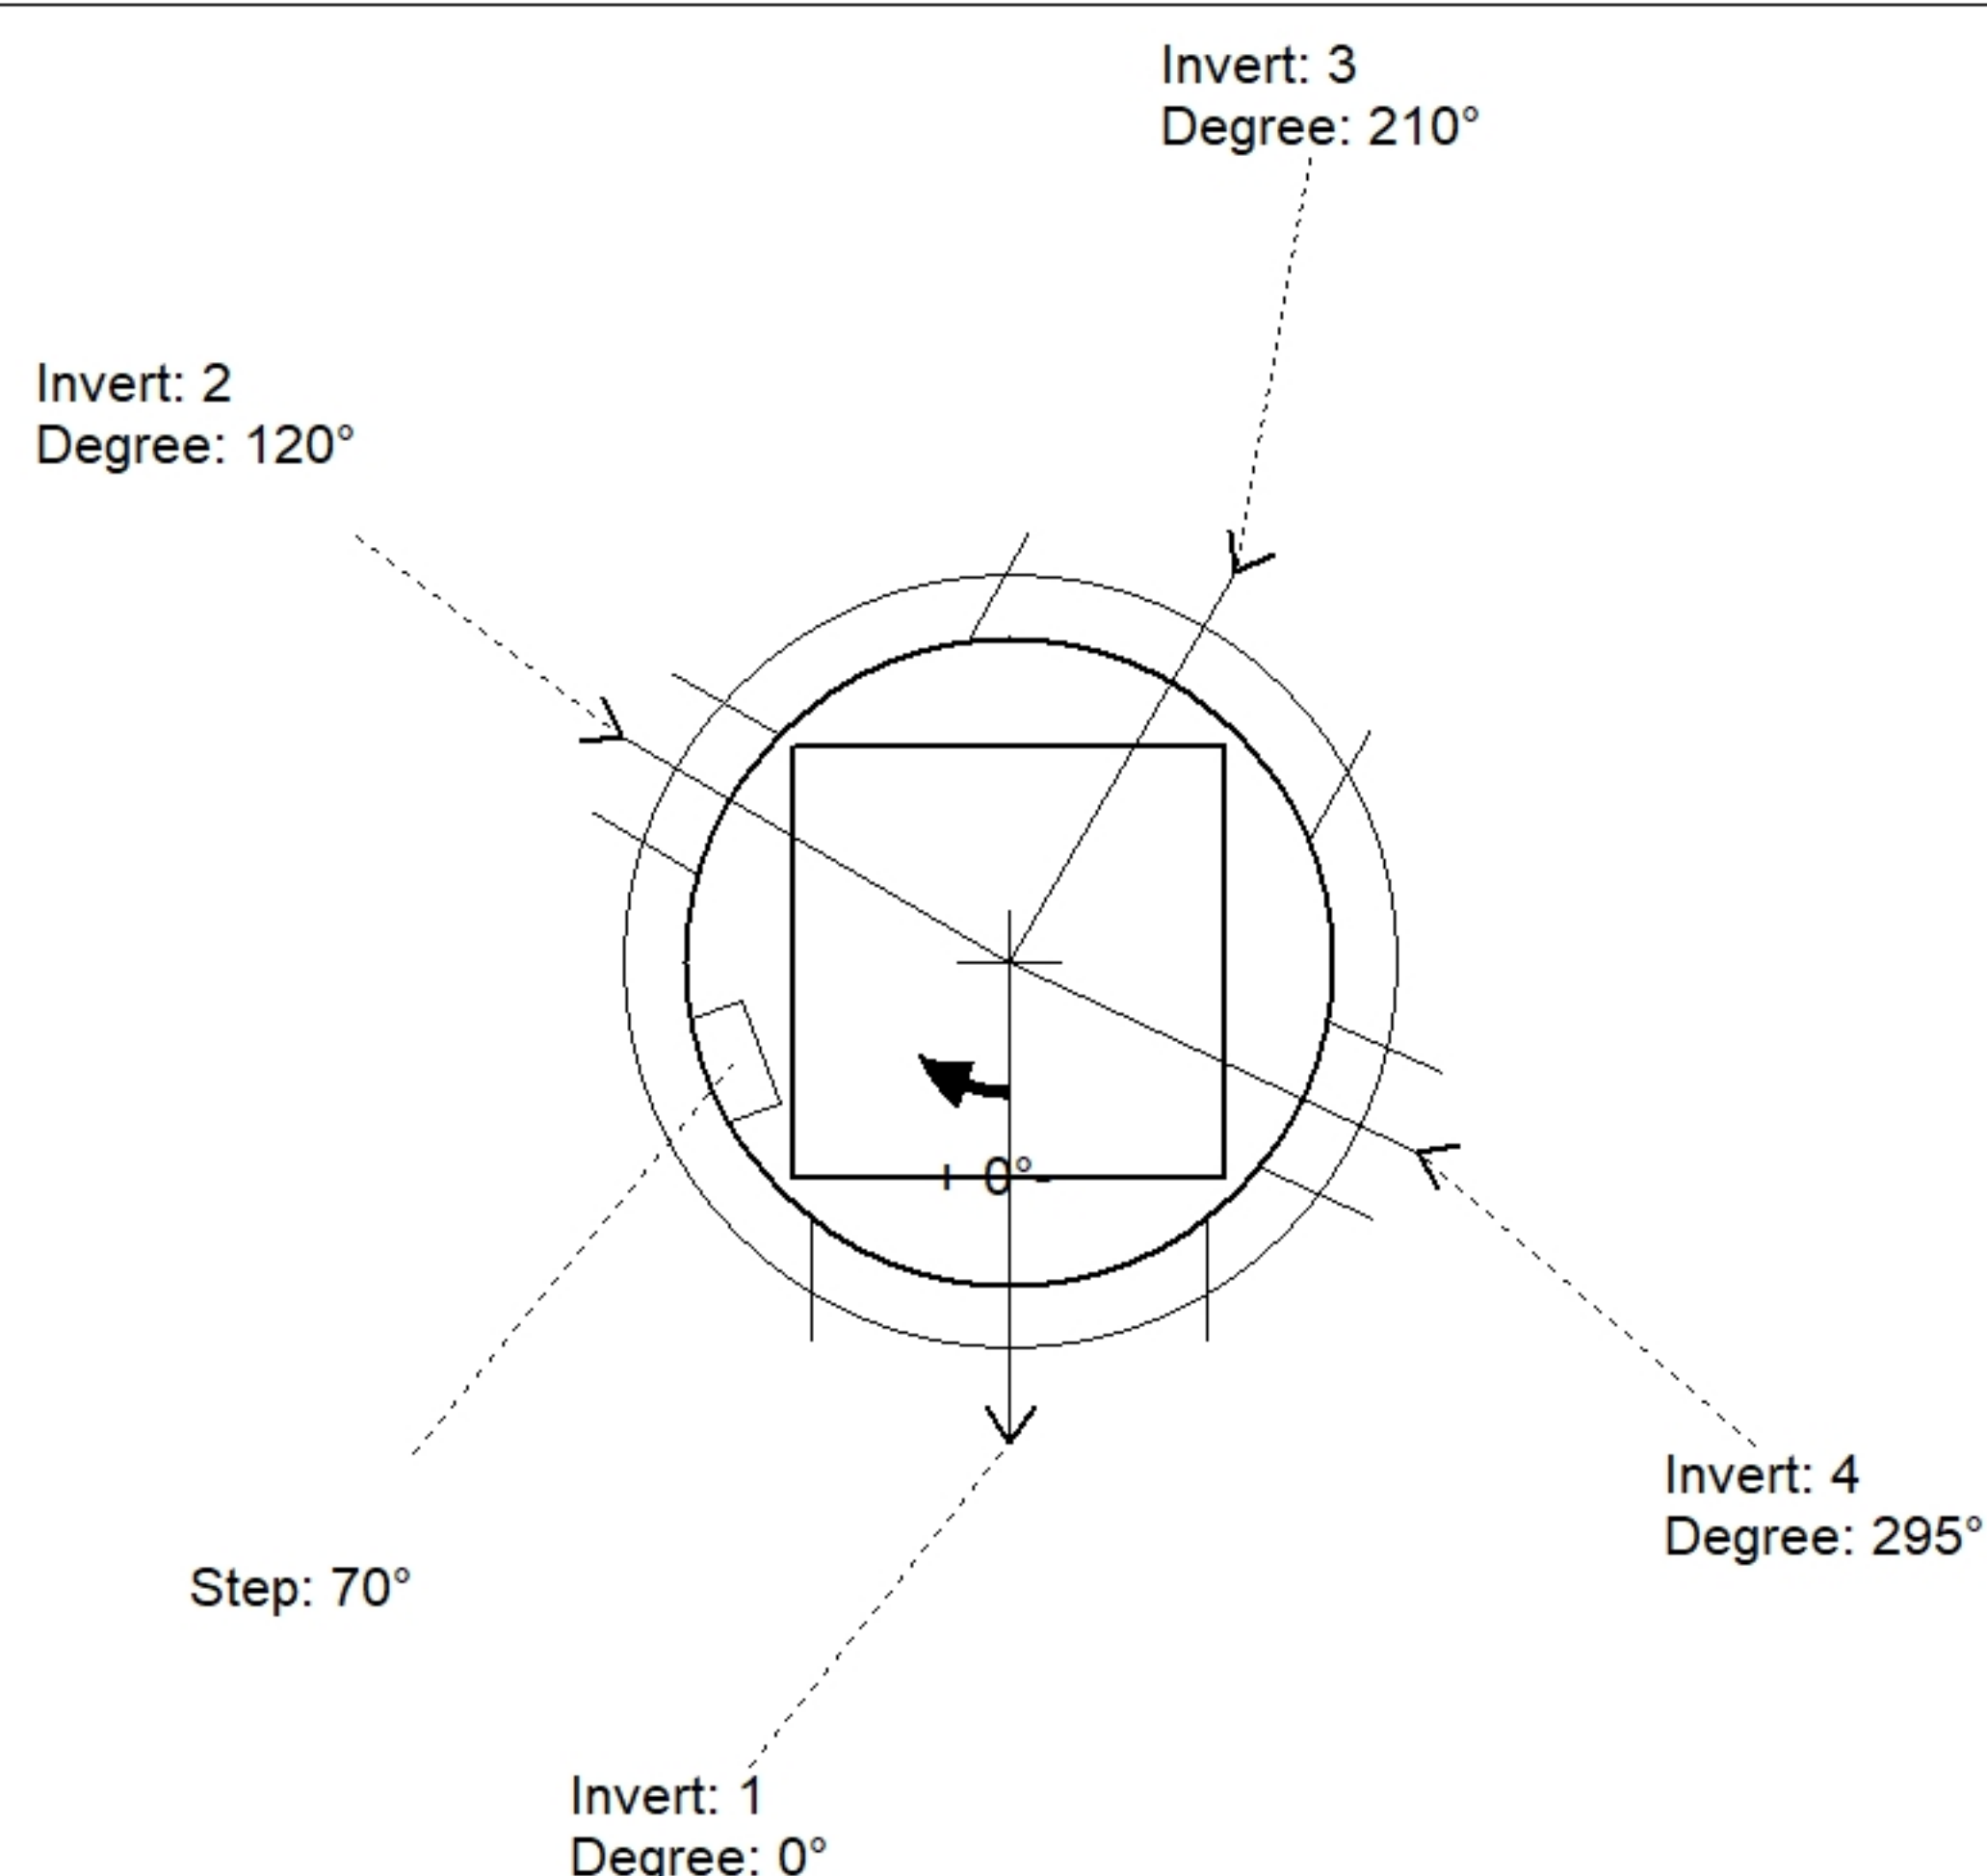

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	587.36'							
Reducer								
Invert 1	580.22'	0°	36" HDPE	41.7"	44"	Hole 44	-2.85"	P1
Invert 2	580.22'	120°	15" PVC SDR35	15.3"	18"	Hole 18	-0.15"	P1
Invert 3	580.22'	210°	36" HDPE	41.7"	44"	Hole 44	-2.85"	P1
Invert 4	580.22'	295°	12" HDPE	14.5"	18"	Hole 18	-1.25"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

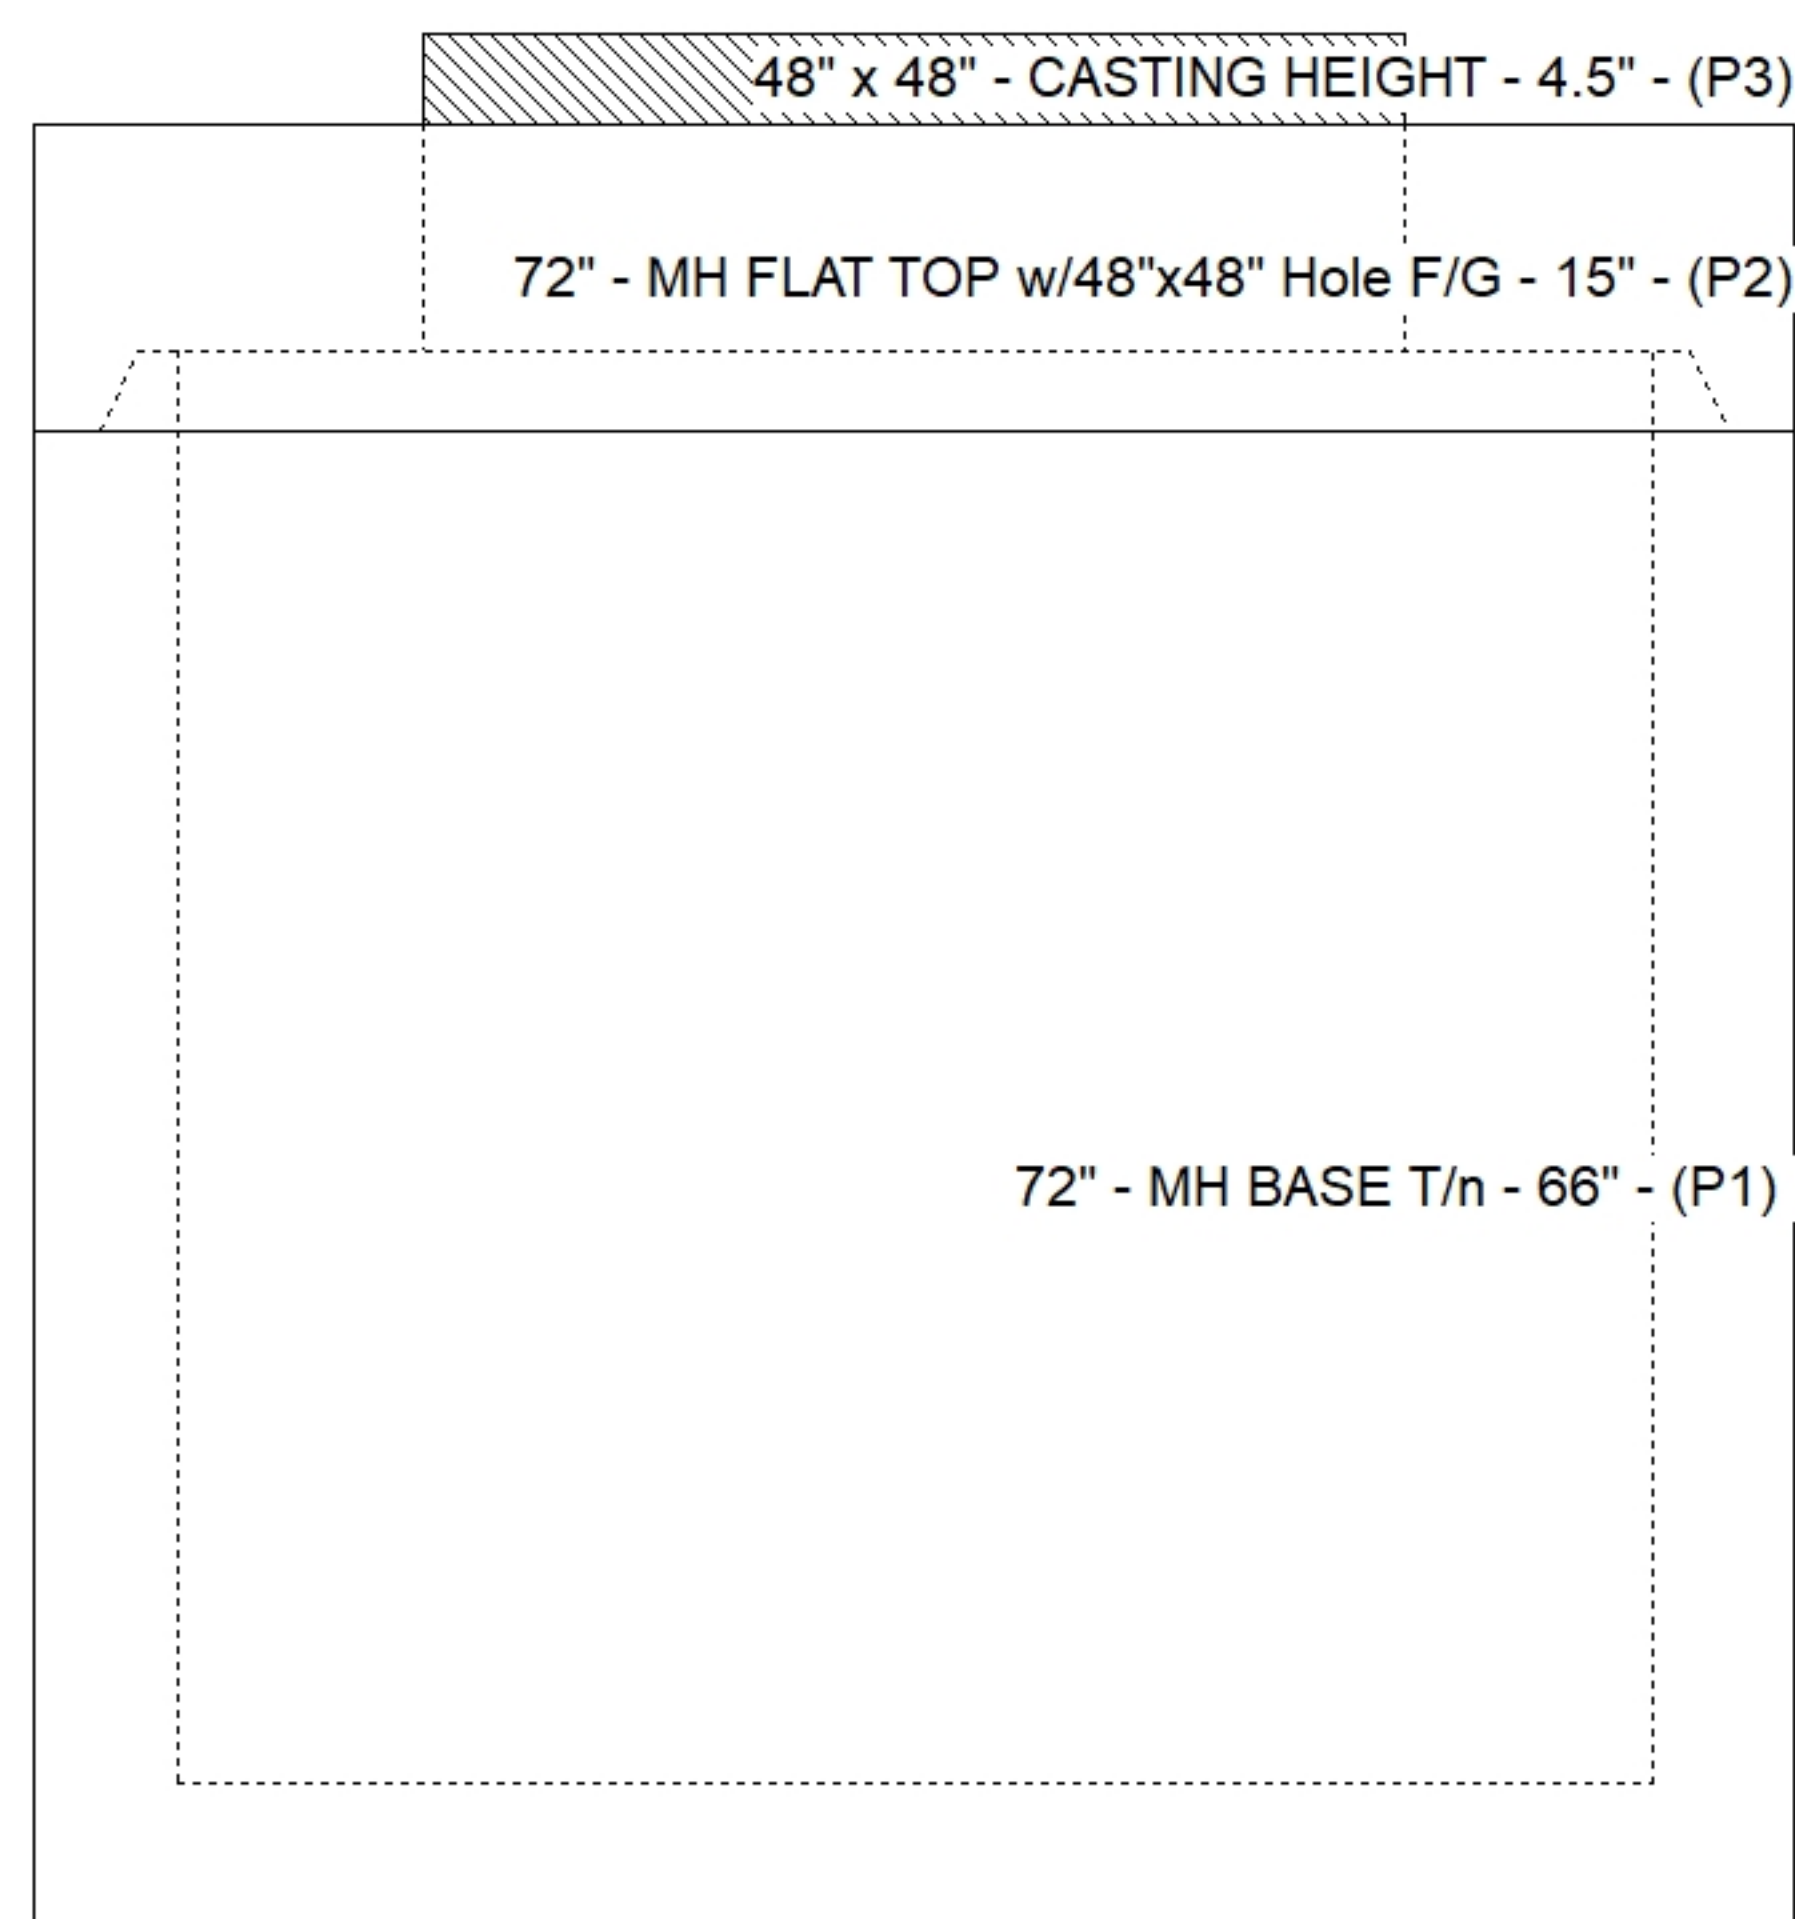

Default - Interior Dimensions

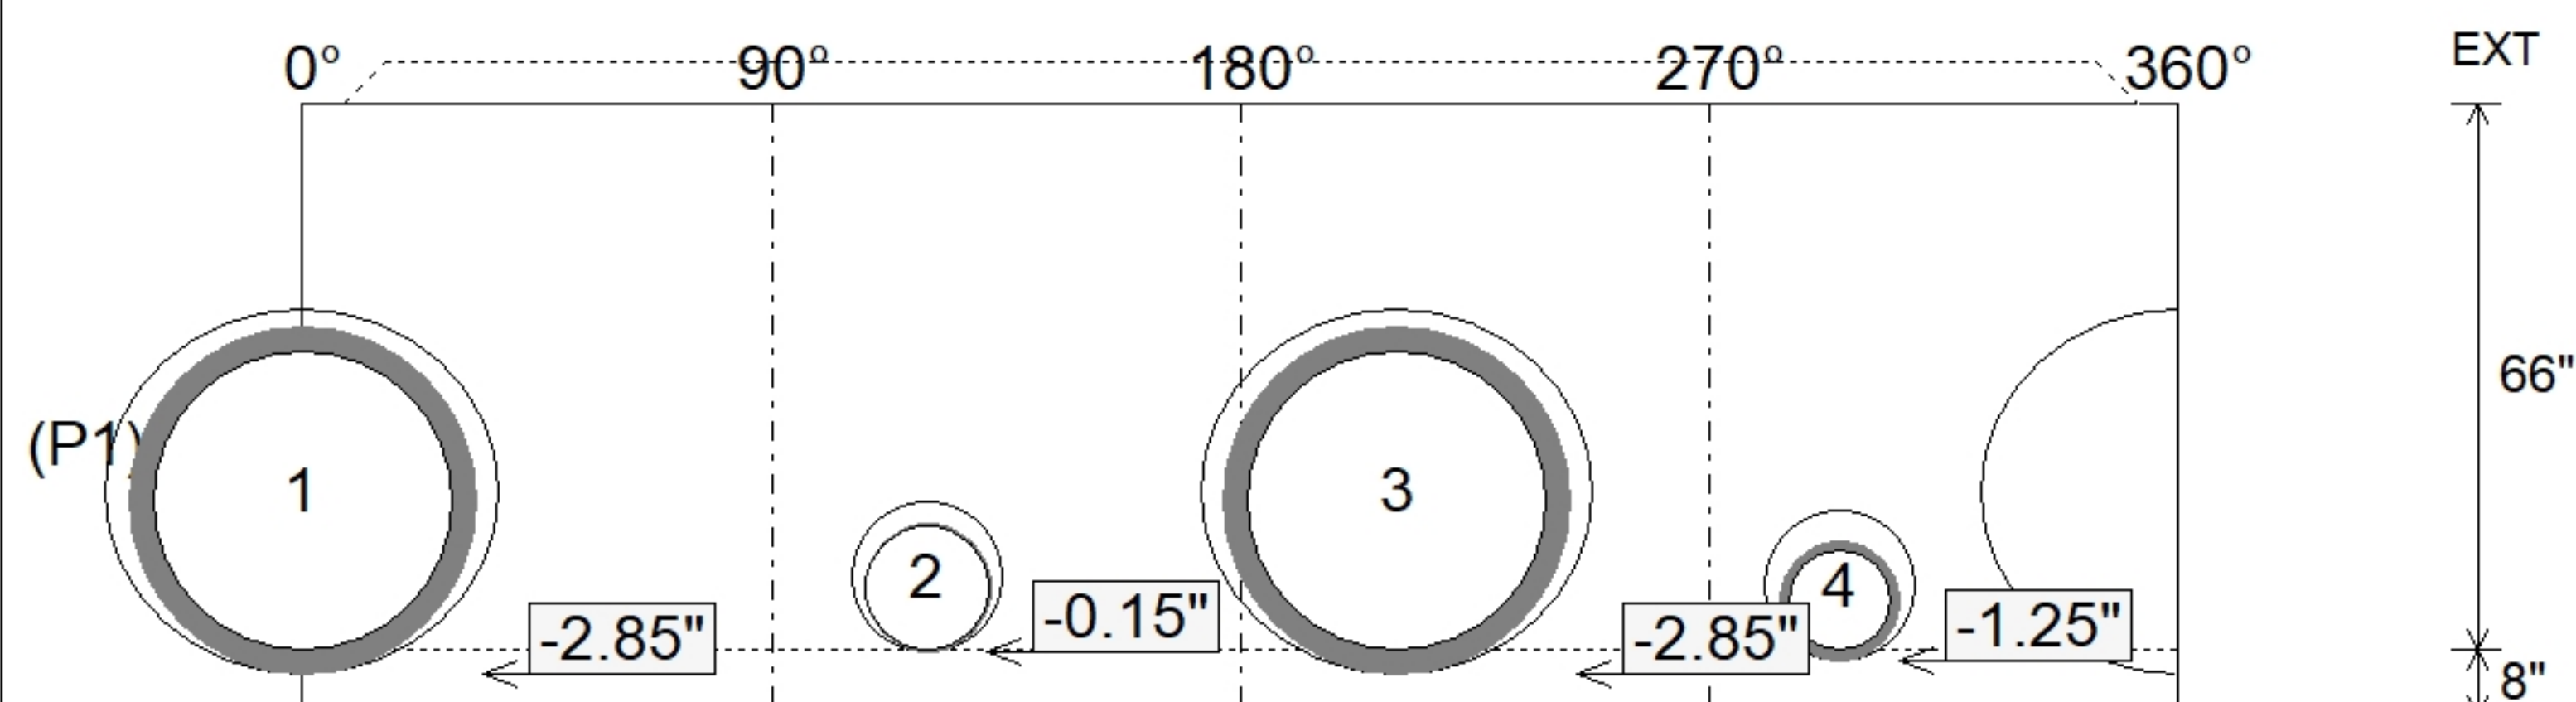

SUBMITTAL
APPROVED BY:
