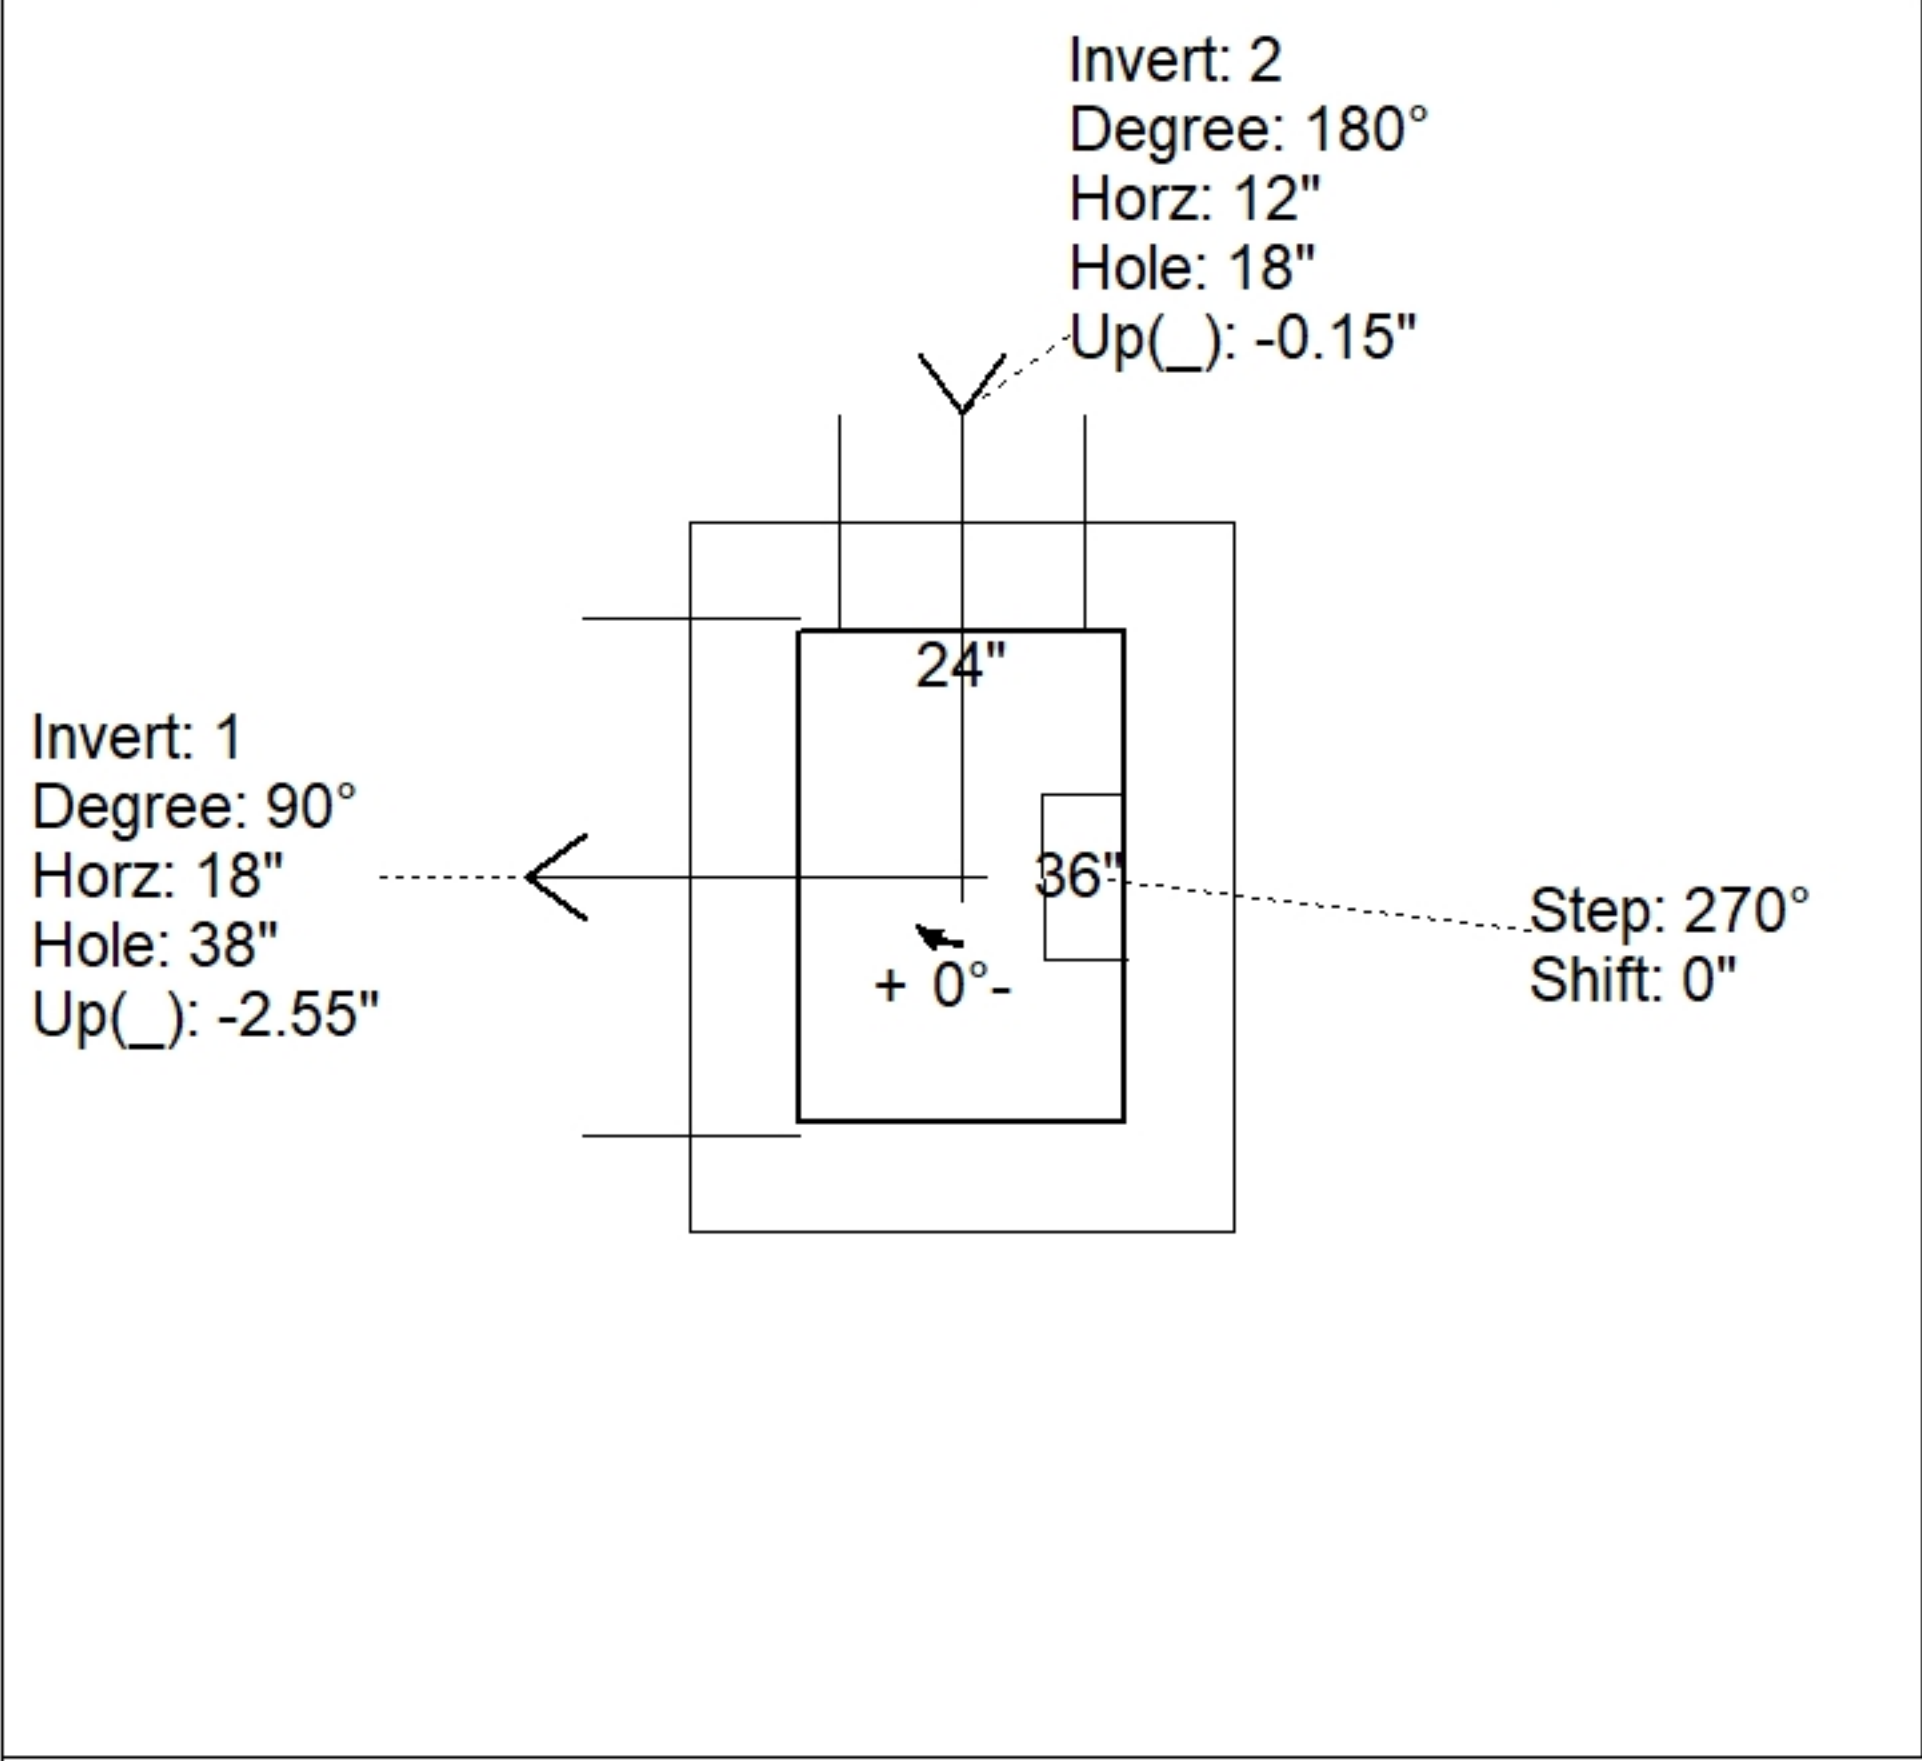
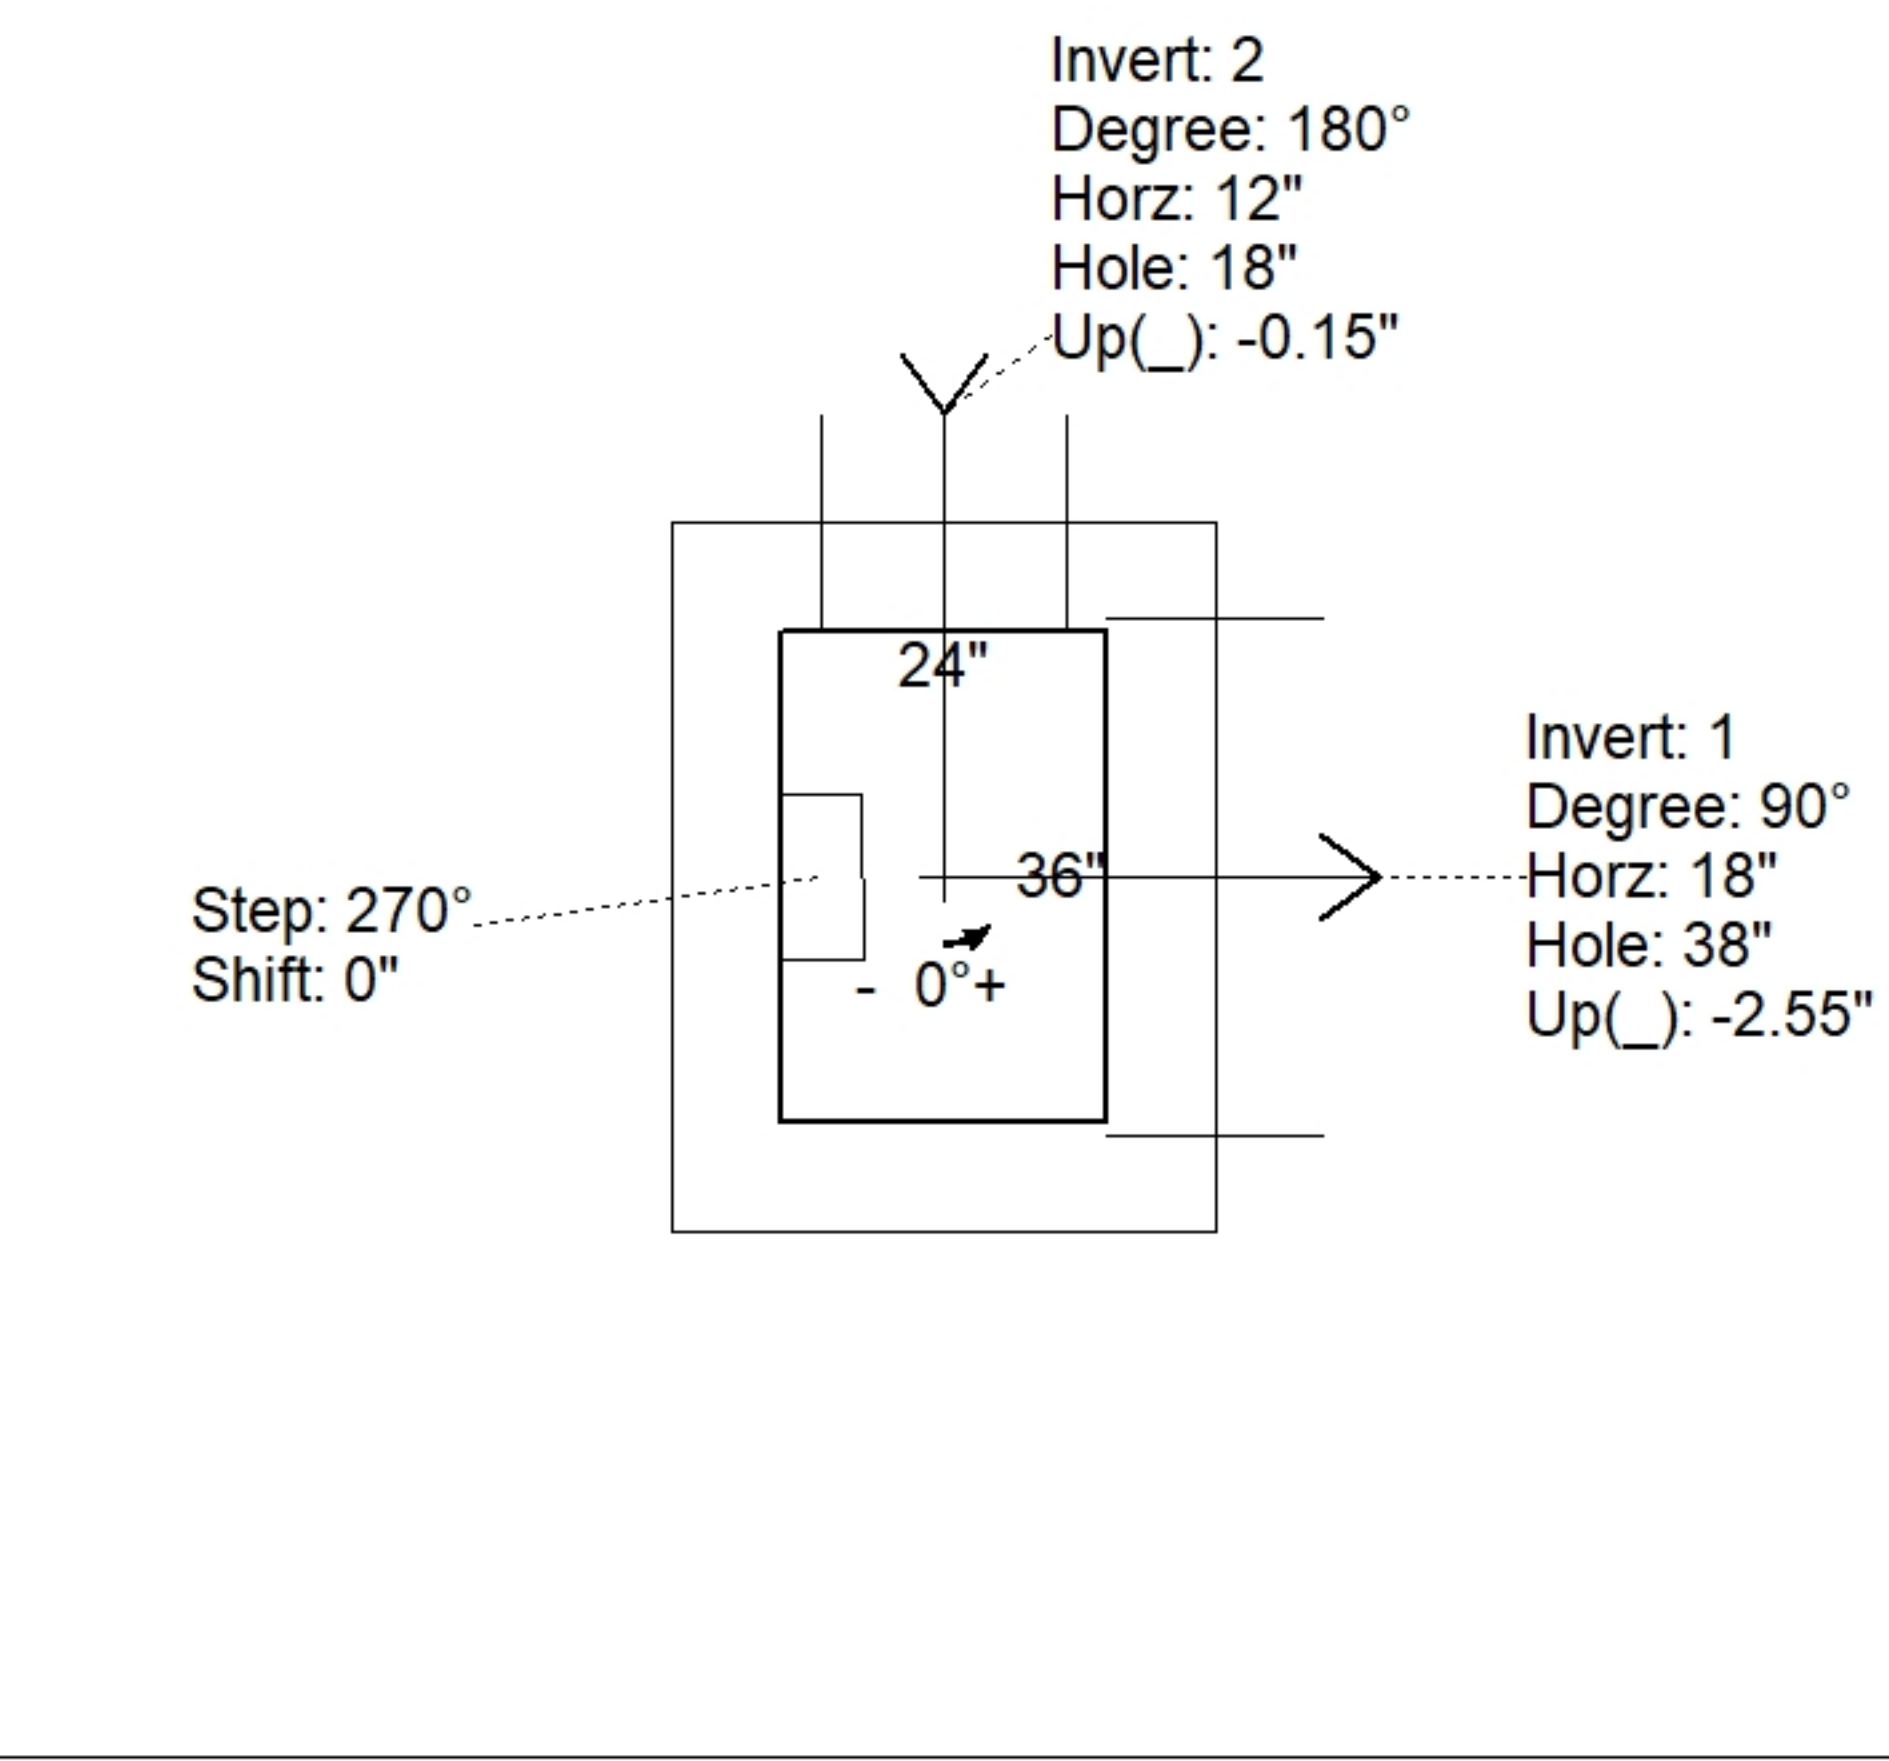
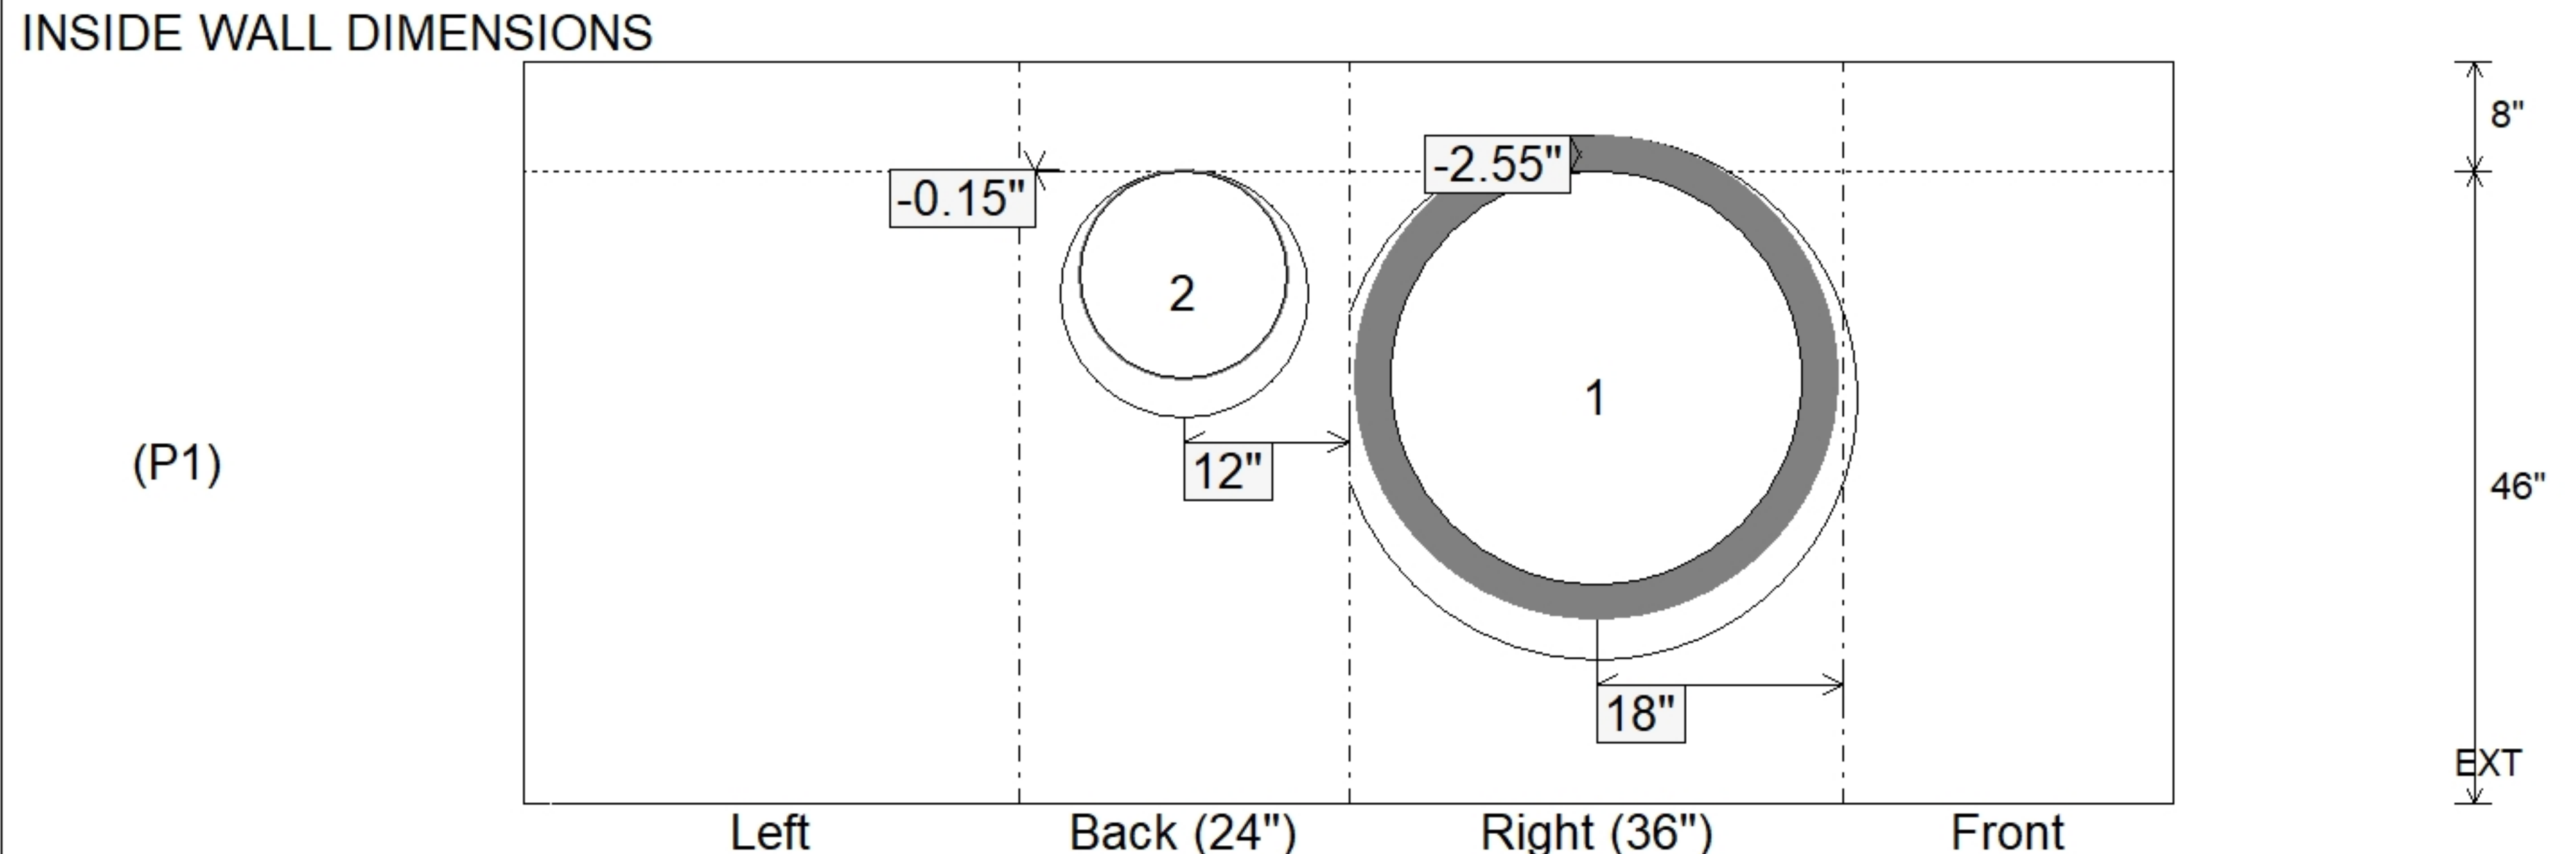


Job Name: 26-1000P2 Clark Distributing New HQ - Site Structures				Plant: Beaver Dam		Tech: S. Felletter				
Job Location: Bowling Green, KY				8/7/2026 10:38:45 AM		PC: M. Sullivan				
Contractor: Scotty's Contracting & Stone, LLC										
Structure ID: DBI-12										
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht F/n						
P2) 24" x 36" - CASTING HEIGHT - 0" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 46" 1) CASTING - HOE 918 F/G 1) 48" x 48" - Conseal CS-102 1.00" 1) Hole - 38 1) Hole - 18 4) MH Step ML-10-TDS-NCR - 10"						0 lb 5348 lb 228 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 5576 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE 918 F/G). . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.		
Rim: 587.63' Rim to Invert: 3.9' Slack: 0.8' Sump: 0' Step Position: 0°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	583.73'	90°	26"	30" HDPE	35.1"	Hole 38	38"	37"	-2.55"	0"
Invert 2	583.73'	180°	20"	15" PVC SDR35	15.3"	Hole 18	18"	18"	-0.15"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions)  INSIDE WALL DIMENSIONS 										
Coating (Int):			Seam Up: Flat		Wall Thickness: 8"		Height (Int): 46"		Weight (Net): 5348 lb	
Coating (Ext):			Seam Dn: n/a		Floor Height: 8"		Height (Ext): 54"		Volume (Net): 1.37cu.yd	
