

Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam



Slack: 0.38"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P4) 24" x 30" - CASTING HEIGHT - 3.50"
P3) 36" x 48" - CB FLAT TOP 8"W w/24"x30" HOLE F/F - 8"
P2) 36" x 48" - BOX RISER 8inW F/G - 48"
P1) 36" x 48" - BOX BASE 8inW, 8inF T/n - 60"
1) CASTING - HOE KY-460-11 F/G (DBI 11)
2) 36" x 48" - Conseal CS-102 1.00"
1) 24" x 30" - Conseal CS-102 1.00"
1) Hole - 50
1) Hole - 44
5) MH Step ML-10-TDS-NCR - 10"

0 lb
1751 lb
6444 lb
8280 lb
421 lb
0 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 16896 lb

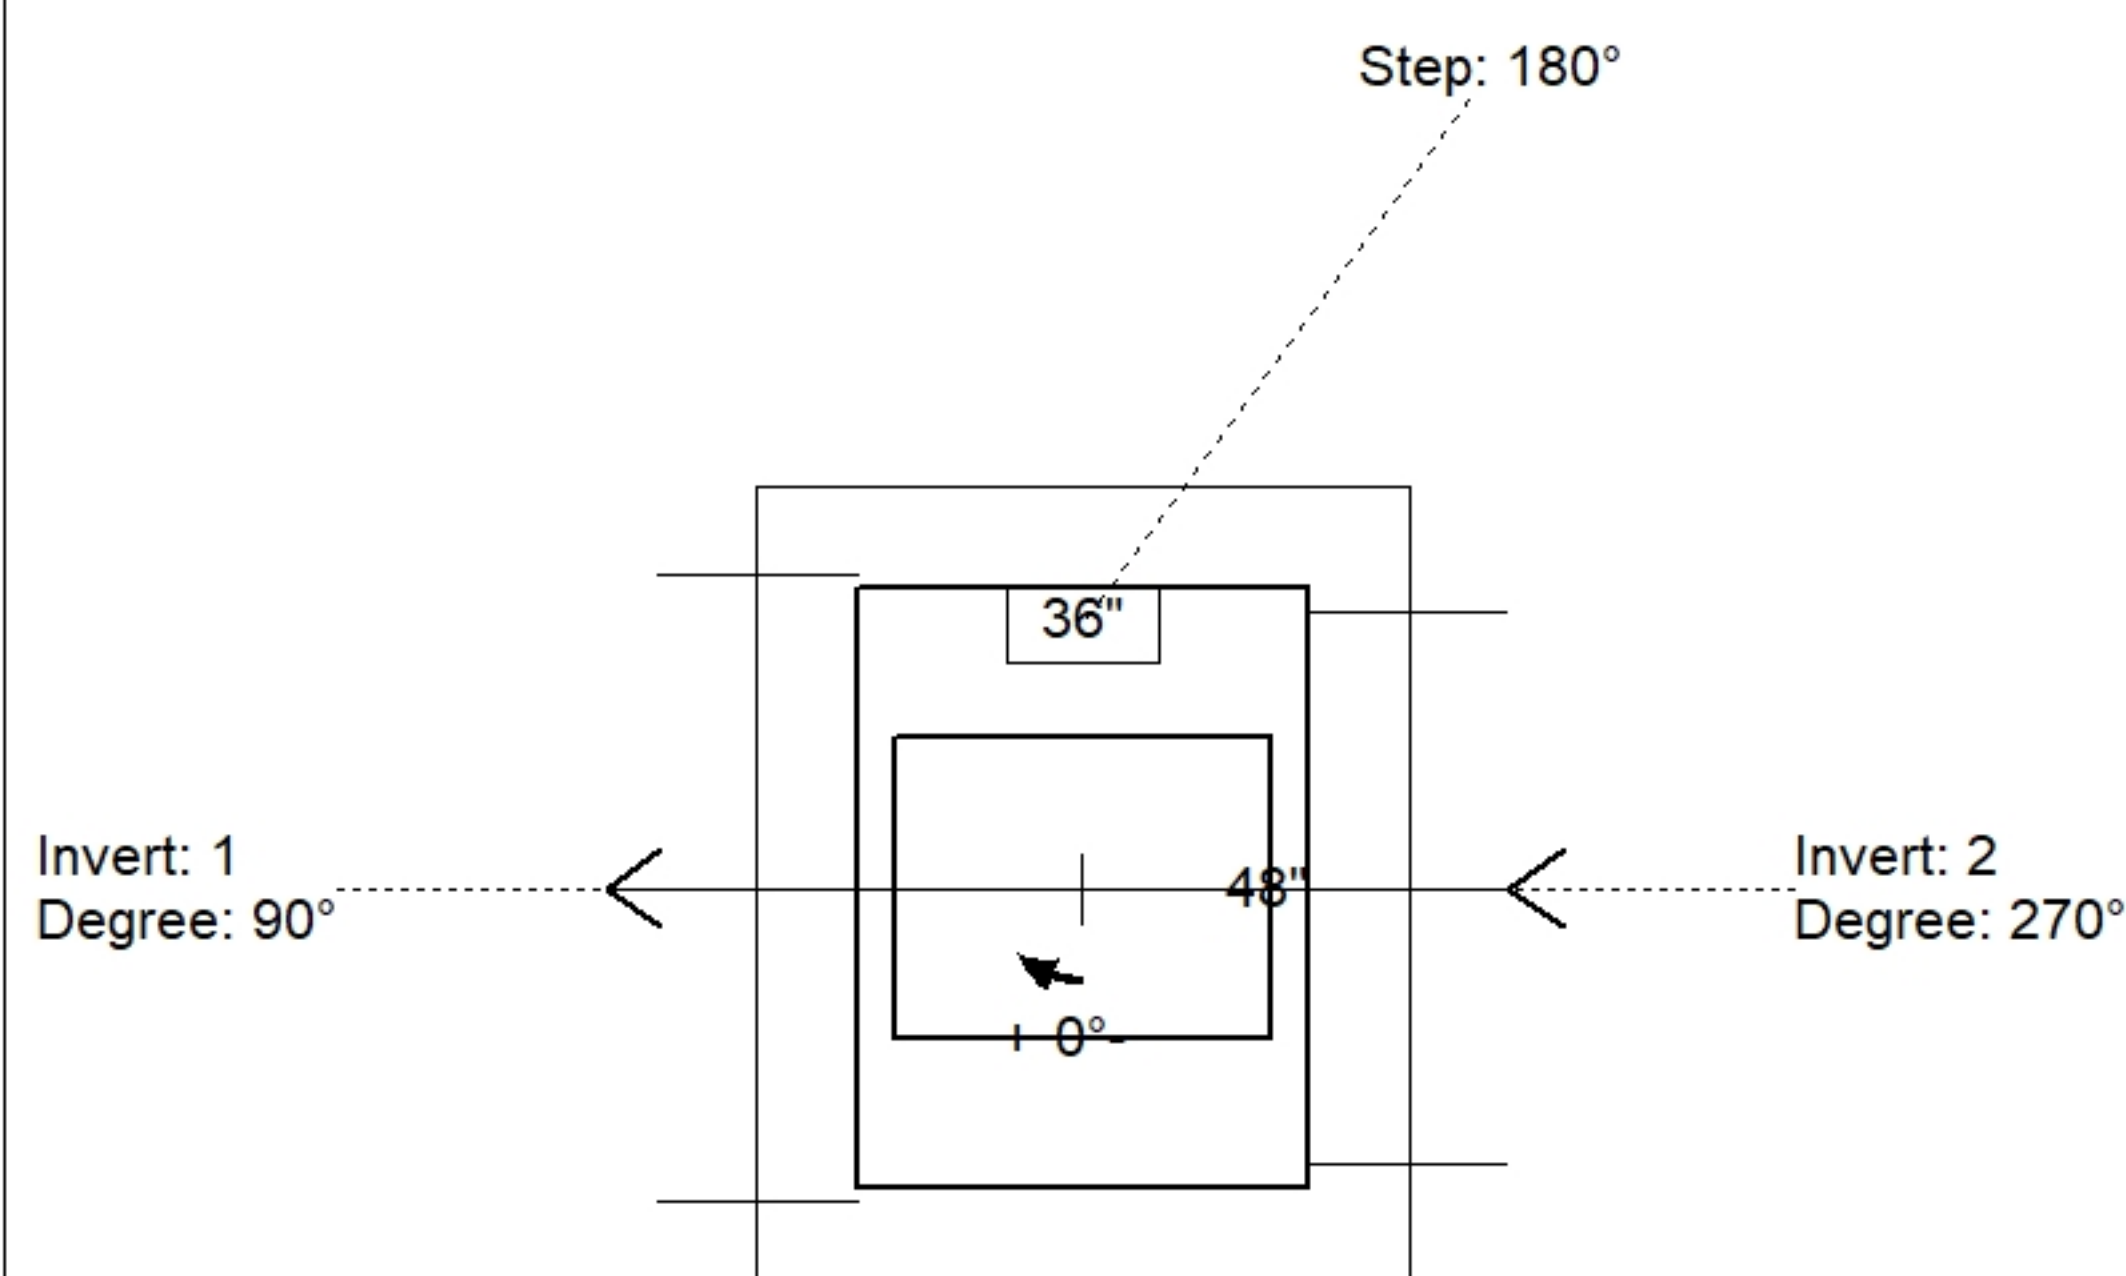

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	591'							
Reducer								
Invert 1	581.01'	90°	42" HDPE	47.7"	50"	Hole 50	-3.15"	P1
Invert 2	581.01'	270°	36" HDPE	41.7"	44"	Hole 44	-2.85"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

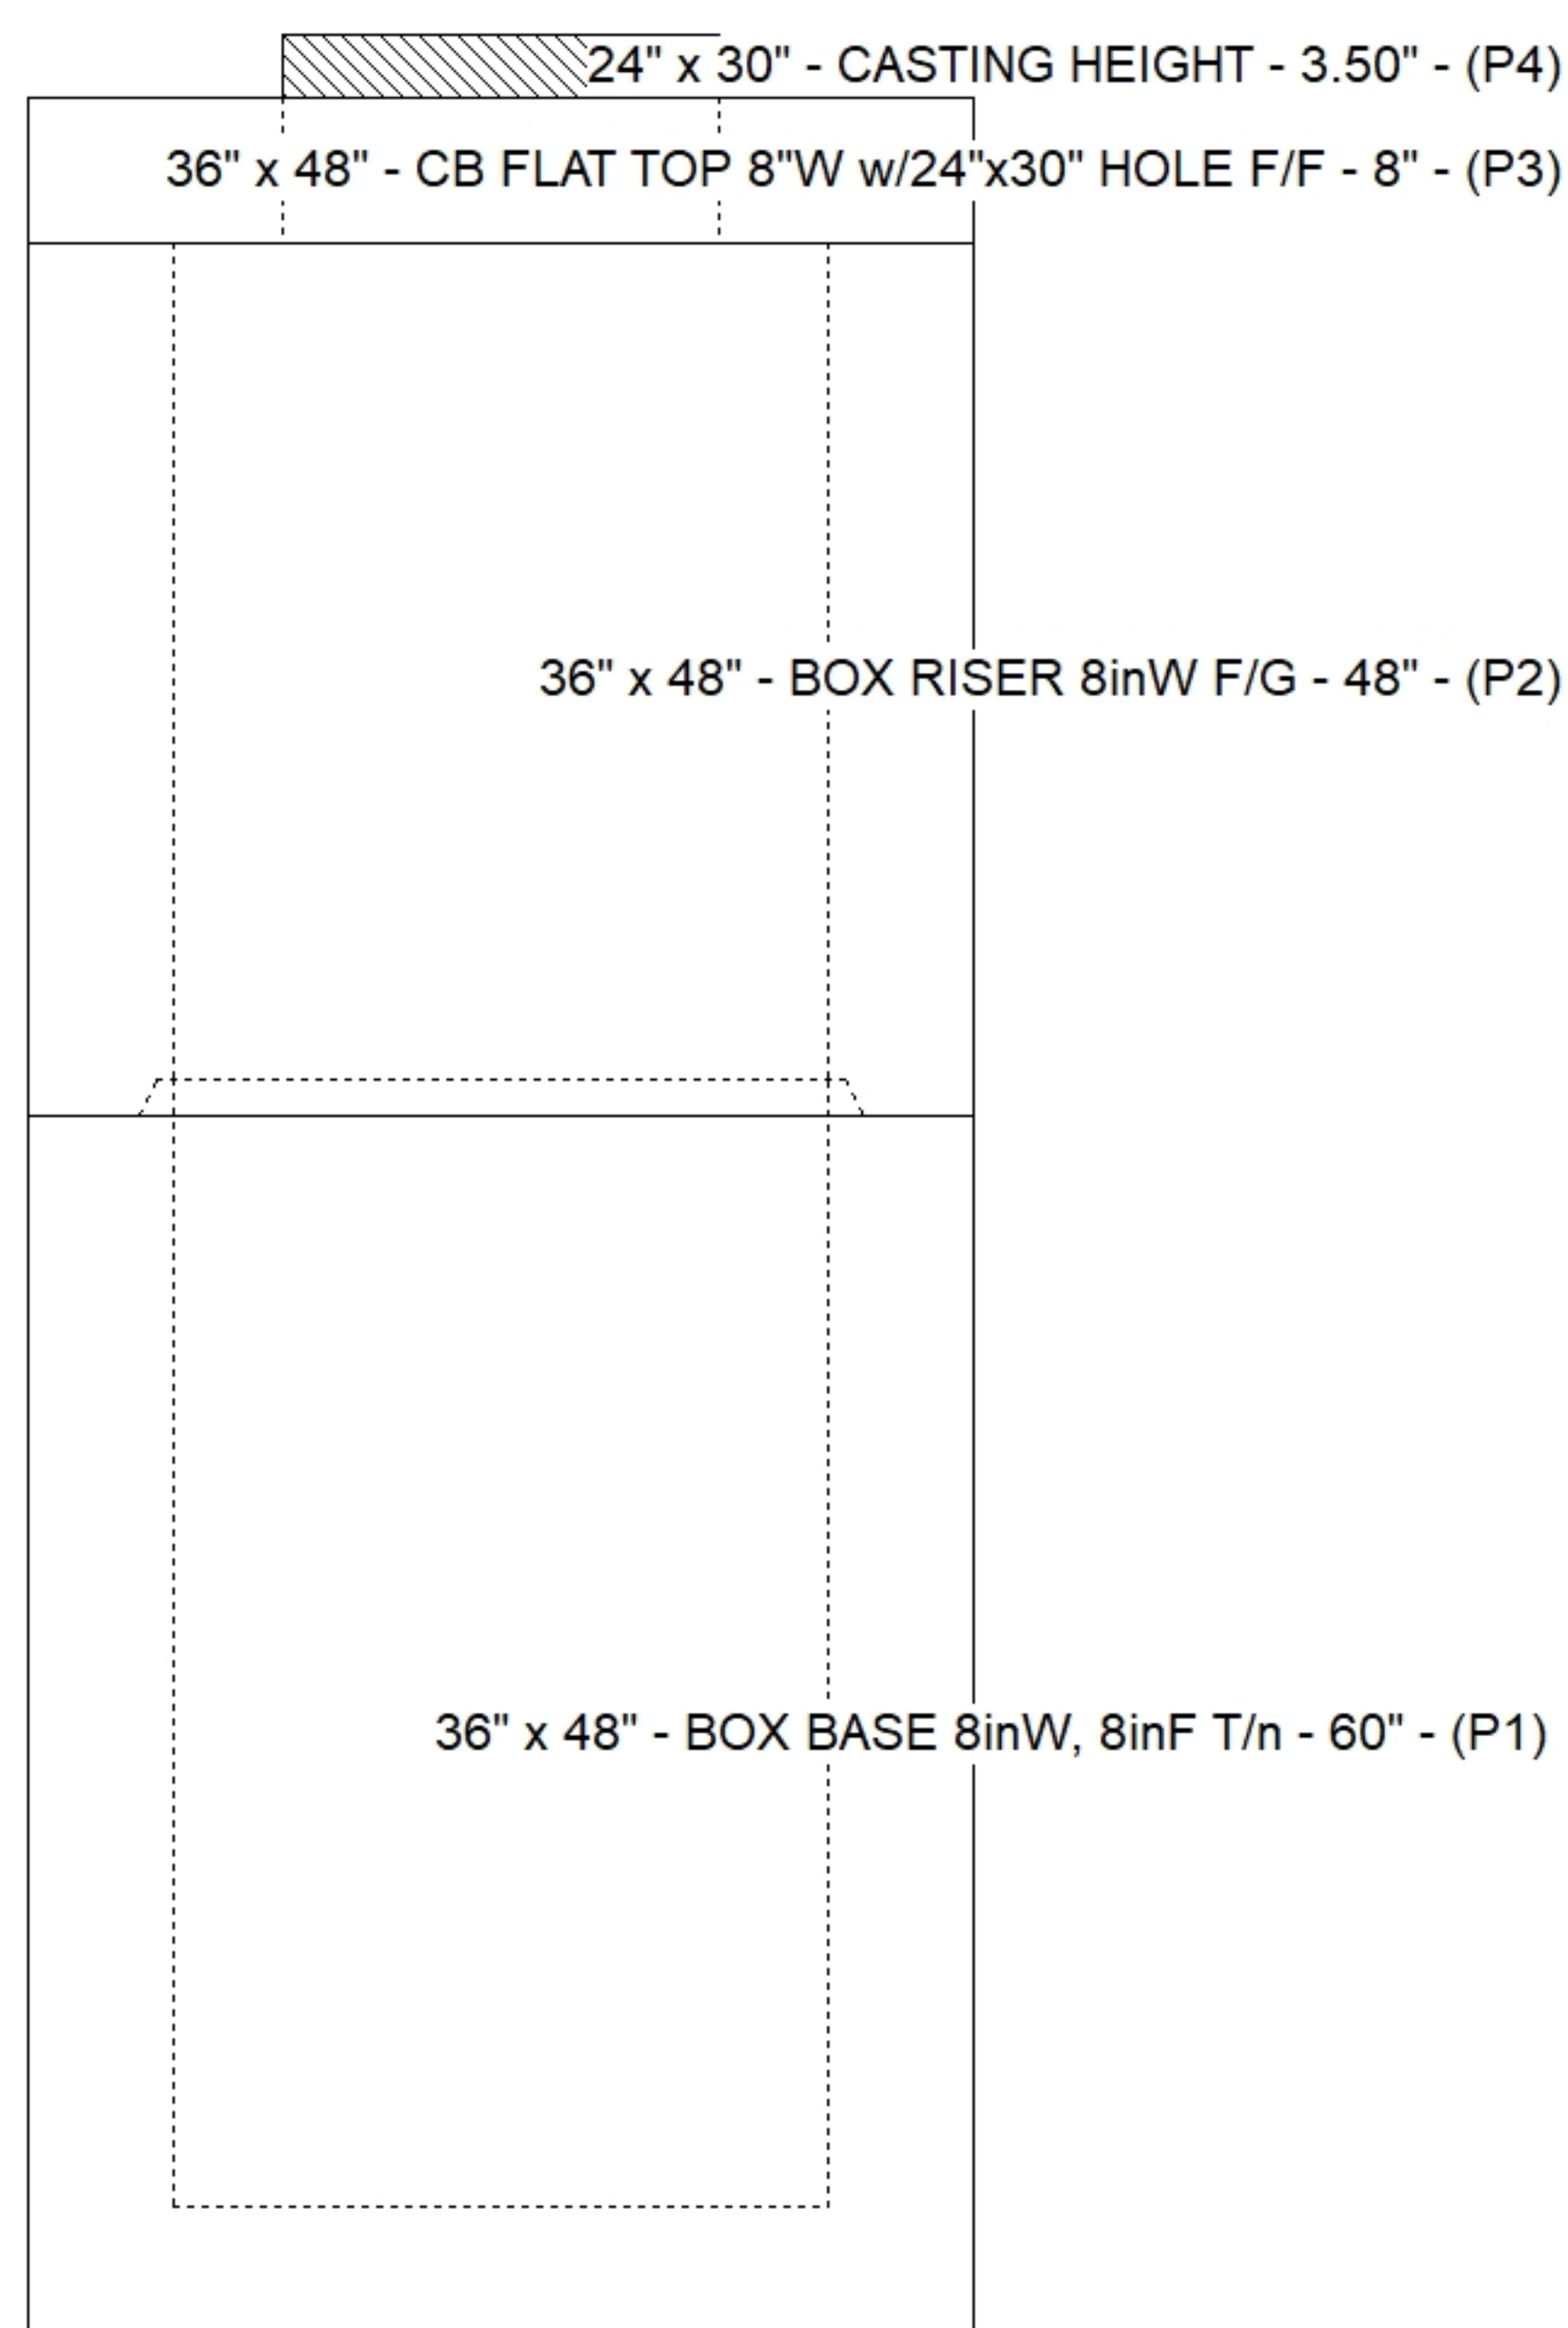

Default - Interior Dimensions

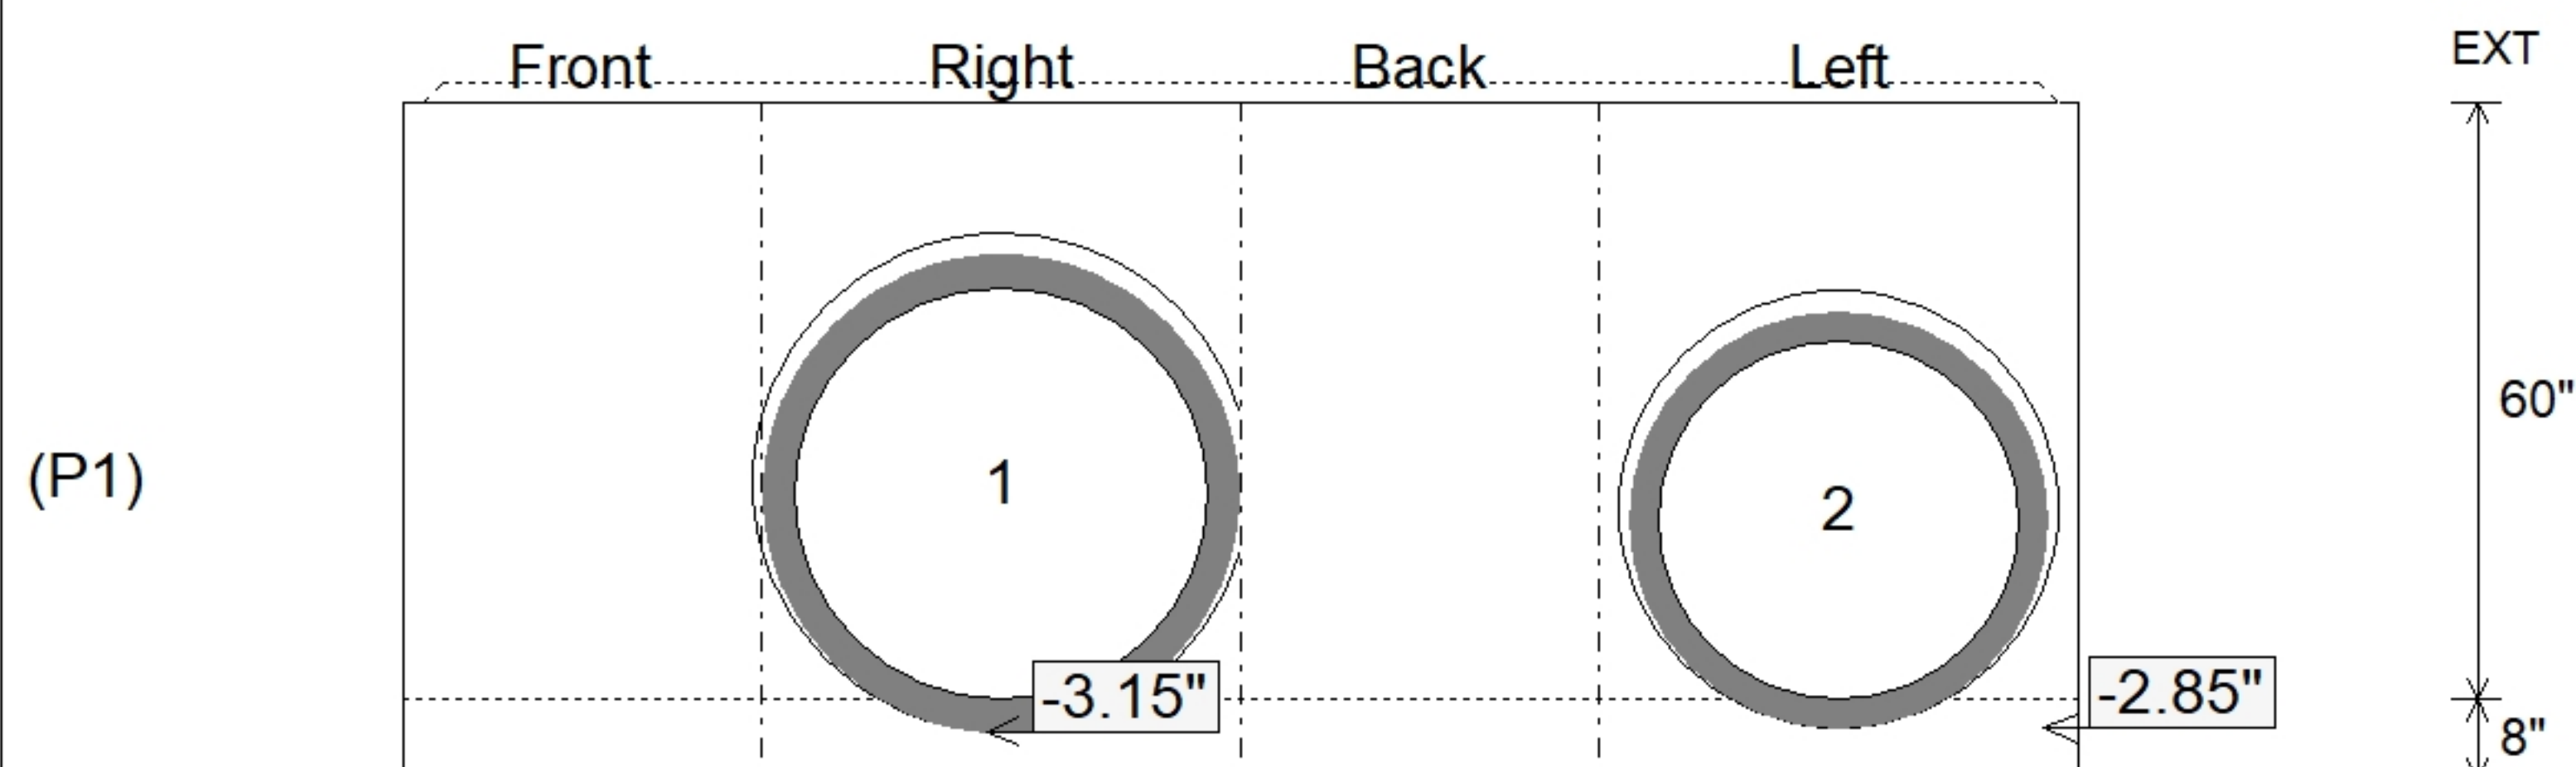

SUBMITTAL
APPROVED BY:
