

Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam



Size: 60"

Rim to Invert: 7.03'

Floor Height: 8"

Slack: 0.86"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.


- P3) 24" x 30" - CASTING HEIGHT - 3.50"
- P2) 60" - MH FLAT TOP w/24"x30" Hole F/G - 13"
- P1) 60" - MH BASE Custom Ht T/n - 67"
- 1) CASTING - HOE KY-460-11 F/G (DBI 11)
- 1) 60" - Conseal CS-102 1.00"
- 1) 24" x 30" - Conseal CS-102 1.00"
- 1) Hole - 44
- 1) Hole - 38
- 6) MH Step ML-10-TDS-NCR - 10"

0 lb
2668 lb
8276 lb
421 lb
0 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 11365 lb

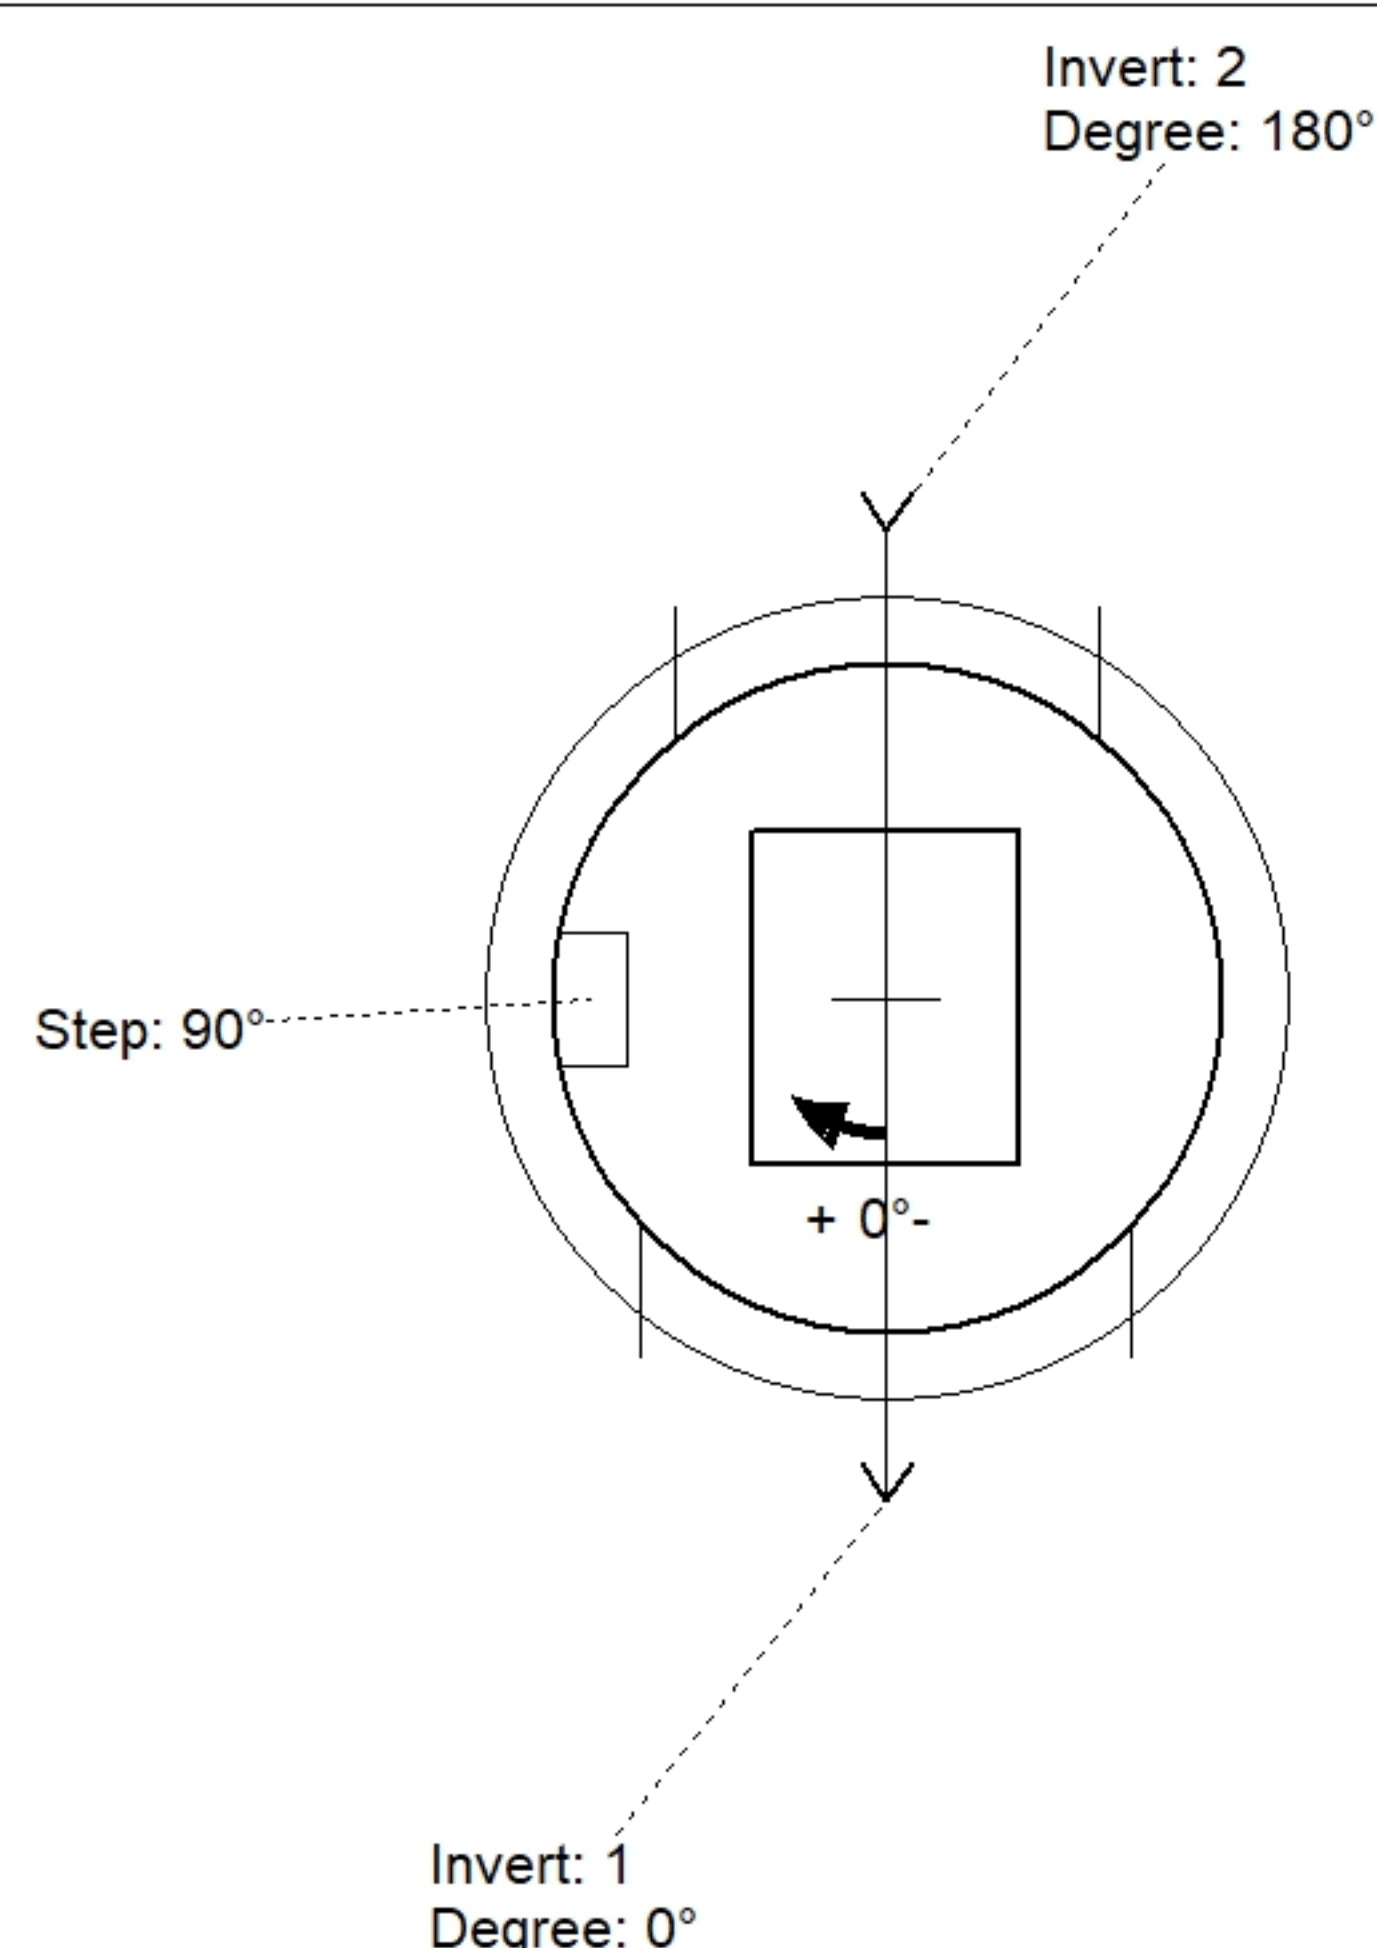

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	591'							
Reducer								
Invert 1	583.97'	0°	36" HDPE	41.7"	44"	Hole 44	-2.85"	P1
Invert 2	583.97'	180°	30" HDPE	35.1"	38"	Hole 38	-2.55"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

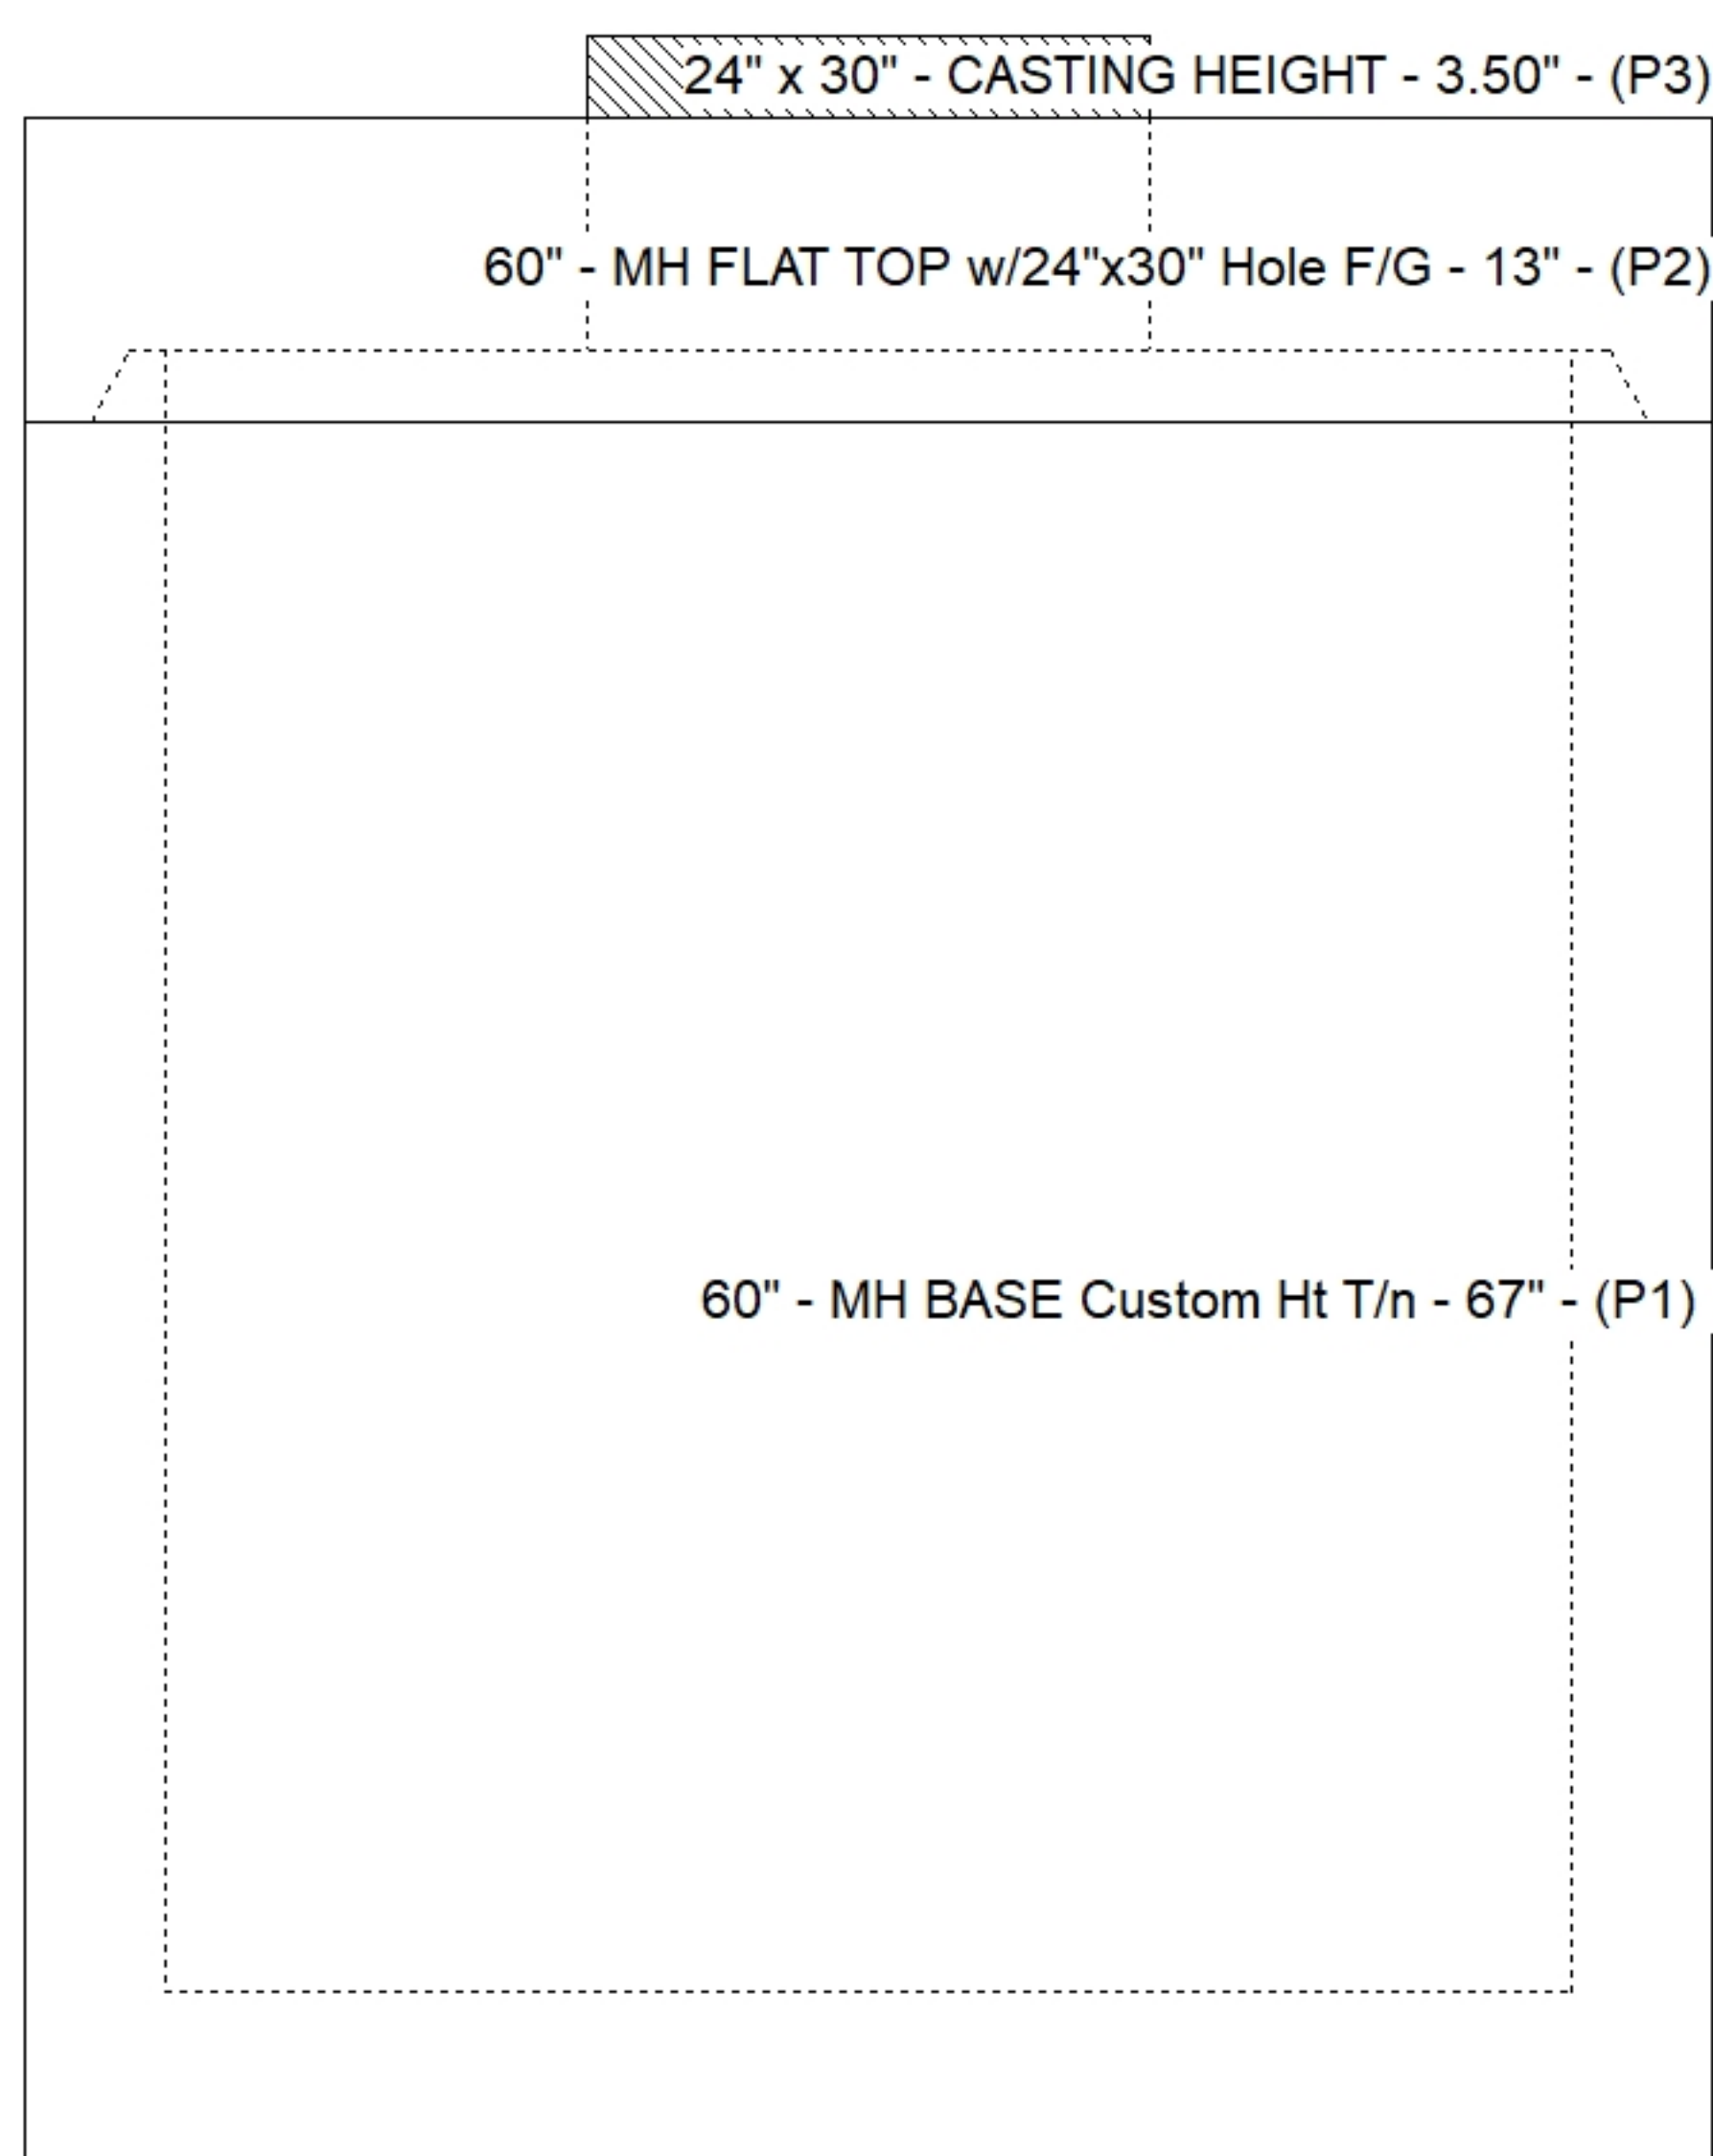

Default - Interior Dimensions

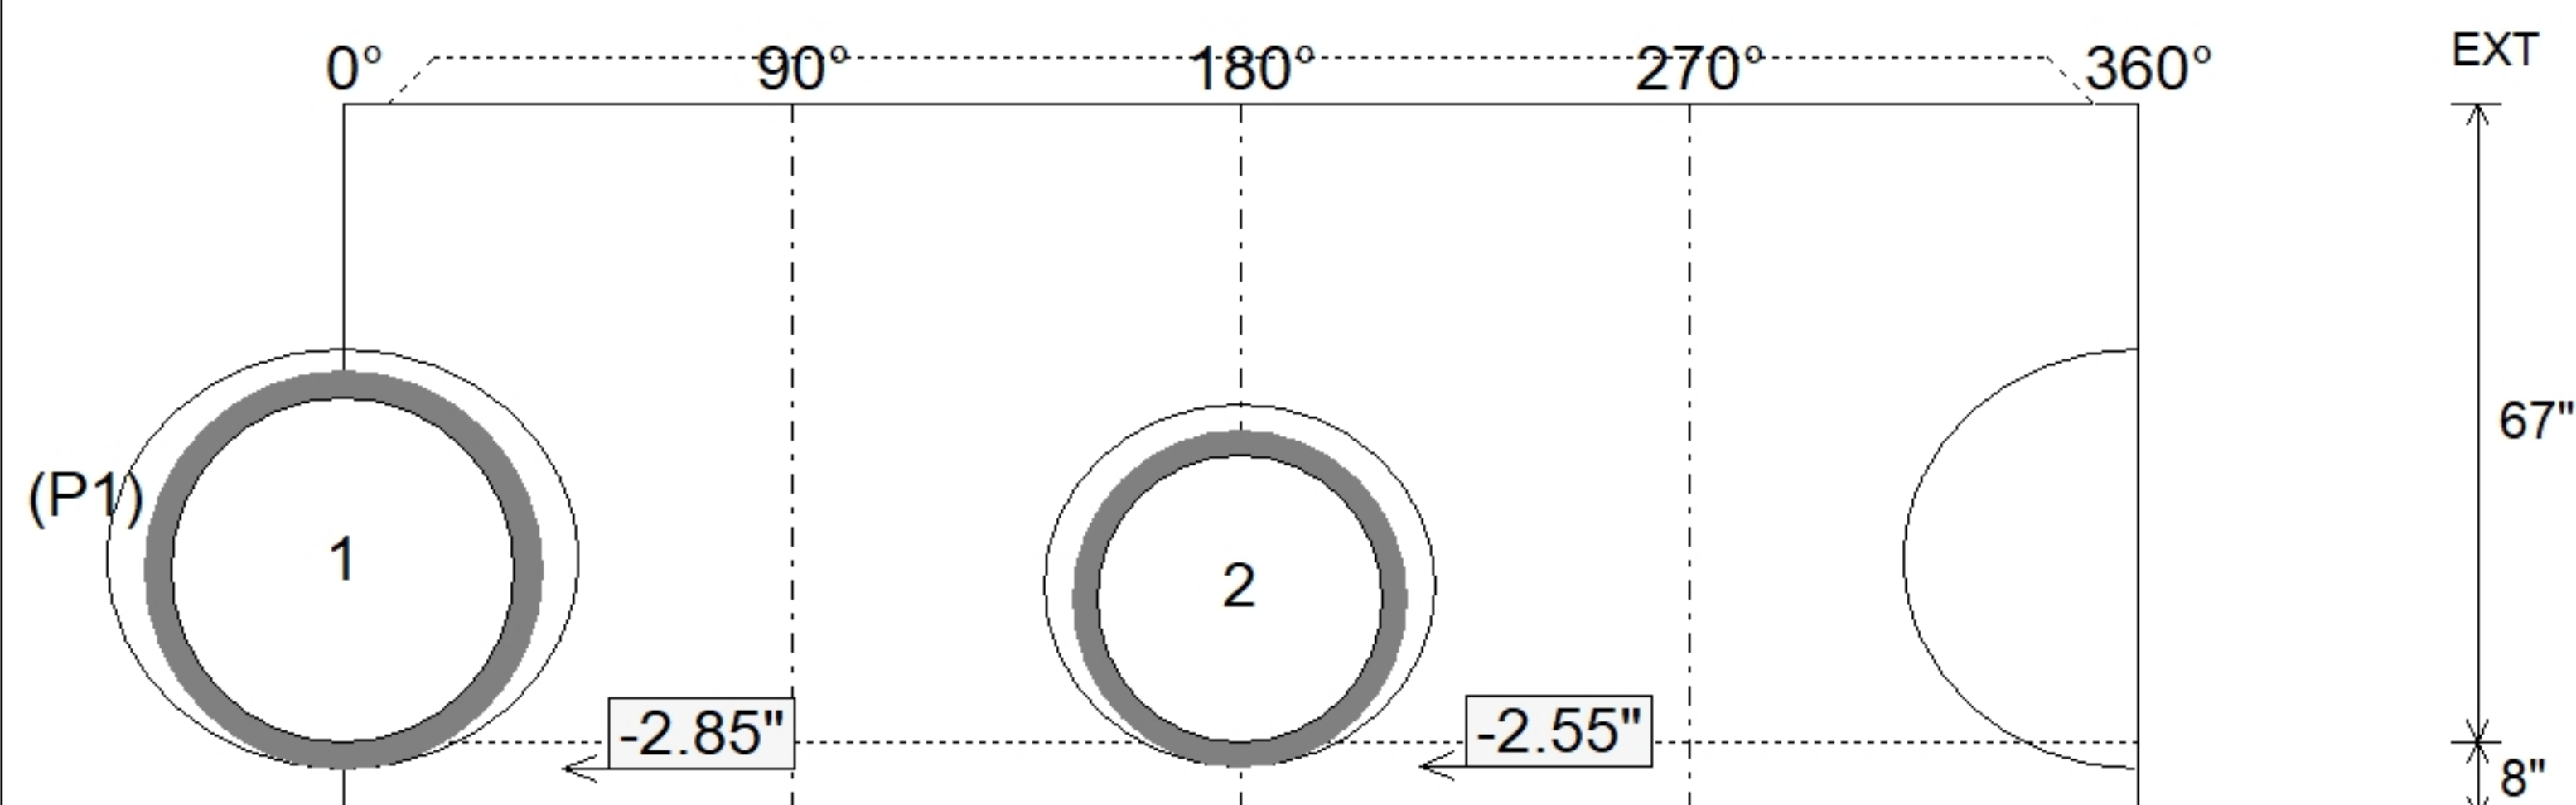

Submittal Drawing
8/11/2026 9:13:02 AM

SUBMITTAL
APPROVED BY:
