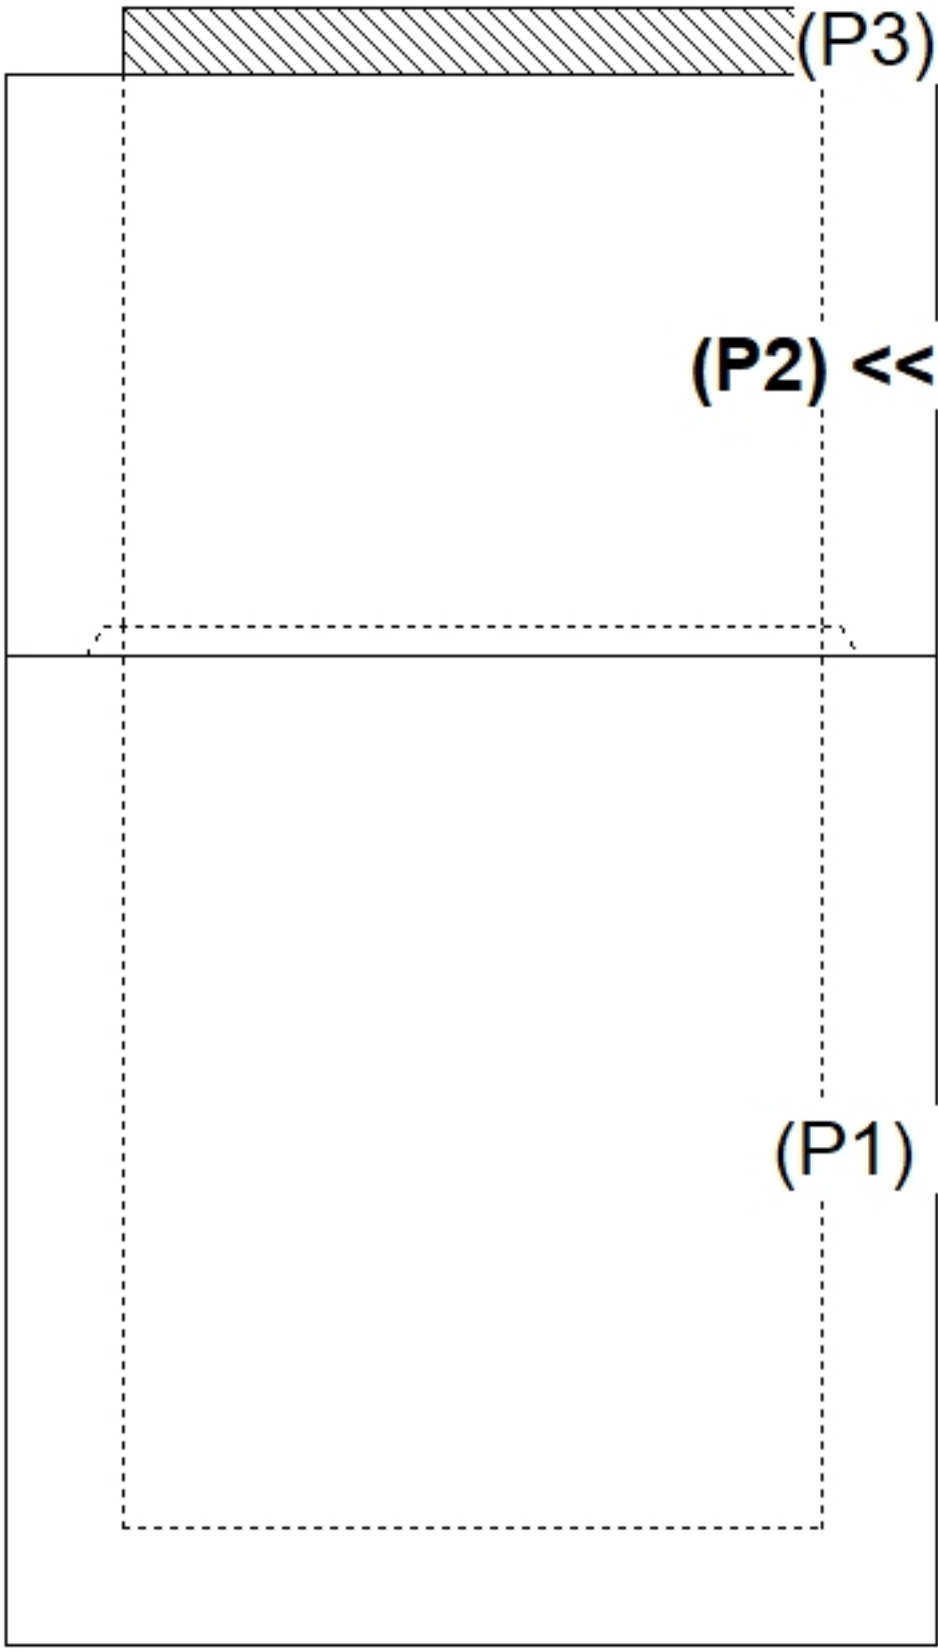
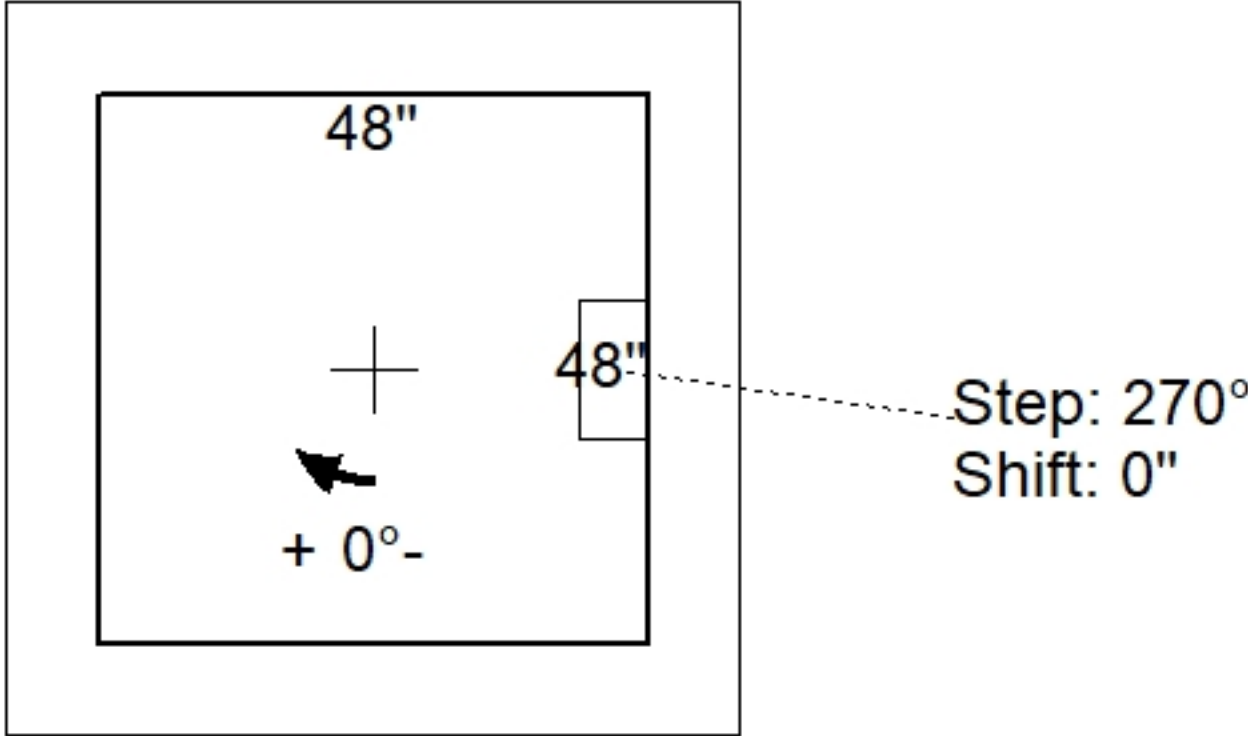



Job Name: 26-1000P2 Clark Distributing New HQ - Site Structures					Plant: Beaver Dam		Tech: S. Felletter				
Job Location: Bowling Green, KY					8/11/2026 9:22:27 AM		PC: M. Sullivan				
Contractor: Scotty's Contracting & Stone, LLC											
Structure ID: DBI-3											
P2		BX4848-08RVF		BOX RISER 8inW, Variable Ht F/G							
P3) 48" x 48" - CASTING HEIGHT - 4.5" P2) 48" x 48" - BOX RISER 8inW, Variable Ht F/G - 40" P1) 48" x 48" - BOX BASE 8inW, 8inF T/n - 60" 1) CASTING - HOE 918 F/G 1) Hole - 44 1) Hole - 38 8) MH Step ML-10-TDS-NCR - 10"					0 lb 6015 lb 9924 lb 228 lb 0 lb 0 lb 0 lb ----- Structure Total: 16167 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE 918 F/G). . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - WALLS/FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 589.54' Rim to Invert: 8.77' Slack: 0.74' Sump: 0" Step Position: 270											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (┘)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
(P2)										EXT 40"	
Coating (Int):				Seam Up: Flat		Wall Thickness: 8"		Height (Int): 40"		Weight (Net): 6015 lb	
Coating (Ext):				Seam Dn: Groove		Floor Height: 0"		Height (Ext): 40"		Volume (Net): 1.54cu.yd	
