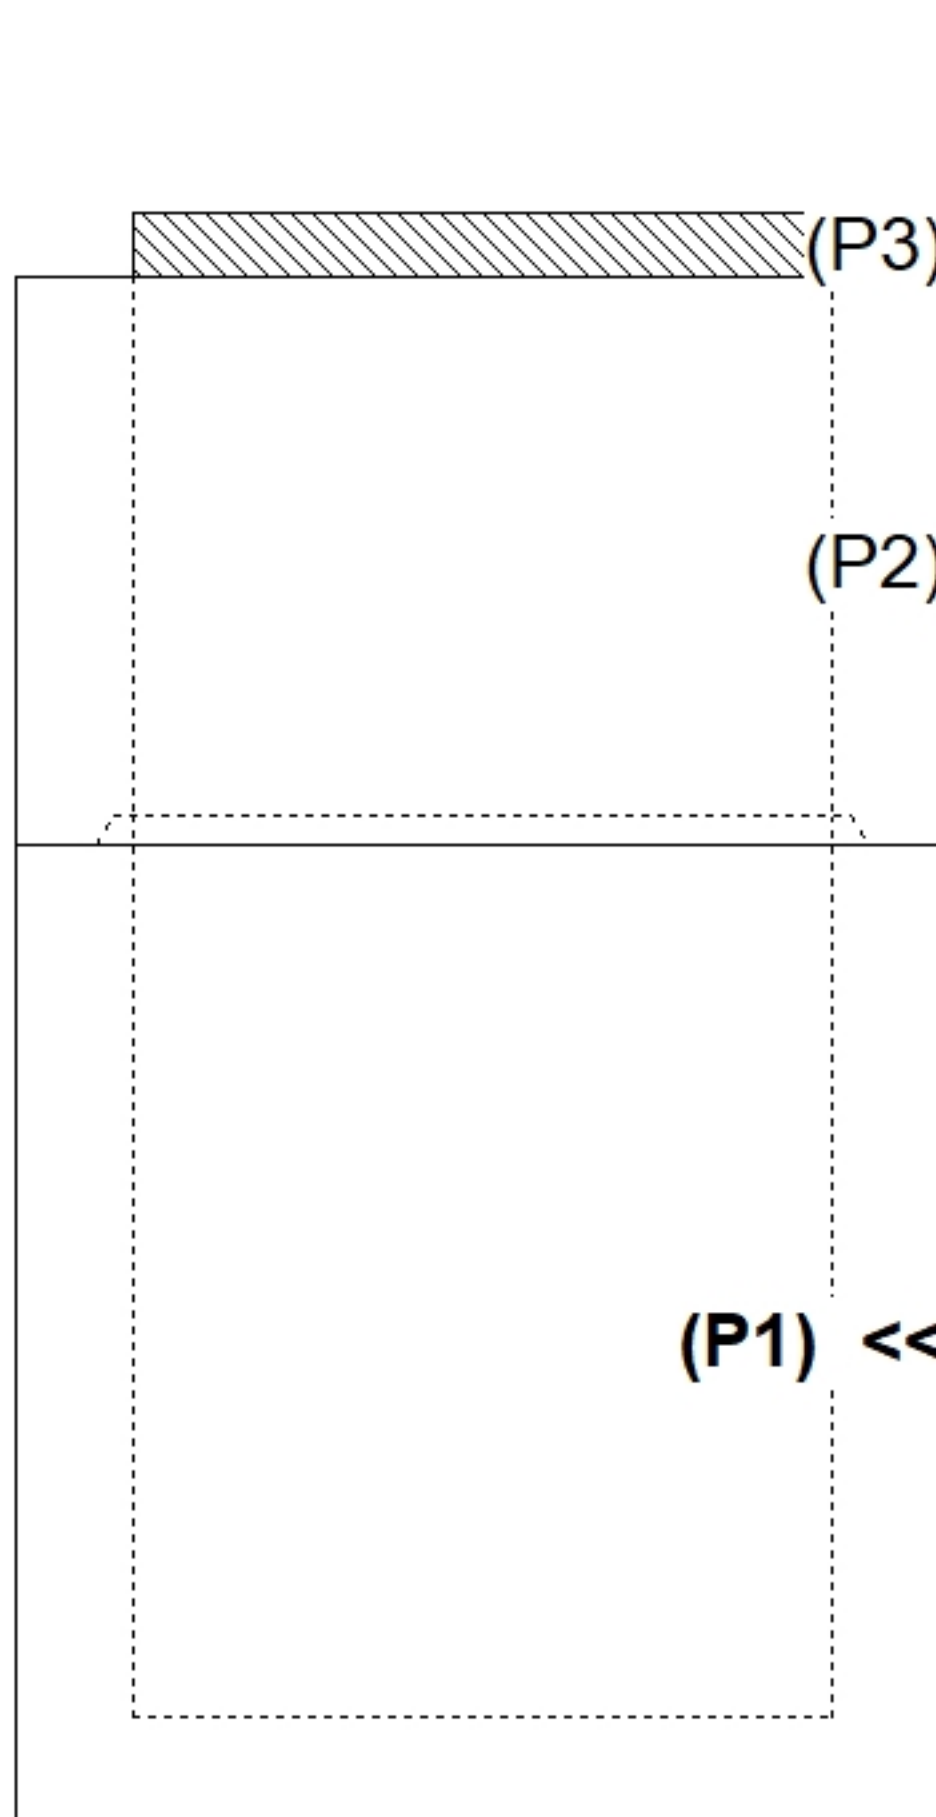
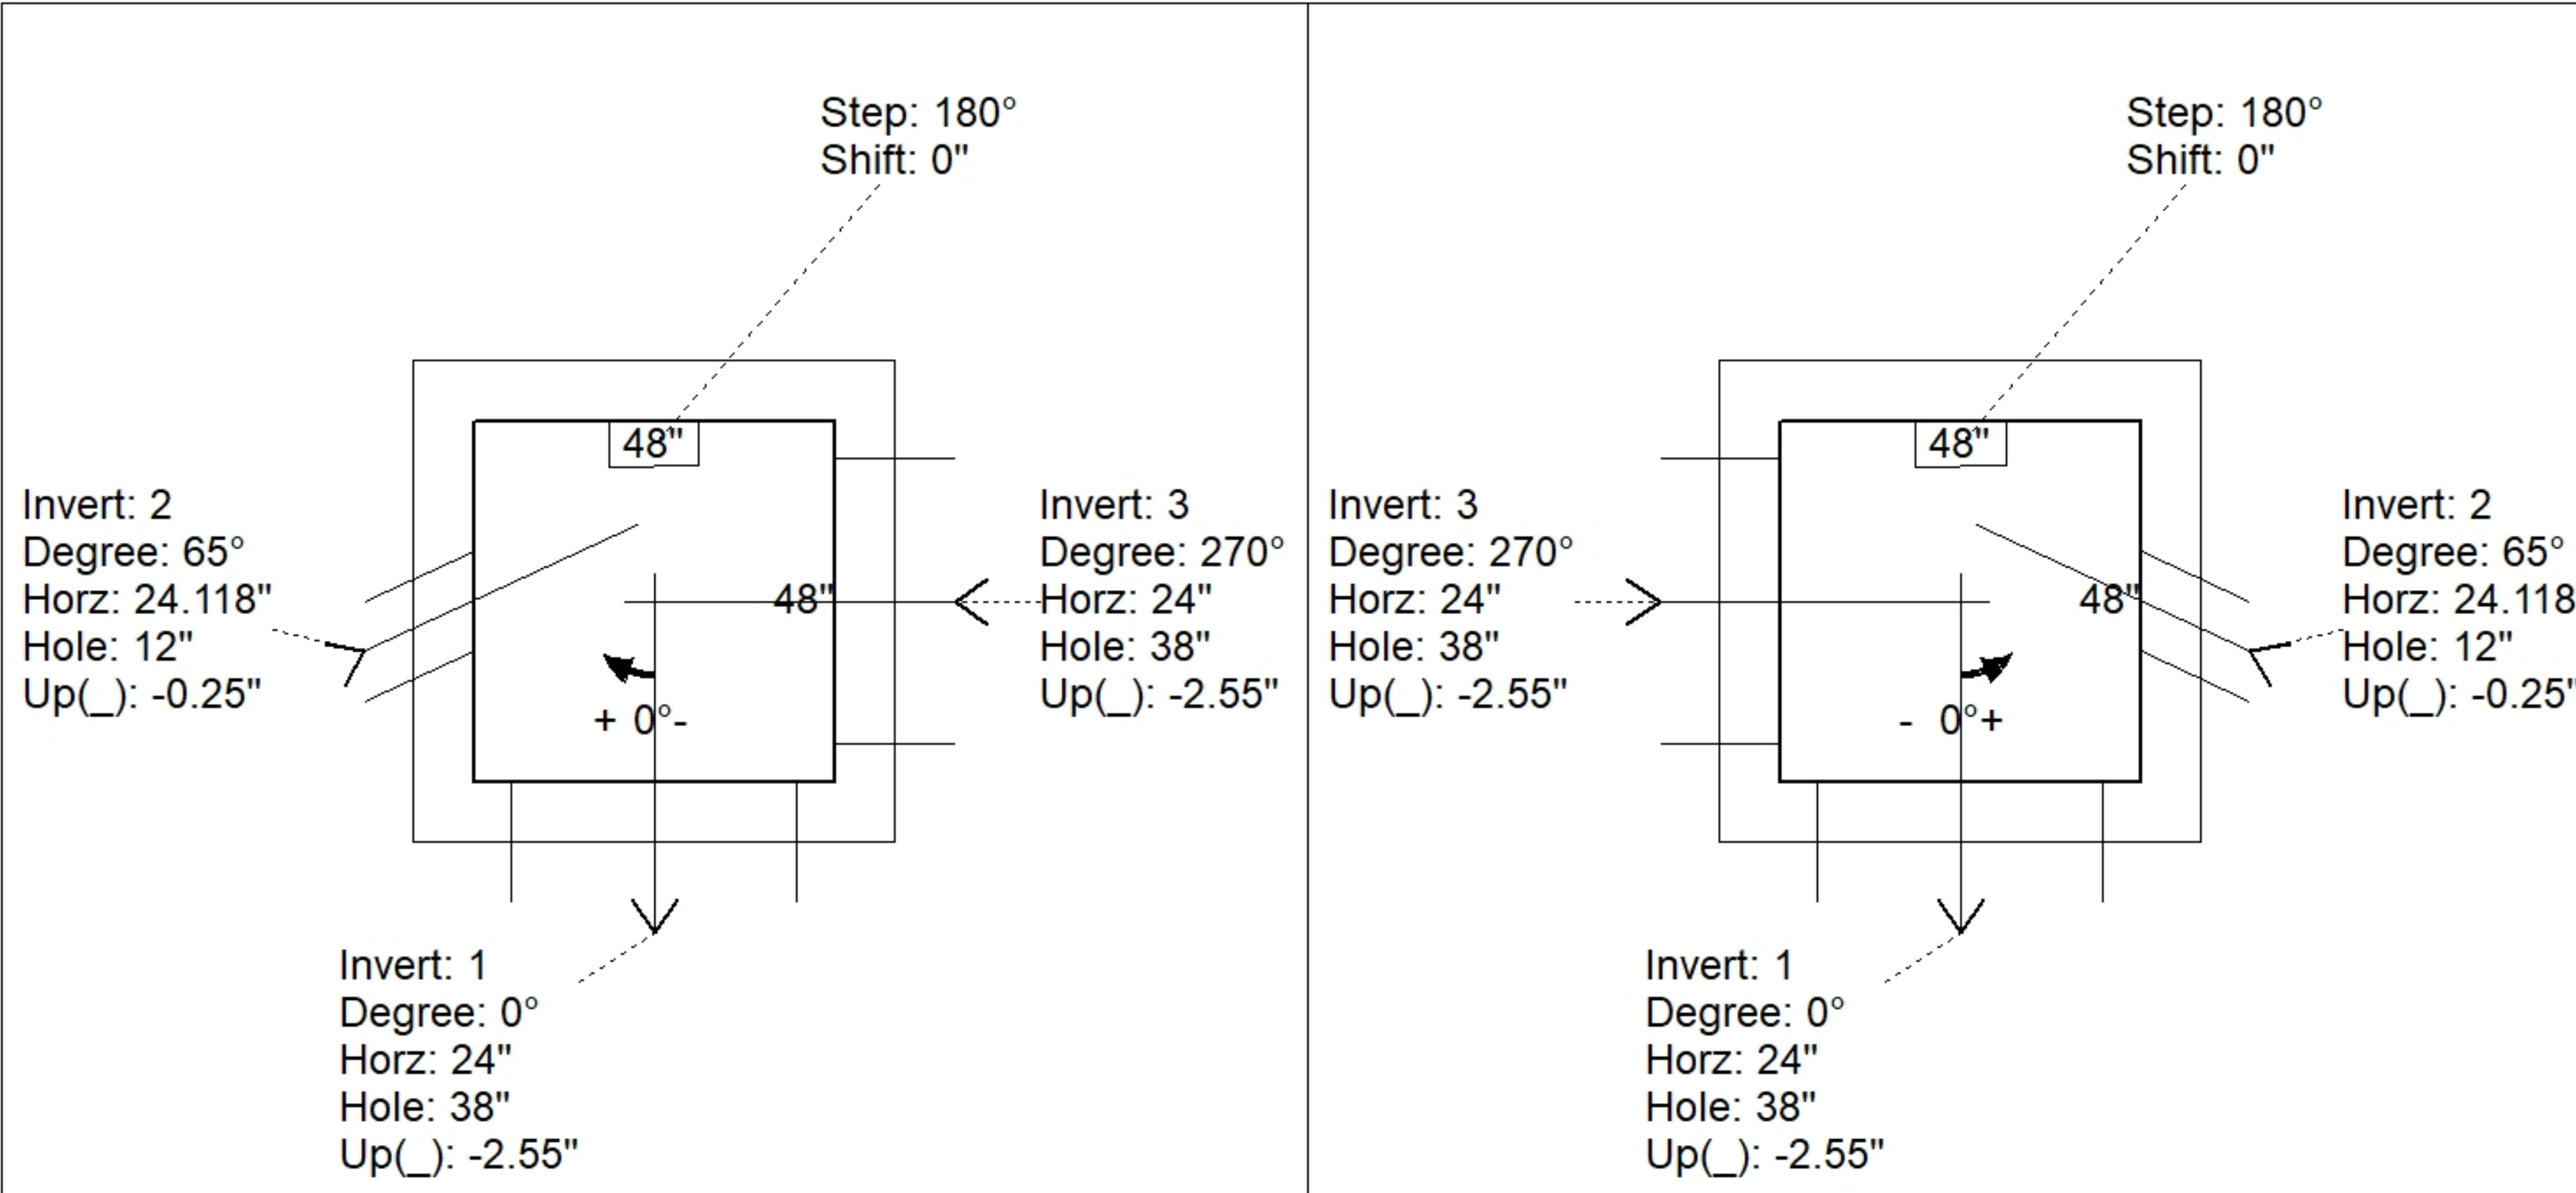
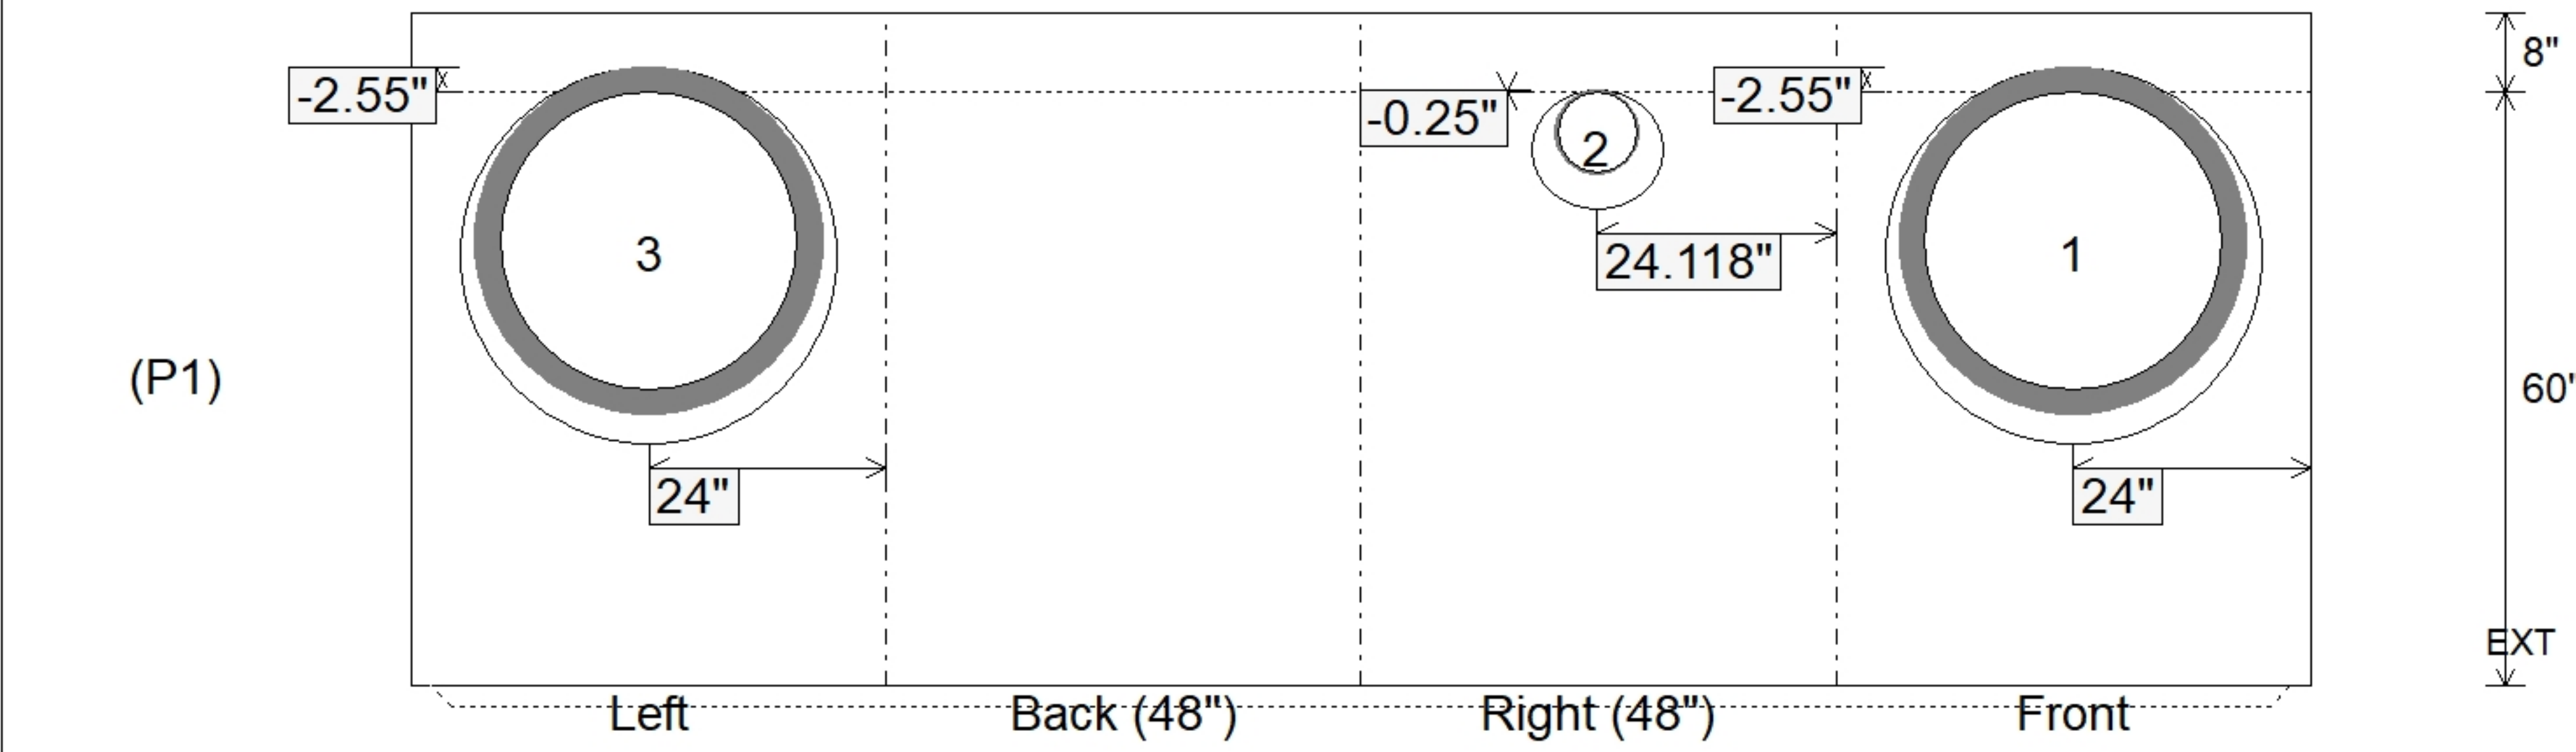


Job Name: 26-1000P2 Clark Distributing New HQ - Site Structures					Plant: Beaver Dam		Tech: S. Felletter			
Job Location: Bowling Green, KY					8/11/2026 9:19:03 AM		PC: M. Sullivan			
Contractor: Scotty's Contracting & Stone, LLC										
Structure ID: DBI-4										
P1		BX4848-08BA60			BOX BASE 8inW, 8inF T/n					
P3) 48" x 48" - CASTING HEIGHT - 4.5" P2) 48" x 48" - BOX RISER 8inW, Variable Ht F/G - 39" P1) 48" x 48" - BOX BASE 8inW, 8inF T/n - 60" 1) CASTING - HOE 918 F/G 2) Hole - 38 1) Hole - 12 8) MH Step ML-10-TDS-NCR - 10"					0 lb 5864 lb 10165 lb 228 lb 0 lb 0 lb 0 lb ----- 16258 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE 918 F/G). . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - WALLS/FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 590.7' Rim to Invert: 8.7' Slack: 0.9" Sump: 0" Step Position: 180										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	582'	0°	32"	30" HDPE	35.1"	Hole 38	38"	38"	-2.55"	0"
Invert 2	582'	65°	28.388"	8" PVC SDR35	8.5"	Hole 12	12"	13.241"	-0.25"	10.25"
Invert 3	582'	270°	32"	30" HDPE	35.1"	Hole 38	38"	38"	-2.55"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										
RIGHT-SIDE UP VIEW (int. dimensions)					UPSIDE-DOWN VIEW (int. dimenions)					
										
INSIDE WALL DIMENSIONS										
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 60" Height (Ext): 68"		Weight (Net): 10165 lb Volume (Net): 2.6cu.yd	
