


Job Name: 26-1038 - Perryville & Junction City WW Improvements
Job Location: Danville, KY
Contractor: Connhurst, LLC

Plant: 100

5/6/2026 4:07:11 PM

Tech: Jared - A

PC: E. Bradley



Structure ID: 61038 (4)

P5 MH096LD17S


MH FLAT TOP w/42"x55" Hatch F/G

P6) 42" x 55" - HATCH (CAST FLUSH) - 3"
P5) 96" - MH FLAT TOP w/42"x55" Hatch F/G - 17"
P4) 96" - MH RISER Custom Ht T/G - 67"
P3) 96" - MH RISER T/G - 72"
P2) 96" - MH RISER T/G - 54"
P1) 96" - MH SEPARATE BASE-T EXT. 14" (142" OD) T/n - 12"
1) This Structure Includes a Cast-in Item - 42" x 55" Hatch (Supplied by Others)
4) JOINT WRAP - 12" WD x 096" MAC WRAP
4) 96" - Conseal CS-231 1.00" (Double)
3) PSX - 8QRS-S NYLO
1) PSX - 12-08 NYLO


0 lb
8820 lb
16574 lb
17851 lb
13452 lb
19580 lb
0 lb
0 lb
0 lb
20 lb
8 lb
Structure Total: 76305 lb

Structure Notes:


- PER ASTM C-478 SPECIFICATIONS
- CONCRETE: 4,500 PSI AT 28 DAYS
- REINFORCEMENT - 2" MIN. REBAR CLEARANCE (TYP):
 - TOP MAT: #4 BAR @ 12" C.C. E.W. (GRADE 60)
 - BOTTOM MAT: #5 BAR @ 10" C.C. E.W. (GRADE 60)
- 42" X 55" (36" X 54" CLEAR OPENING) HATCH SUPPLIED BY OTHERS - TO BE CAST INTO FLAT LID
- 4" VENT PIPE SUPPLIED BY OTHERS
- LIFTERS: 4 EA. 5CA14 CONAC A-ANCHORS FOR PLANT & FIELD HANDLING - INSTALLED AS SHOWN
- TOP SURFACE TO RECEIVE LIGHT BRUSH FINISH

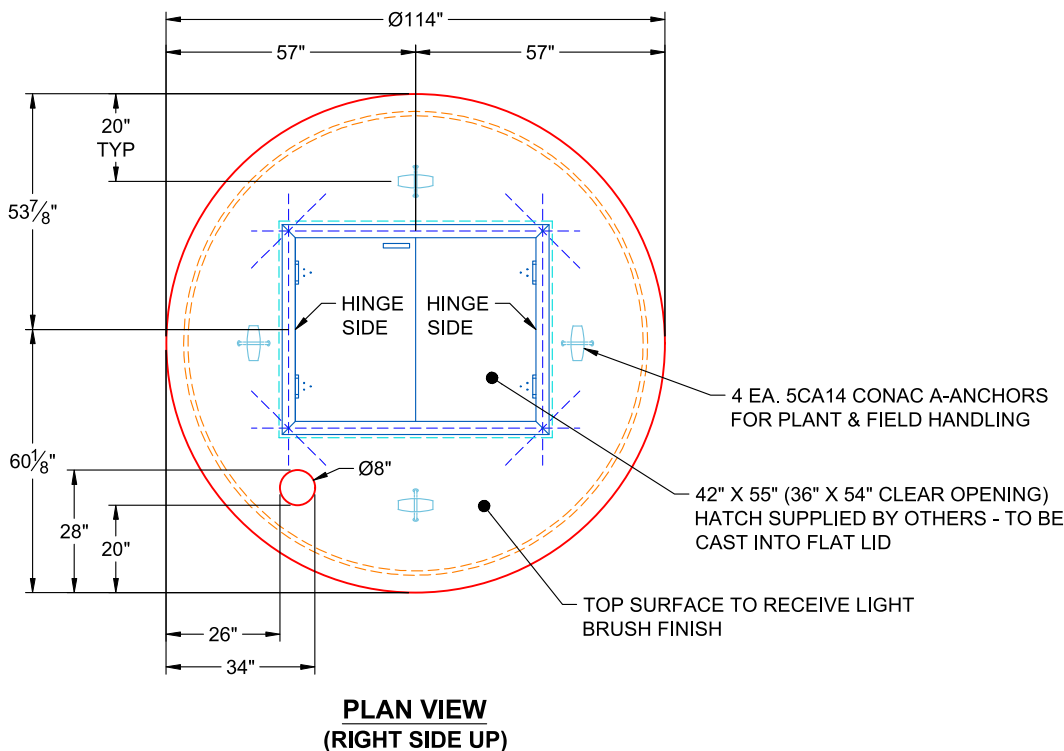

**PLAN VIEW
(RIGHT SIDE UP)**

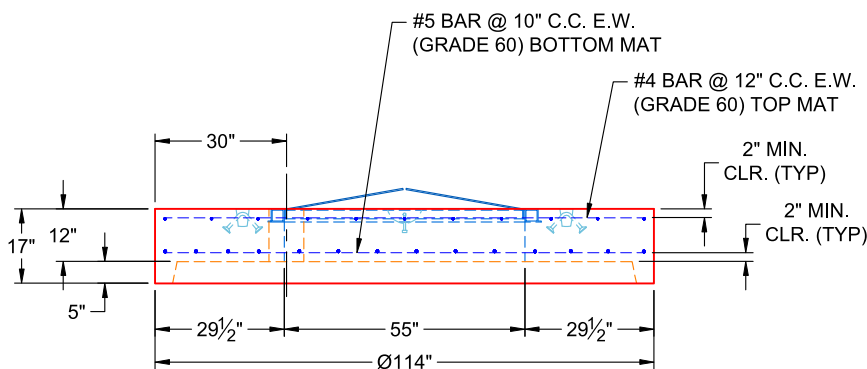

**FRONT VIEW
(RIGHT SIDE UP)**

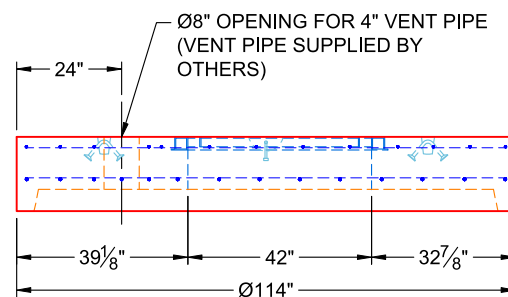

**SIDE VIEW
(RIGHT SIDE UP)**

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 9"

Height (Ext): 17"

Weight (Net): 8820 lb
Volume (Net): 2.25cu.yd

Job Number:

26-1038

Job Name:

Perryville & Junction City WW
Improvements

Structure:

61038 (4)

Note:

42" x 55" (36" x 54" Clear Opening)
Hatch Supplied By Others To Be Cast
Into Flat Lid
