

Contractor: Hayes Pipe Supply

TECH: J. Horsley

Plant: 100



Type: SAN.MH w/ConBlock-CDA Red
Size: 48"

Rim: 567.51'
Invert: 560.4'
Rim to Invert: 7.11'

Sump: 2"
Floor (Top): 560.233'
Floor Height: 6"

Floor (Bot): 559.733'
Overall Height: 7.583'
Slack: 2.32"


1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. ADMIXTURE = CONBLOCK CDA RED.
4. CASTING (JBS-1150 F/C) SUPPLIED BY CONTRACTOR).

- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P4) 24" - CASTING HEIGHT - 7"
P3) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G - 24"
P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 24"
P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 30"
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT
2) 48" - Conseal CS-102 1.00" (Double)
1) 24" - Conseal CS-102 1.00" (Double)
2) PSX - 12-08 NYLO
6) MH Step ML-10-TDS-NCR - 10"

0 lb
1297 lb
1677 lb
3330 lb
1440 lb
0 lb
0 lb
16 lb
0 lb


Structure Total: 7760 lb

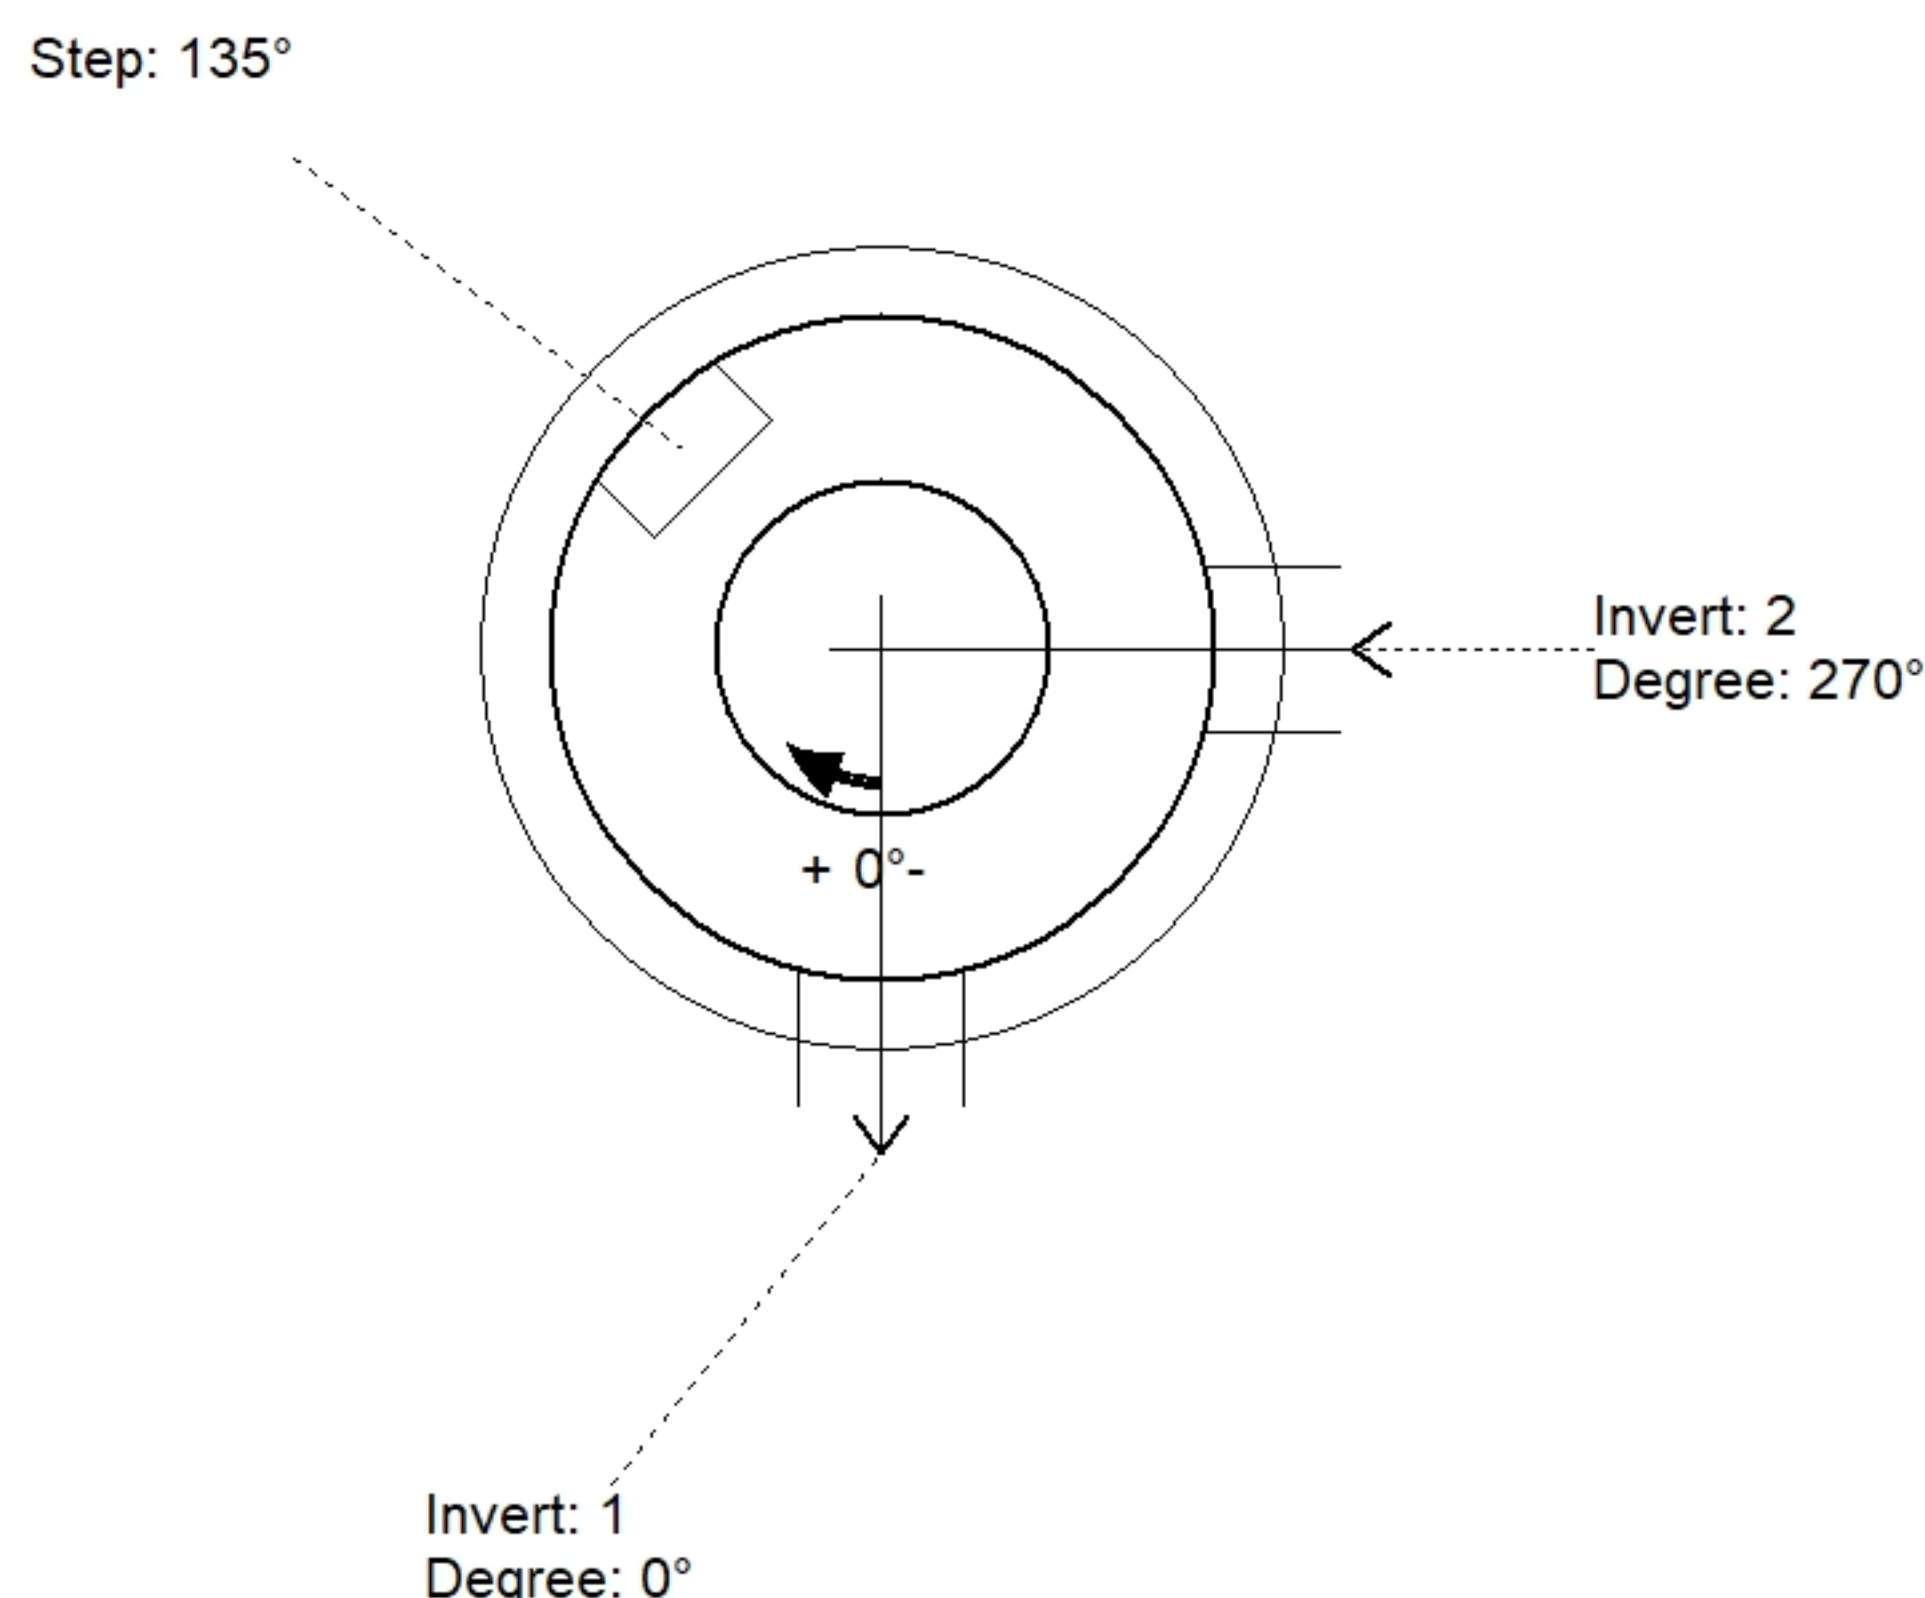

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	567.51'							
Reducer								
Invert 1	560.4'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	560.6'	270°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	2.375"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

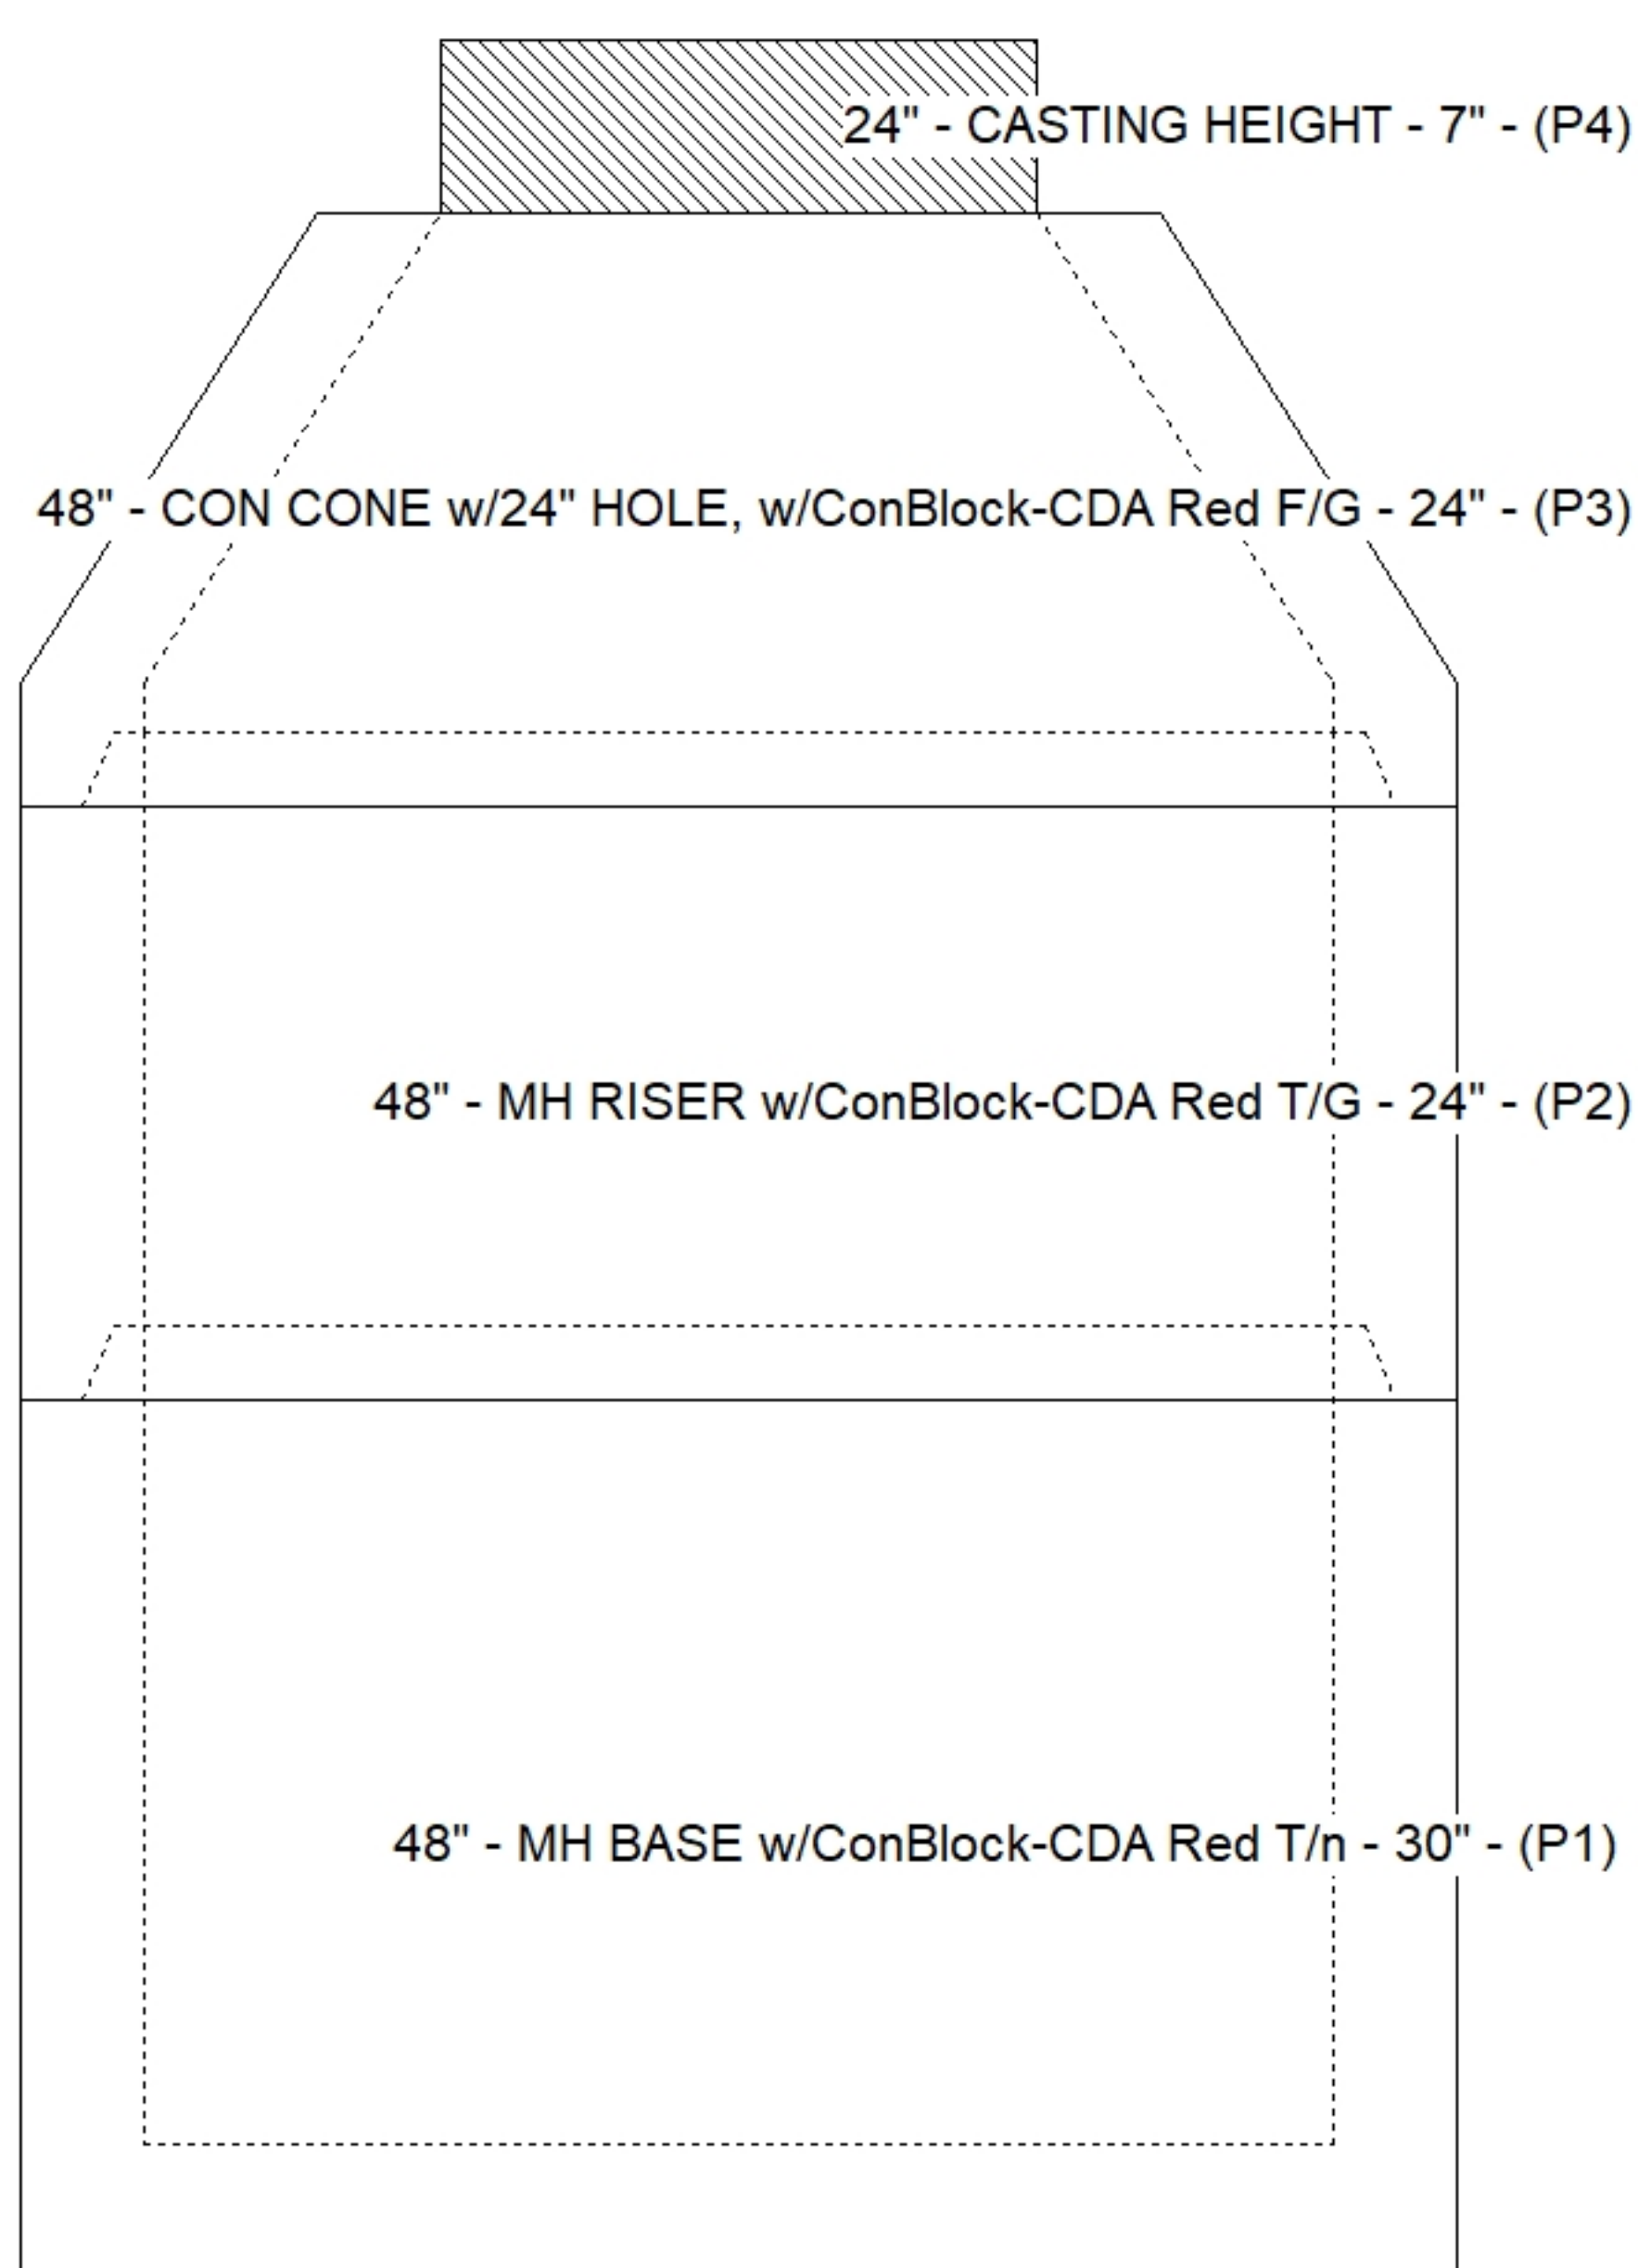

Cast (Int. Dim.) - Interior Dimensions

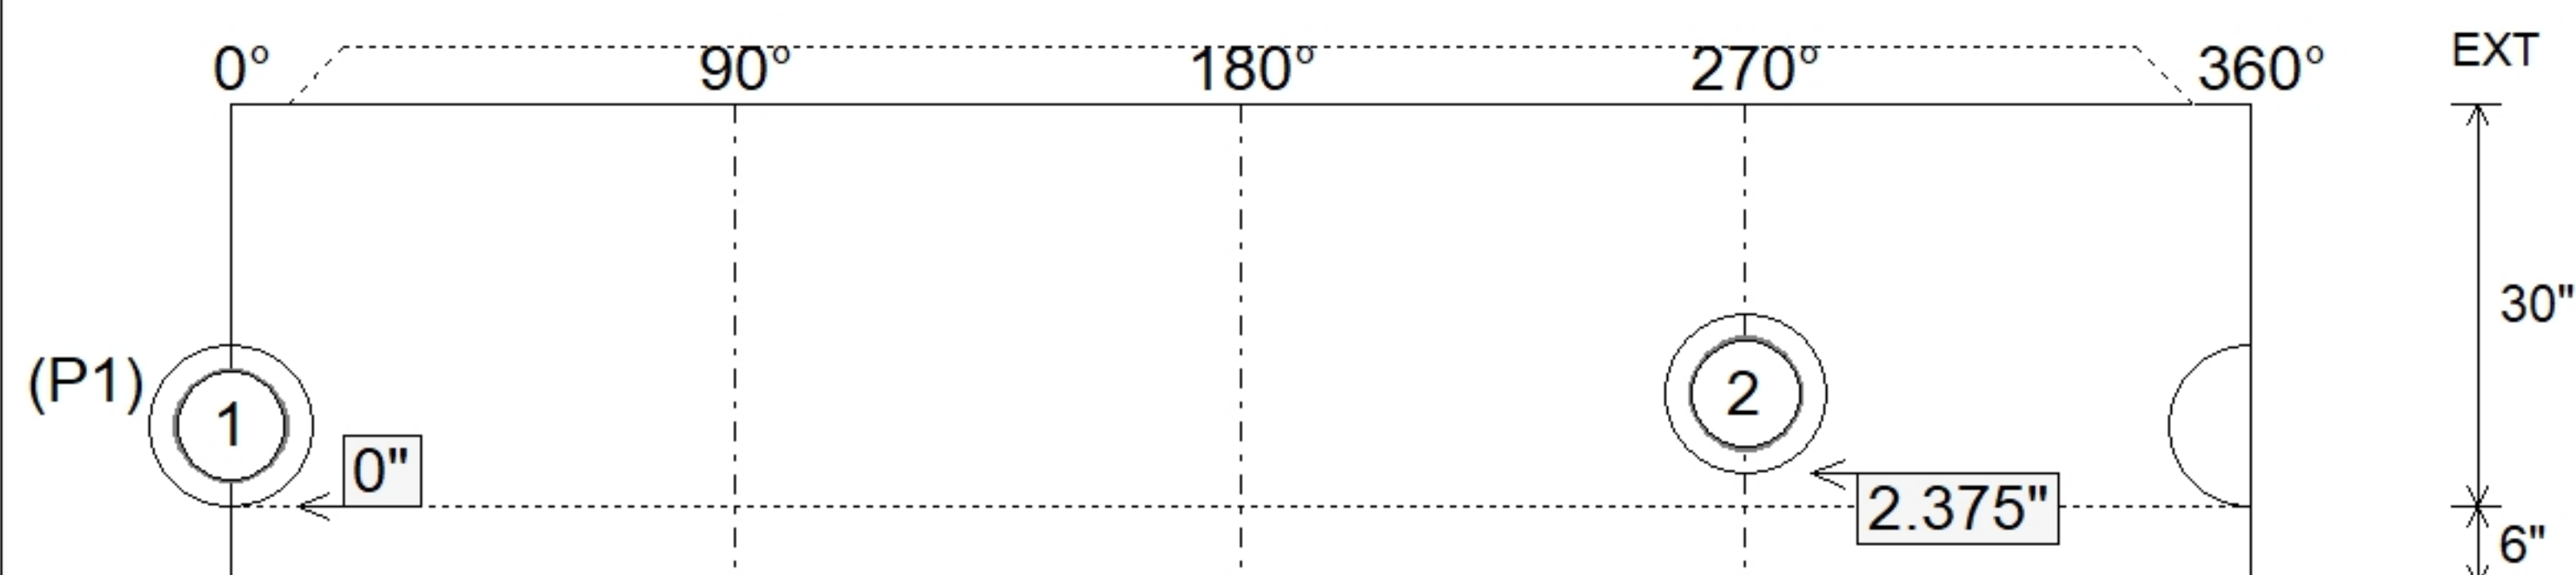

Submittal Drawing
9/8/2026 9:06:53 AM

SUBMITTAL
APPROVED BY:
