

Contractor: Connhurst, LLC

TECH: Jared - F

Plant: 100



Size: 48"


Rim to Invert: 9.81'

Floor Height: 6"


Slack: 0.72"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total: 11750 lb

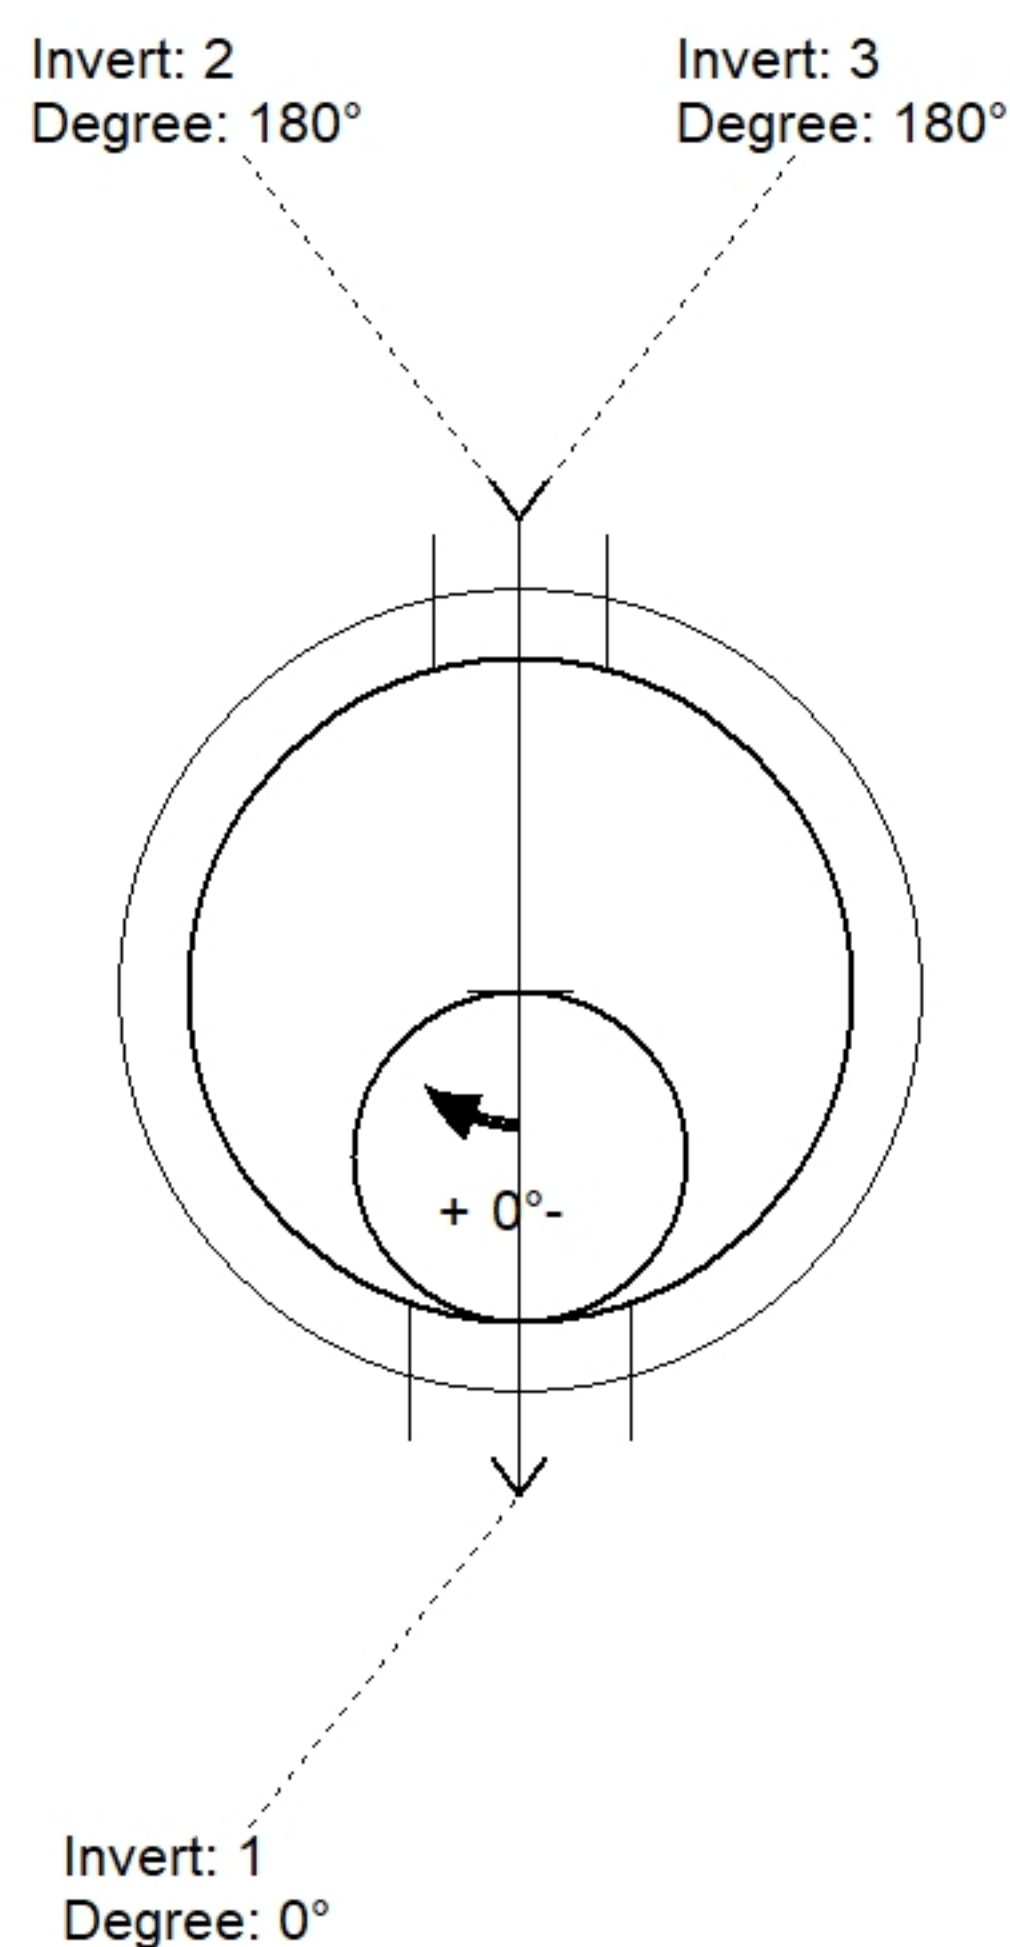

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	556.7'							
Reducer								
Invert 1	546.89'	0°	12" DI	13.2"	16"	PSX 16M DD	0.32"	P1
Invert 2	552.18'	180°	12" PVC SDR35	12.5"	12.5"	Drop Tee 12" PVC	32.98"	P2
Invert 3	546.99'	180°	12" PVC SDR35	12.5"	12.5"	Drop Elbow 12" PVC	2.95"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

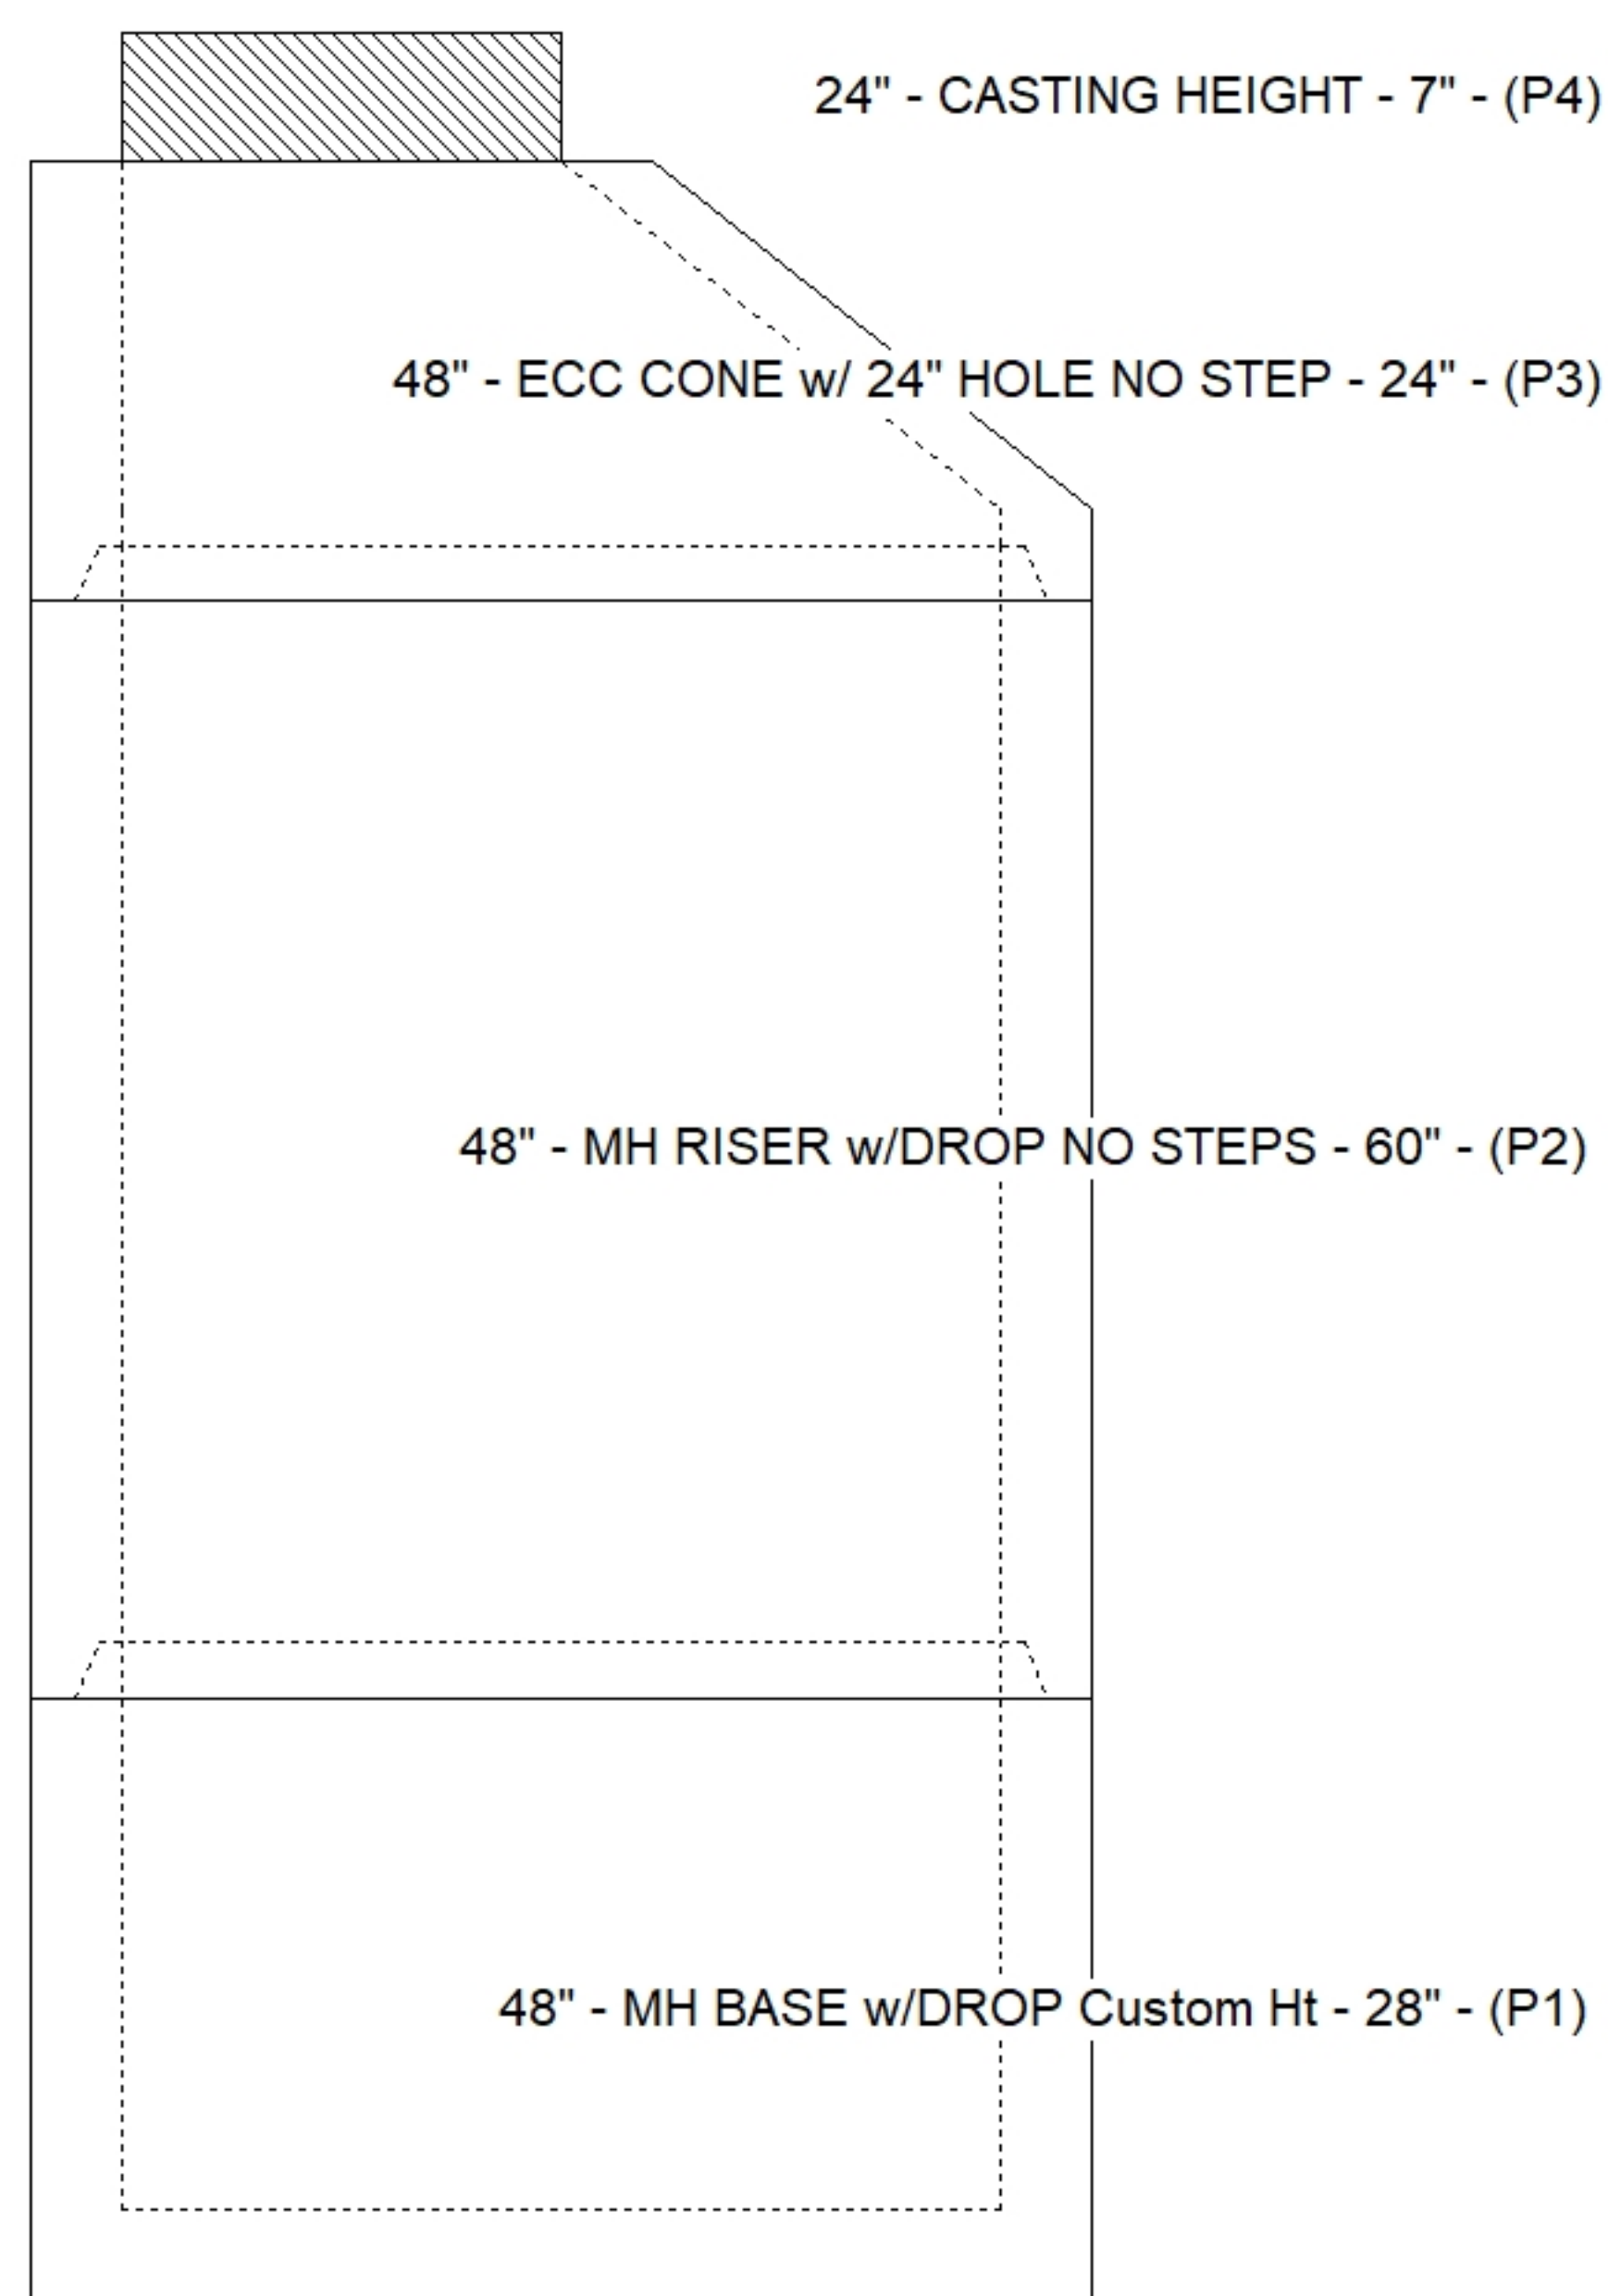

SUBMITTAL
APPROVED BY:
