

Job Name: 26-1077 - Westside Markets of Greensboro Village
Job Location: Gallatin, TN
Contractor: Cleary Construction, Inc.

PC: C. Goff
 TECH: J. Coppage - F
 Plant: 100



Structure ID: **A0**
 Spec: HEADWALLS
 Type: HW PIPE CULVERT w/Flat Bottom
 Size: 36"

Rim: 3.5'
 Invert: 3.5'
 Rim to Invert: 0'


Sump: 42"
 Floor (Top): 0'
 Floor Height: 0"

Floor (Bot): 0'
 Overall Height: 3'
 Slack: 6"

Structure Notes:



STRUCTURE SUMMARY:

P1) 36" - PIPE CULVERT HEADWALL w/Flat Bottom/Dissipators - 36" 8700 lb
 1) 36" - Conseal CS-102 1.00" (Double) 0 lb
 Structure Total: 8700 lb

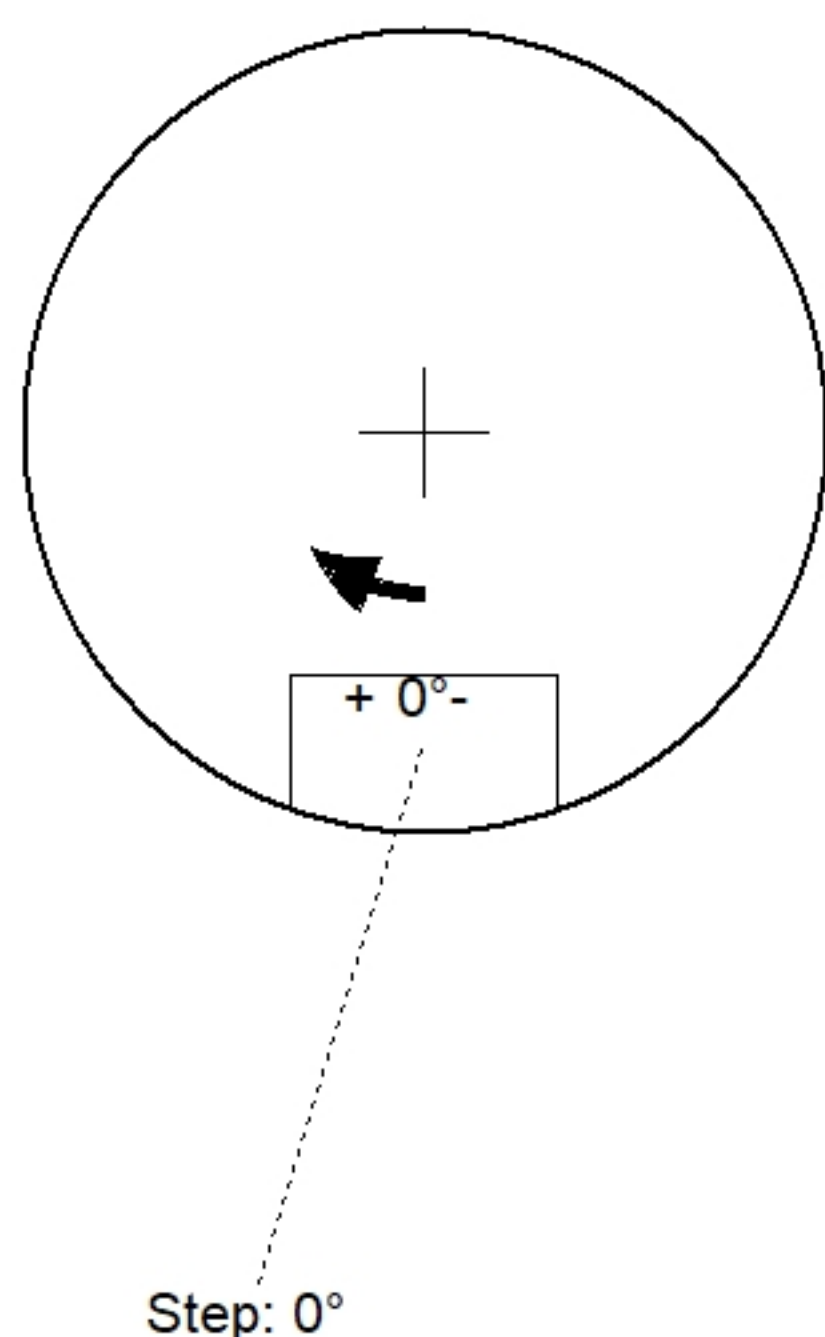

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	3.5'							
Reducer								
Invert 1								
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

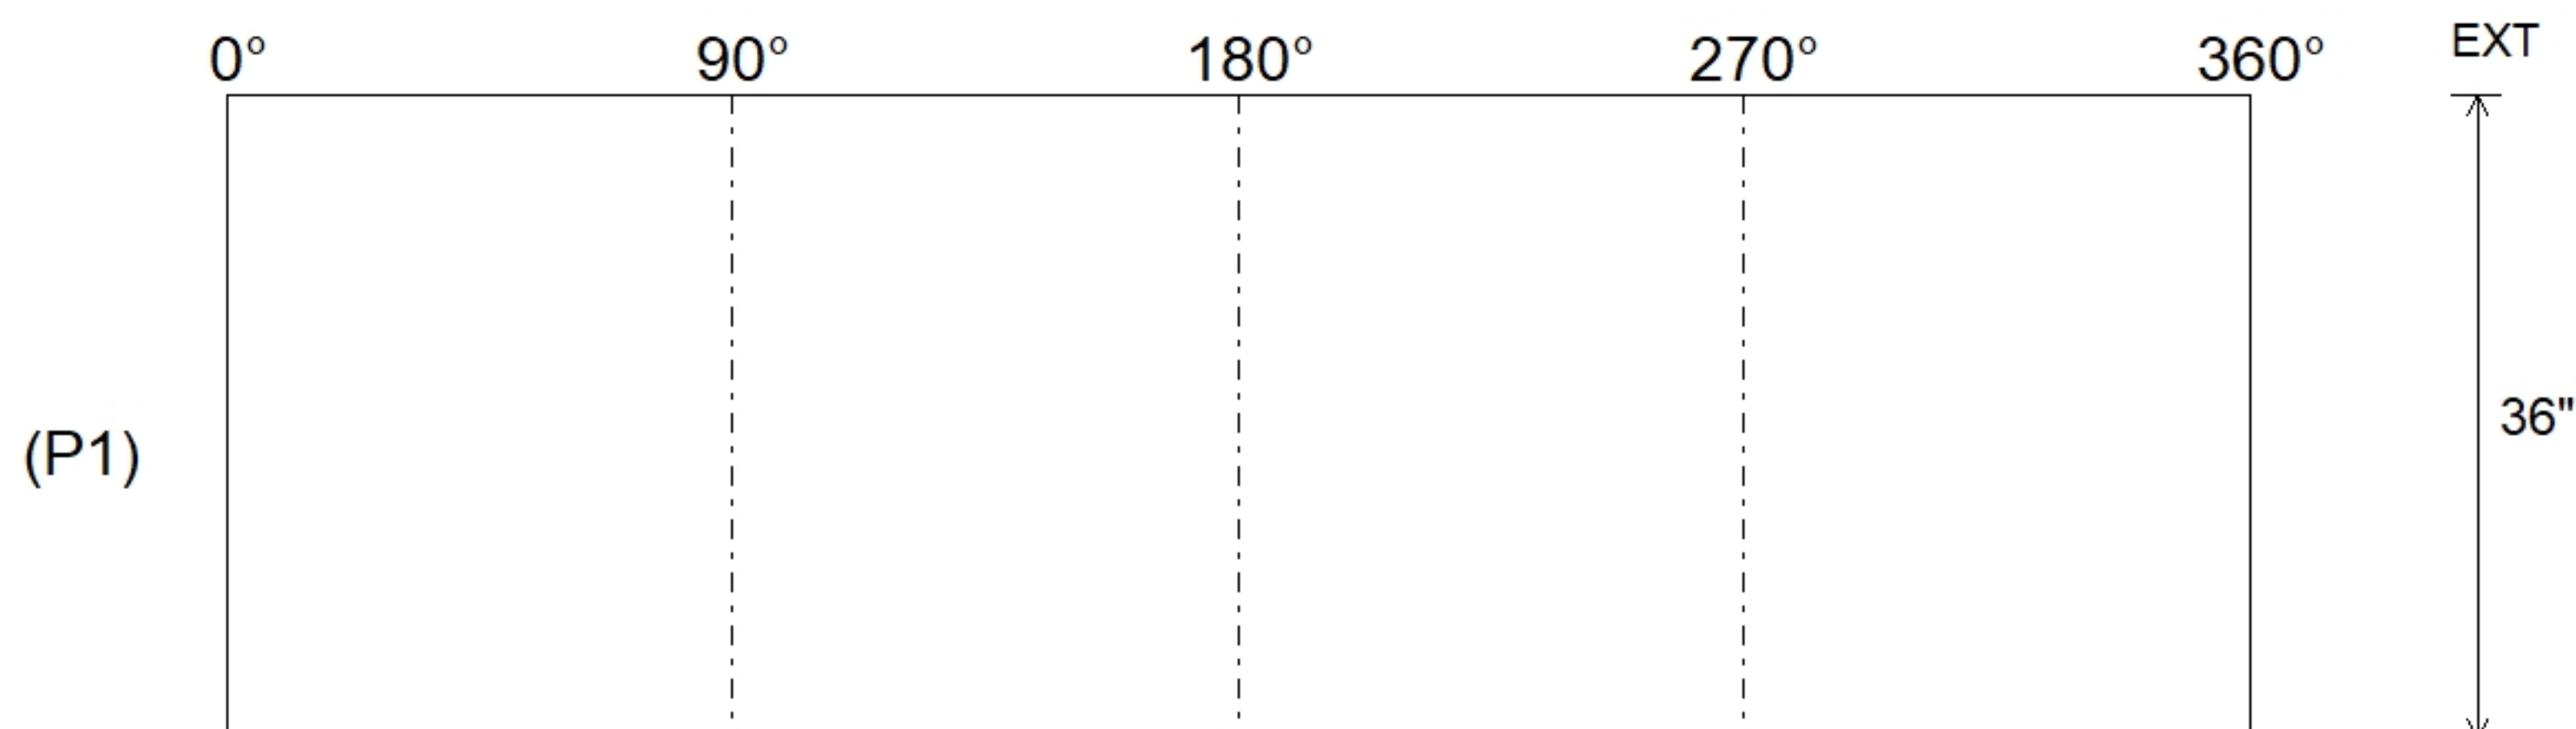

36" - PIPE CULVERT HEADWALL w/Flat Bottom/Dissipators - 36" - (P1)

Submittal Drawing
 4/2/2026 3:00:11 PM

SUBMITTAL
 APPROVED BY:
