

Job Name: 26-1117 Horse Soldier Farms Visitor Entry Road  
 Job Location: Somerset, KY  
 Contractor: Weddle Enterprises, Inc

Plant: 100

3/24/2026 12:36:25 PM

Tech: Jared - A

PC: Celina Goff



**Structure ID: S1 Riser**

**P1 MH048RS60S**

**MH RISER SPECIAL**

- P1) 48" - MH RISER SPECIAL - 60"
- 1) 48" - DBL 1"x14.5" Butyl (2x)
- 5) MH Step ML-10-TDS-NCR - 10"



4192 lb  
 0 lb  
 0 lb  
 -----  
 Structure Total: 4192 lb

- Structure Notes:**
1. PER KYTC MH A / ASTM C478 SPEC'S.
  2. CONCRETE = 5,000 PSI AT 28 DAYS.
  3. REINFORCING PER ASTM A615 (GRADE 60.)  
 - RISER/WALLS (As .12)

Rim: 5' Rim to Invert: 0' Slack: 0" Sump: 0" Step Position: 0°


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ( )	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

**RIGHT-SIDE UP VIEW (int. dimensions)**

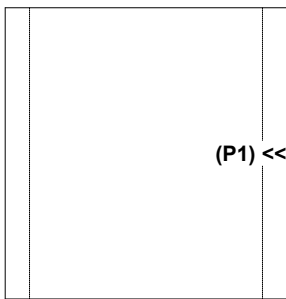

Step: 0°  
 Horz: 0"

**INSIDE WALL DIMENSIONS**

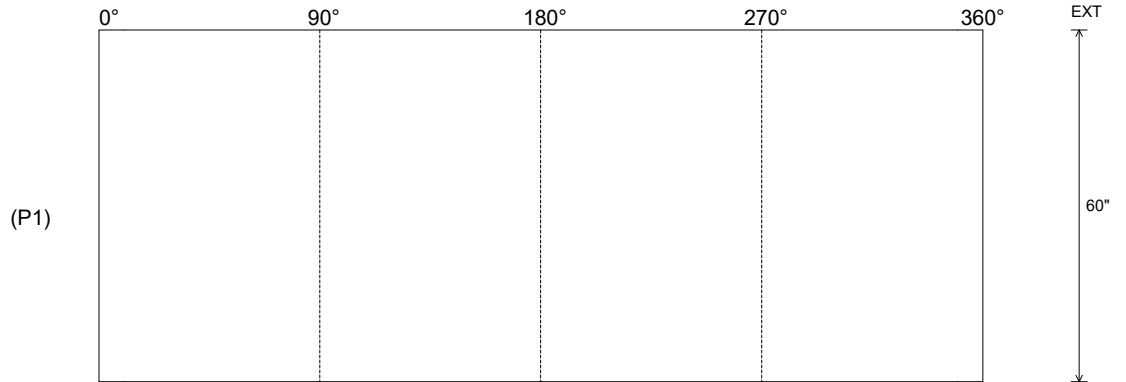

Coating (Int):  
 Coating (Ext):

Seam Up: Flat  
 Seam Dn: Flat

Wall Thickness: 5"  
 Floor Height: 0"

Height (Int): 60"  
 Height (Ext): 60"

Weight (Net): 4192 lb  
 Volume (Net): 1.07cu.yd
