

Job Name: 26-1141 - KYTC Warren Co (261106)  
 Job Location: Bowling Green, KY  
 Contractor: Mick-Murf Construction Inc.

Plant: 100  
 3/17/2026 4:01:15 PM

Tech: Jared - F  
 PC: C. Goff



**Structure ID: A12 (33)**

**P1 BX2424-08BA36**

**BOX BASE 8inW, 8inF/n**

P2) 24" x 24" - CASTING HEIGHT - 5"  
 P1) 24" x 24" - BOX BASE 8inW, 8inF/n - 36"  
 1) 24" x 24" - Conseal CS-102 1.00"  
 1) Hole - 18

0 lb  
 3997 lb  
 0 lb  
 0 lb  
 -----  
 Structure Total: 3997 lb

**Structure Notes:**  
 \*\*KYTC STATE PROJECT\*\*  
 1. KYTC CBI TYPE F / ASTM C913 SPECIFICATIONS.  
 2. CONCRETE = 4,000 PSI AT 28 DAYS.  
 3. CASTING SUPPLIED BY OTHERS (HOE KY-465 SET (CBI TY F)).



REINFORCING PER ASTM A615 (GRADE 60).  
 - WALLS (As .31) #5 BARS AT 12" C.C.E.W.  
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Rim: 481.46' Rim to Invert: 3.71' Slack: 3.52" Sump: 0" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ( )	Offset
Invert 1	477.75'	0°	20"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

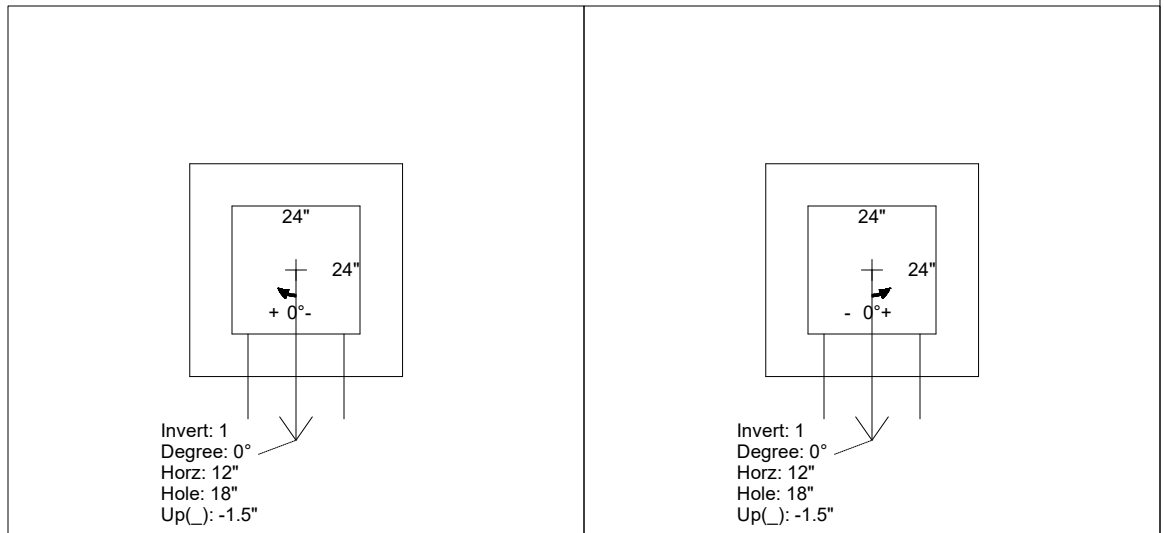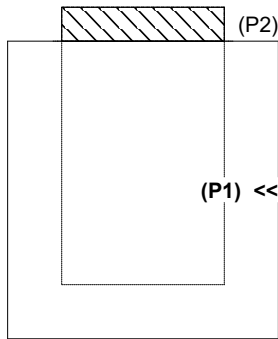

INSIDE WALL DIMENSIONS

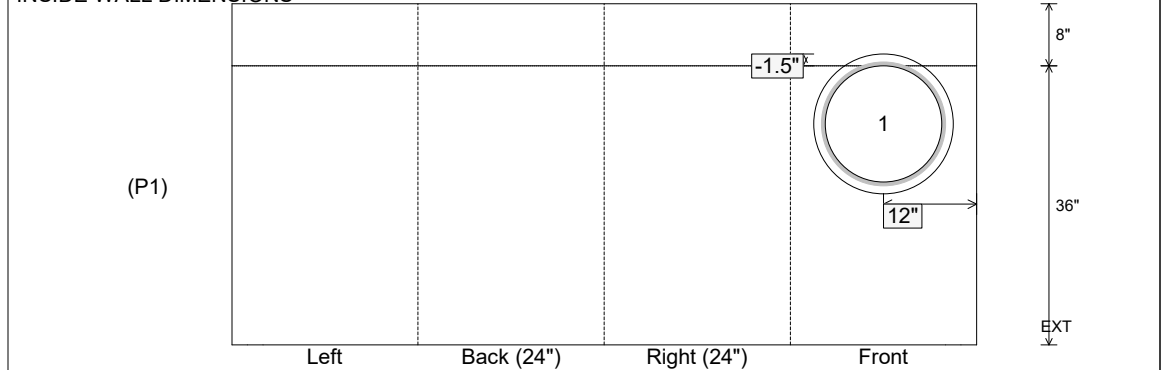

Coating (Int):  
 Coating (Ext):

Seam Up: Flat  
 Seam Dn: n/a

Wall Thickness: 8"  
 Floor Height: 8"

Height (Int): 36"  
 Height (Ext): 44"

Weight (Net): 3997 lb  
 Volume (Net): 1.02cu.yd
