

Job Name: 26-1185 - Wells Fargo Smyrna
Job Location: Smyrna, TN 37167
Contractor: Hayes Pipe Supply

Plant: 100

7/22/2026 10:01:43 AM

Tech: Jared - F
PC: E. Bradley



Structure ID: A3-5 ST-MH

P3 GR3

GRADE RING

- P4) 24" - CASTING HEIGHT - 7"
P3) 24" - GRADE RING - 3"
P2) 48" - ECC CONE w/ 24" HOLE - 30"
P1) 48" - MH BASE - 36"
1) 48" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
2) Hole - 22
6) MH Step ML-10-TDS-NCR - 10"

Structure Total:

0 lb
202 lb
2050 lb
3516 lb
0 lb
0 lb
0 lb
0 lb
5768 lb


Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. CASTING SUPPLIED BY OTHERS.


REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

NOTES:


1. GRADE RINGS MEET OR EXCEED THE FOLLOWING SPECIFICATIONS:
 - CONCRETE: 4,000 PSI @ 28 DAYS.
 - REINFORCING: (1) #3 HOOP CENTERED (GRADE 60)

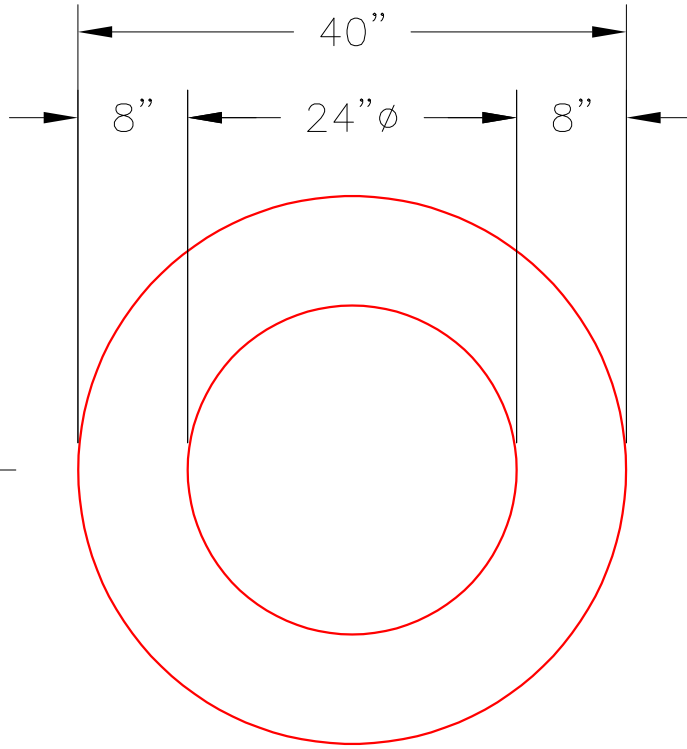

PLAN VIEW



SECTION A-A

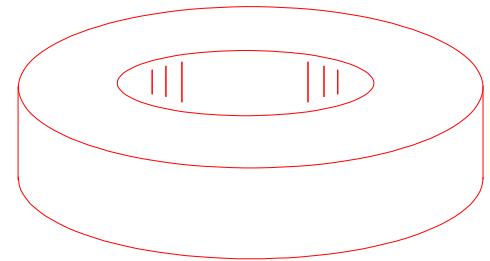

ISOMETRIC VIEW

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 3"

Weight (Net): 202 lb
Volume (Net): 0.05cu.yd
