

Job Name: 26-1193 Williamsburg Village Storm

Job Location: Danville, KY

Contractor: May Excavation & Contracting, LLC

Plant: 100

6/19/2026 9:02:58 AM

Tech: Jared - A

PC: Thomas Ryan



Structure ID: JB2-4 JBB

P2 BX2424-08R24

BOX RISER 8inW

P4) 24" - CASTING HEIGHT - 4"

P3) 24" x 24" - BX FLAT LID 8inW w/CC 24" HOLE - 8"

P2) 24" x 24" - BOX RISER 8inW - 24"

P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht - 39"

1) CASTING - HOE KY-206 F/C (KY TY1)

2) 24" x 24" - Conseal CS-102 1.00"

1) 24" - Conseal CS-102 1.00"

3) Hole - 20

0 lb

770 lb

2062 lb

3771 lb

206 lb

0 lb

0 lb

0 lb

6809 lb

Structure Notes: .

1. HOE KY-206 F/C (KY TY1) PROVIDED BY ICAST.

2. KYTC JUNCTION BOX B1 / PER ASTM C913 SPEC'S.

3. CONCRETE = 4,000 PSI AT 28 DAYS.

4. TOP SLAB w KYTC TYPE 1 F/C CAST FLUSH.

5. REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As. 62) #5 BARS AT 6" C.C.E.W.

- WALLS (As .31) #5 BARS AT 12" C.C.E.W.

- FLOOR (As .31) #5 BARS AT 12: C.C.E.W.

Structure Total:

6809 lb

Rim: 906.25'

Rim to Invert: 6.25'


Slack: 0"

Sump: 0"

Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

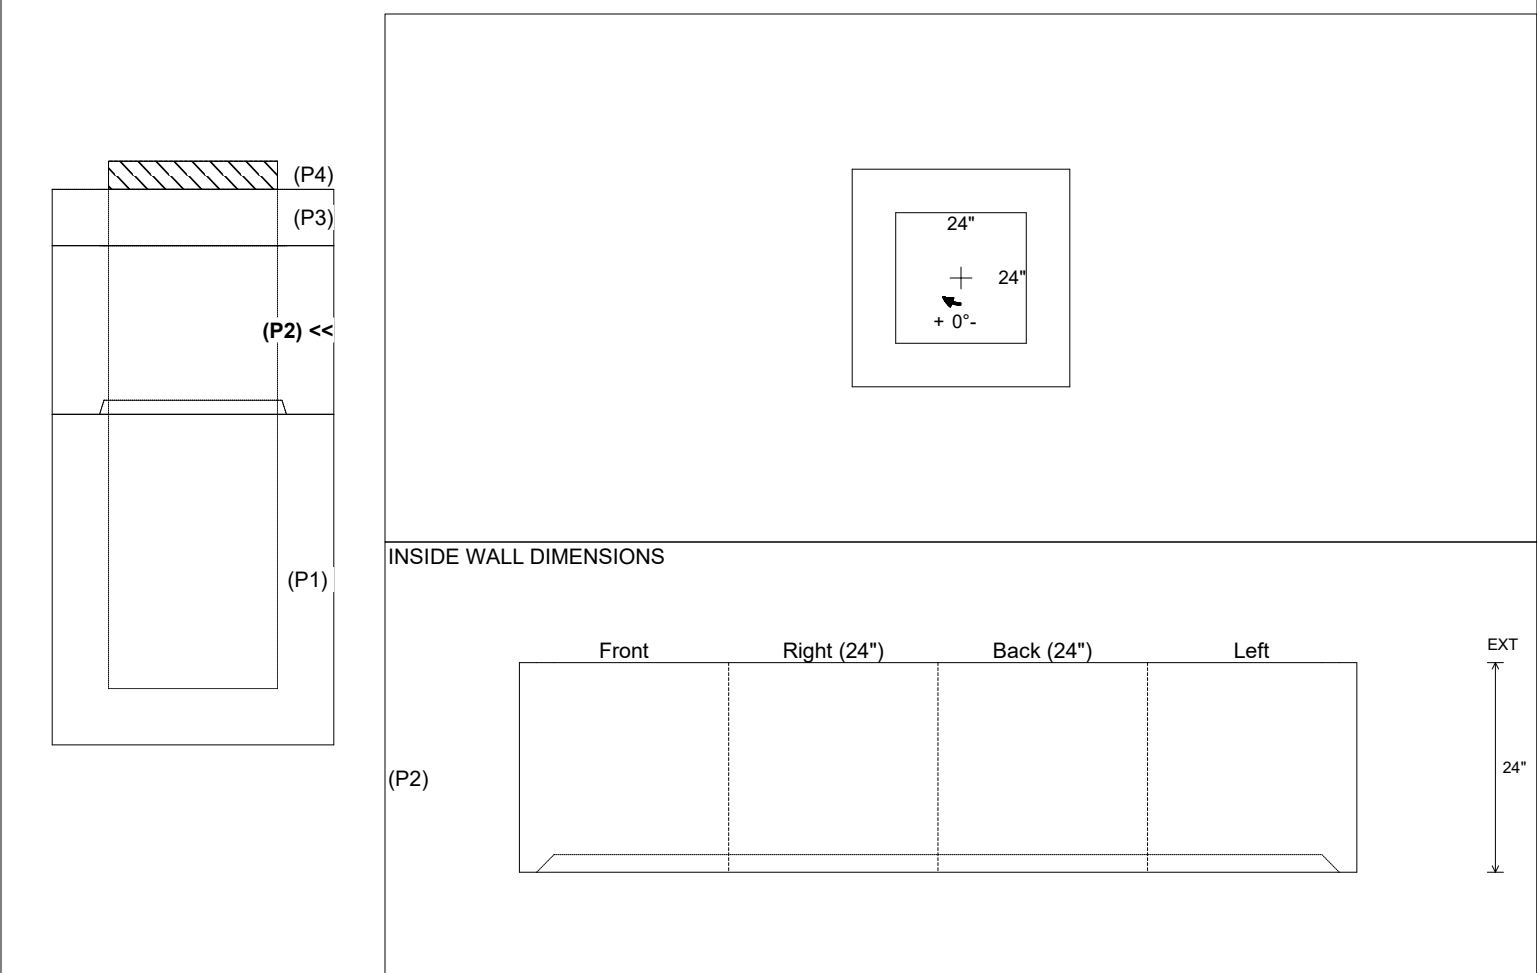

Coating (Int):	Seam Up: Flat	Wall Thickness: 8"	Height (Int): 24"	Weight (Net): 2062 lb
Coating (Ext):	Seam Dn: Groove	Floor Height: 0"	Height (Ext): 24"	Volume (Net): 0.53cu.yd
