

Job Name: 26-1232 - Mustang Village Apartments Ph.1	Plant: 100	Tech: Jared - F	
Job Location: Paducah, KY Contractor: Wood Brothers	4/24/2026 1:19:30 PM	PC: T. Lewis	


Structure ID: SSMH C-2-54 SS-MH

P4 GR3 GRADE RING

P5) 24" - CASTING HEIGHT - 7"	0 lb
P4) 24" - GRADE RING - 3"	202 lb
P3) 48" - ECC CONE w/ 24" HOLE - 24"	1550 lb
P2) 48" - MH RISER - 48"	3353 lb
P1) 48" - MH BASE - 30"	3282 lb
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) 48" - MH INVERT CHANNEL - FULL HEIGHT	1440 lb
1) CASTING - HOE MC-375 F/C Sanitary	271 lb
2) 48" - Conseal CS-102 1.00" (Double)	0 lb
1) PSX - 12-08 NYLO	8 lb
2) PSX - 12-06 NYLO	16 lb
8) MH Step ML-10-TDS-NCR - 10"	0 lb
Structure Total:	10123 lb

Structure Notes:
 1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
 3. CASTING BY ICAST (HOE MC-375 F/C SANITARY)

REINFORCING PER ASTM A615 (GRADE 60).
 - CONE (As .12)
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

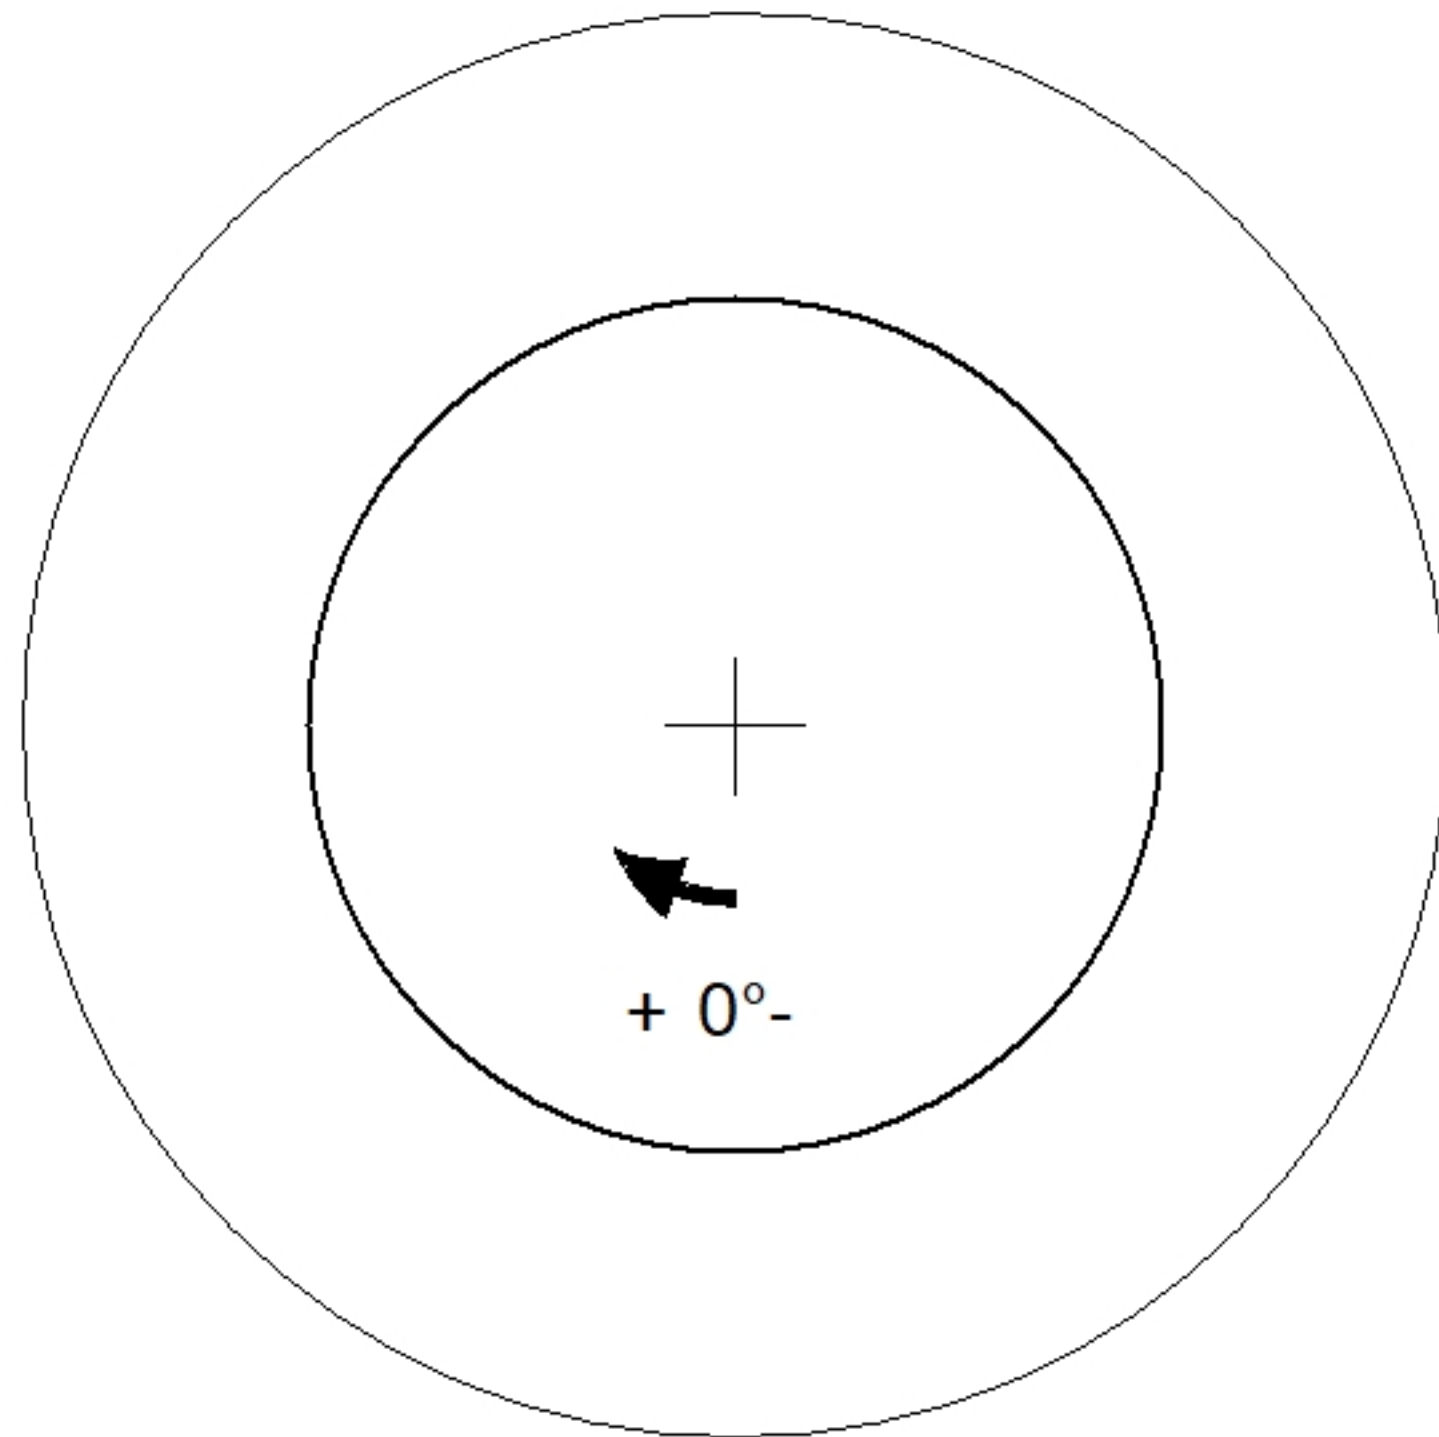

Coating (Int):	Seam Up: Flat	Wall Thickness: 8"	Height (Ext): 3"	Weight (Net): 202 lb
Coating (Ext):	Seam Dn: Flat			Volume (Net): 0.05cu.yd
