

Contractor: Endesol, Inc.

TECH: Jared - F

Plant: 100



Size: 60" x 60"


Rim to Invert: 4.5'

Floor Height: 12"

Slack: 0"



- FLOOR (As .31) #5 BARS AT 12" C.C.E.W. (DOUBLE MAT)

Structure Total: 19550 lb



Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	5.667'							
Reducer								
Invert 1	1.167'	0°	8" DI	9"	12"	PSX 12M DD	12"	P1
Invert 2	1.167'	180°	8" DI	9"	12"	PSX 12M DD	12"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

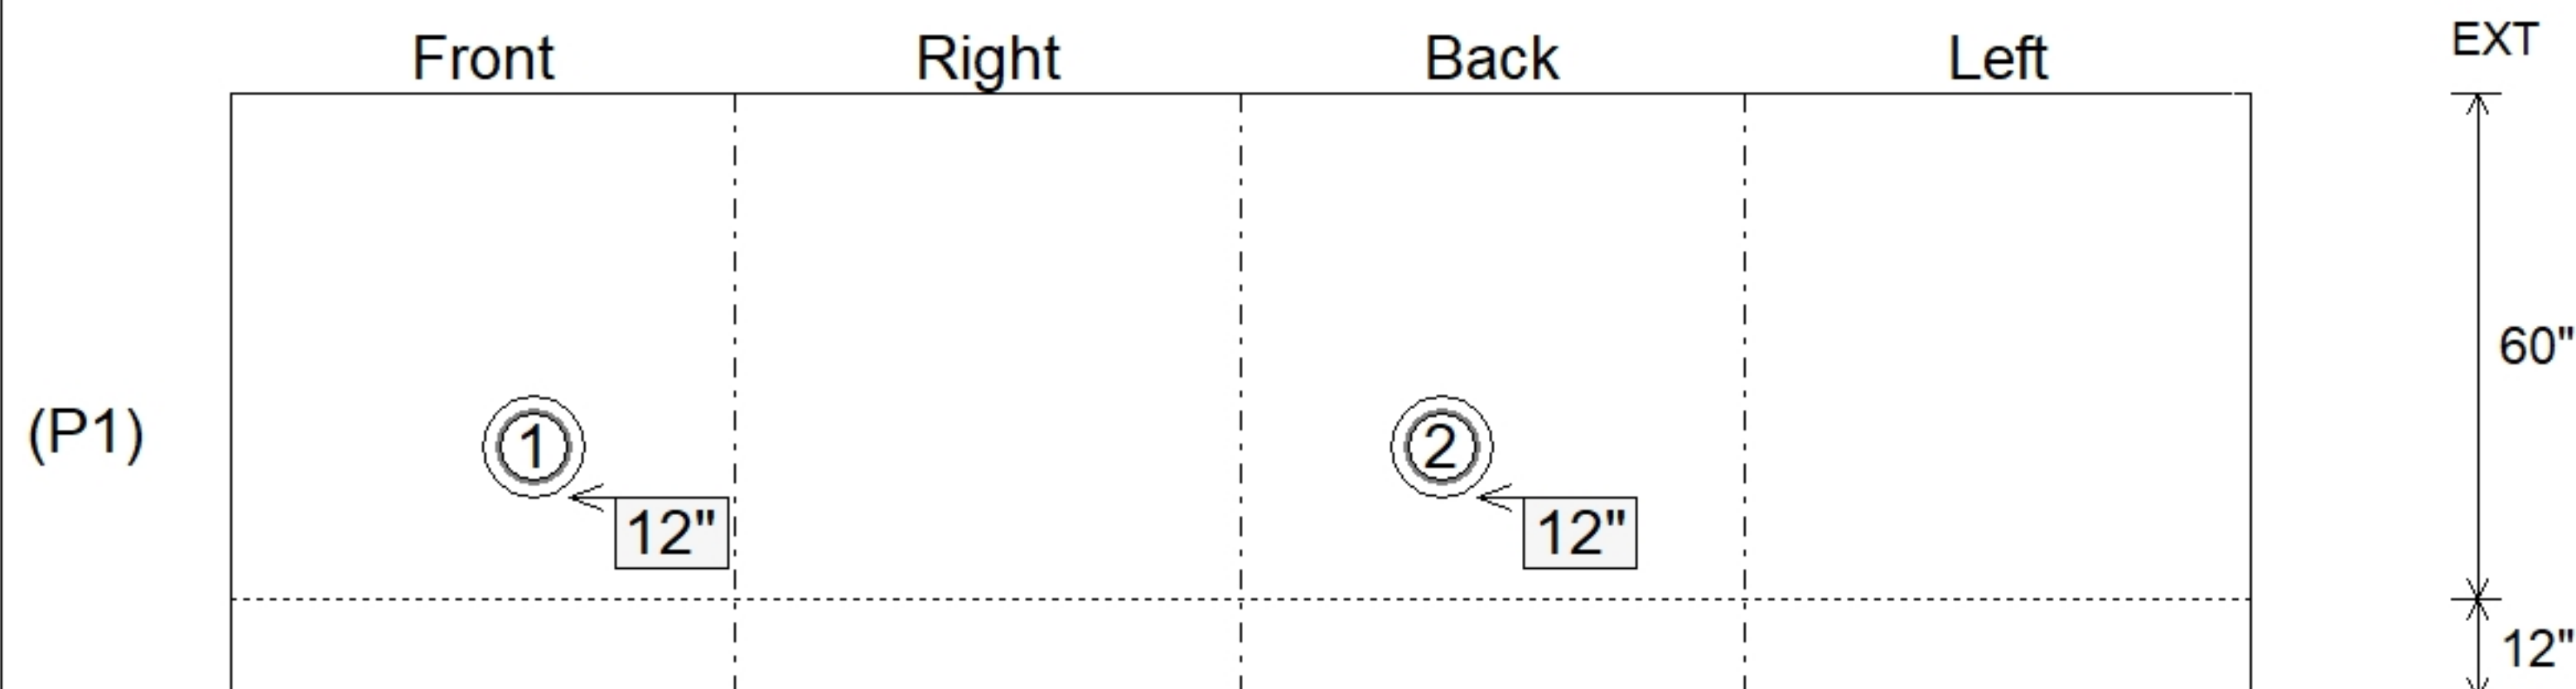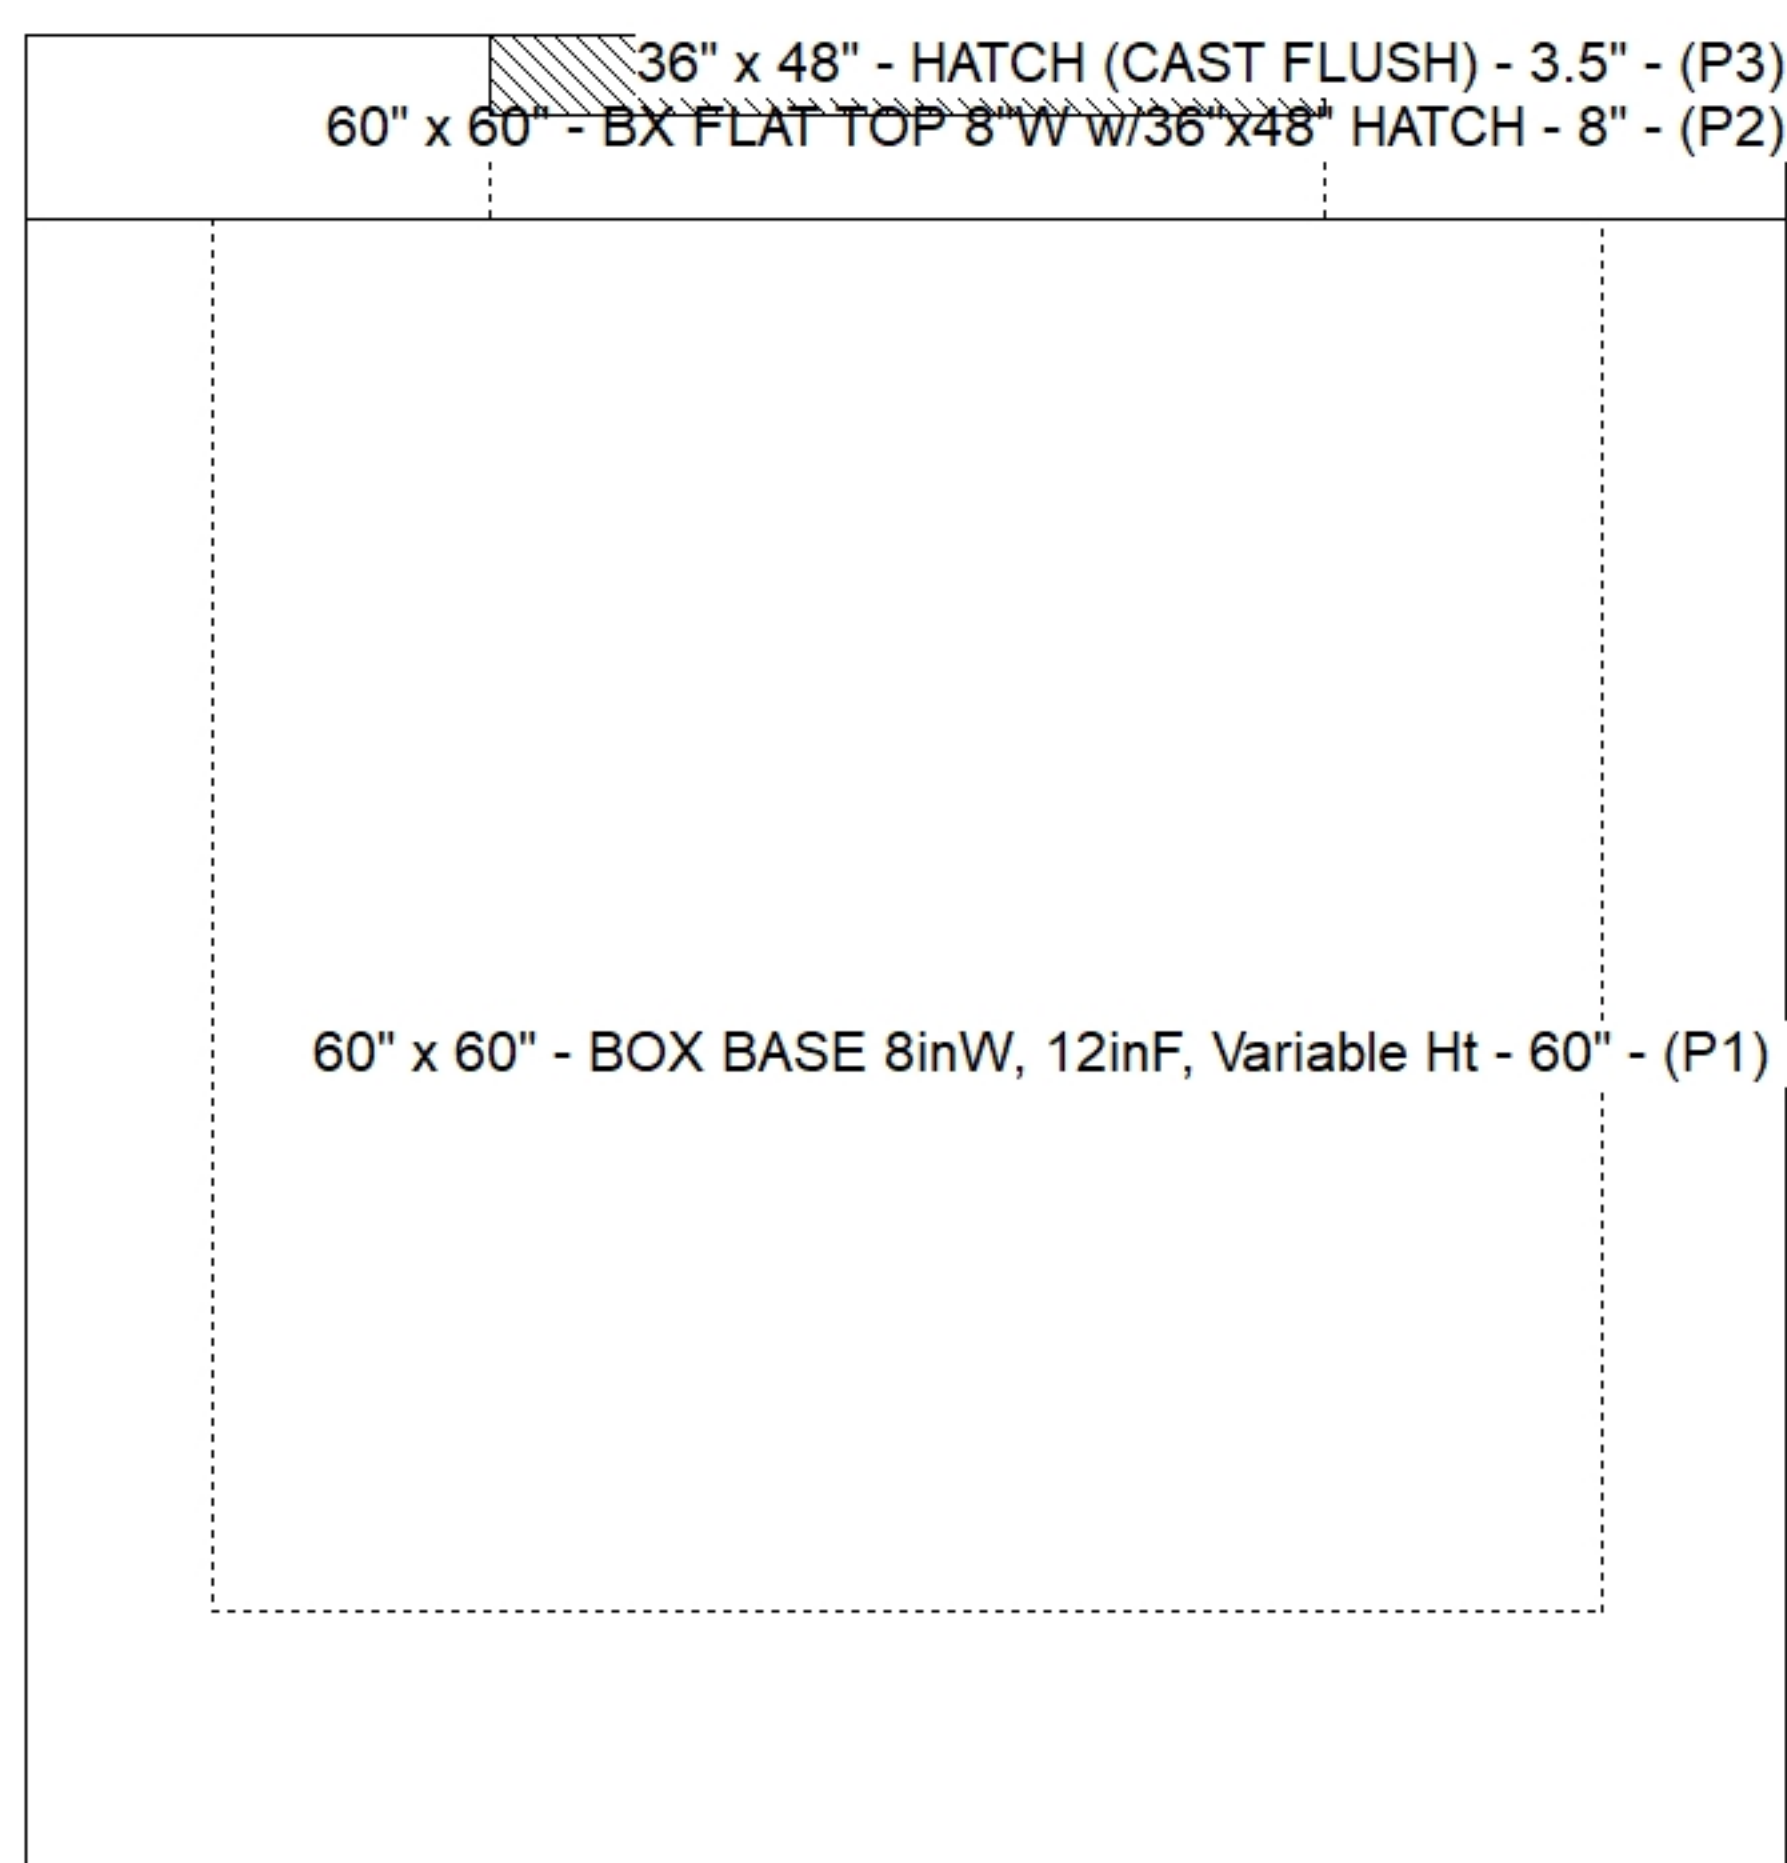

SUBMITTAL
APPROVED BY:
