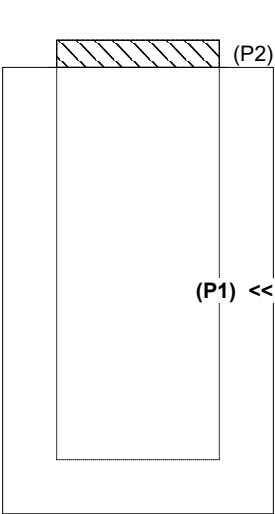
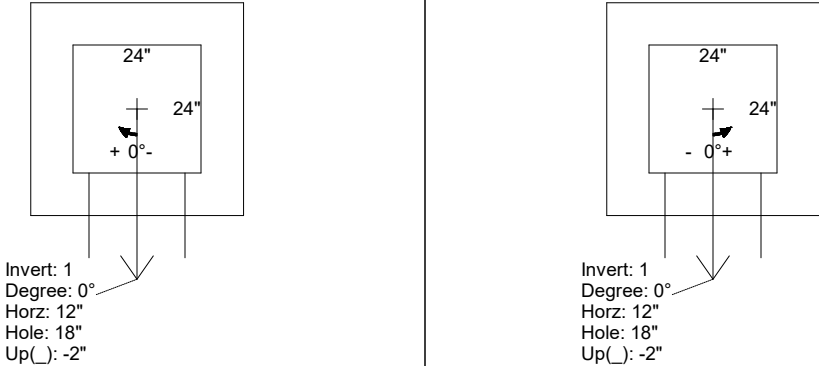
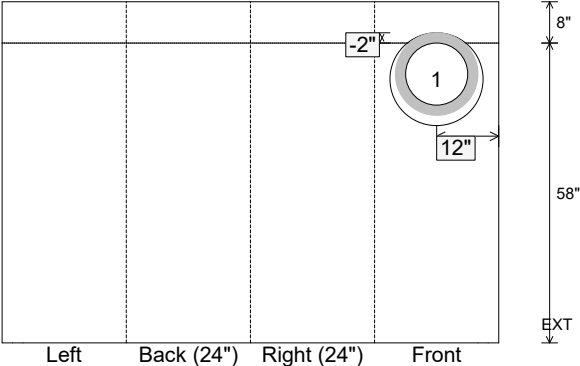


Job Name: 26-1260 - Meade Co 2023 Water Improvements Job Location: Brandenburg, KY Contractor: Endesol, Inc.					Plant: 100 9/10/2026 3:57:30 PM		Tech: Jared - F PC: E. Bradley				
Structure ID: 4 ST-CB											
P1 BX2424-08BAVF			BOX BASE 8inW, 8inF, Variable Ht F/n								
P2) 24" x 24" - CASTING HEIGHT - 4" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht F/n - 58" 1) CASTING - HOE 280T F/G 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 18						0 lb 5887 lb 182 lb 0 lb 0 lb ----- 6069 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING SUPPLIED BY ICAST (HOE 280T F/G). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.			
Rim: 590.31' Rim to Invert: 5.17' Slack: 0.04" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	585.14'	0°	20"	12" RCP B WALL	16"	Hole 18	18"	18"	-2"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)   INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 58" Height (Ext): 66"		Weight (Net): 5887 lb Volume (Net): 1.5cu.yd		
