

Contractor: Endesol, Inc.

TECH: Jared - F

Plant: 100



Size: 24" x 24"

Rim to Invert: 5.17'

Floor Height: 8"


Slack: 0.04"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.


P2) 24" x 24" - CASTING HEIGHT - 4"
P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht - 58"
1) CASTING - HOE 280T F/G
1) 24" x 24" - Conseal CS-102 1.00"
1) Hole - 18

0 lb
5887 lb
182 lb
0 lb
0 lb

Structure Total: 6069 lb

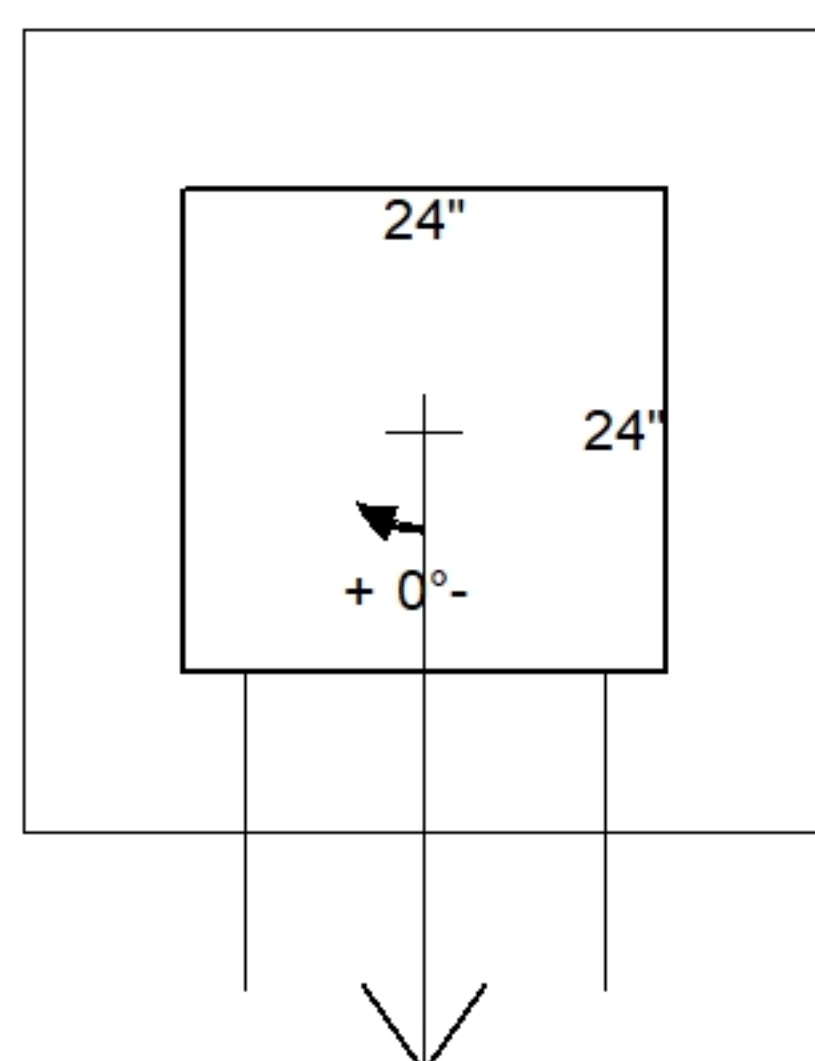


Invert: 1
Degree: 0°

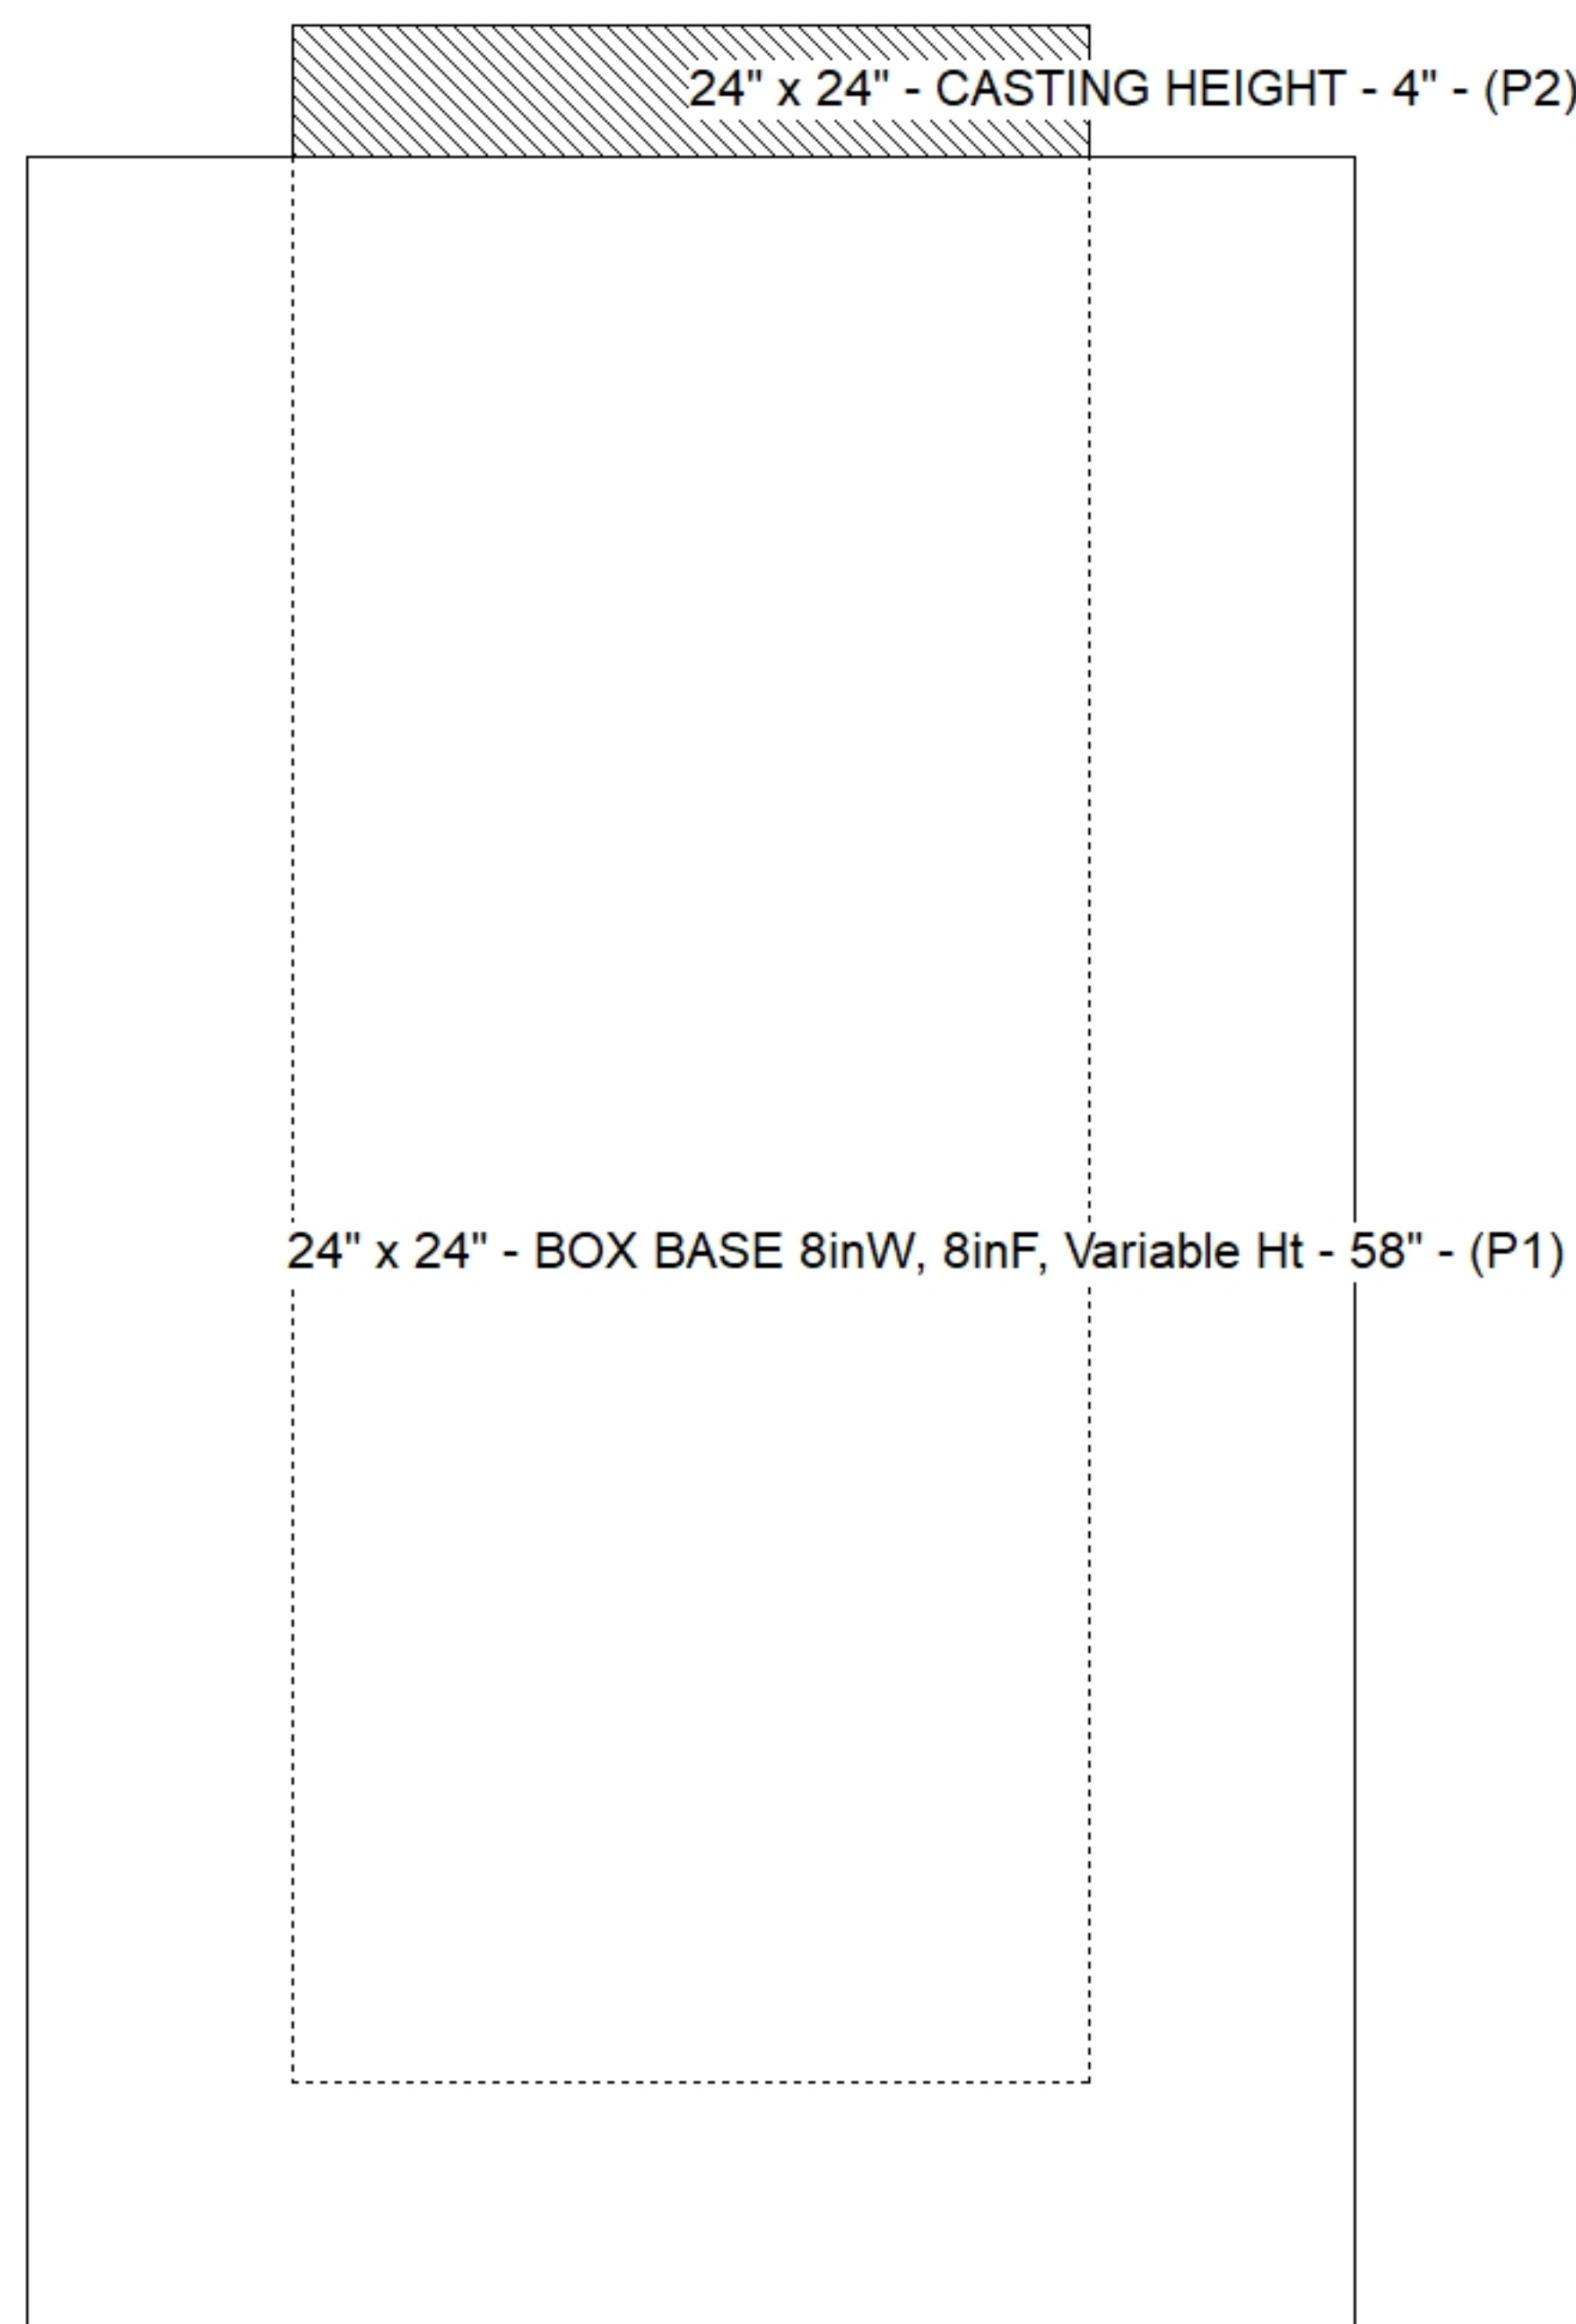

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	590.31'							
Reducer								
Invert 1	585.14'	0°	12" RCP B WALL	16"	18"	Hole 18	-2"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

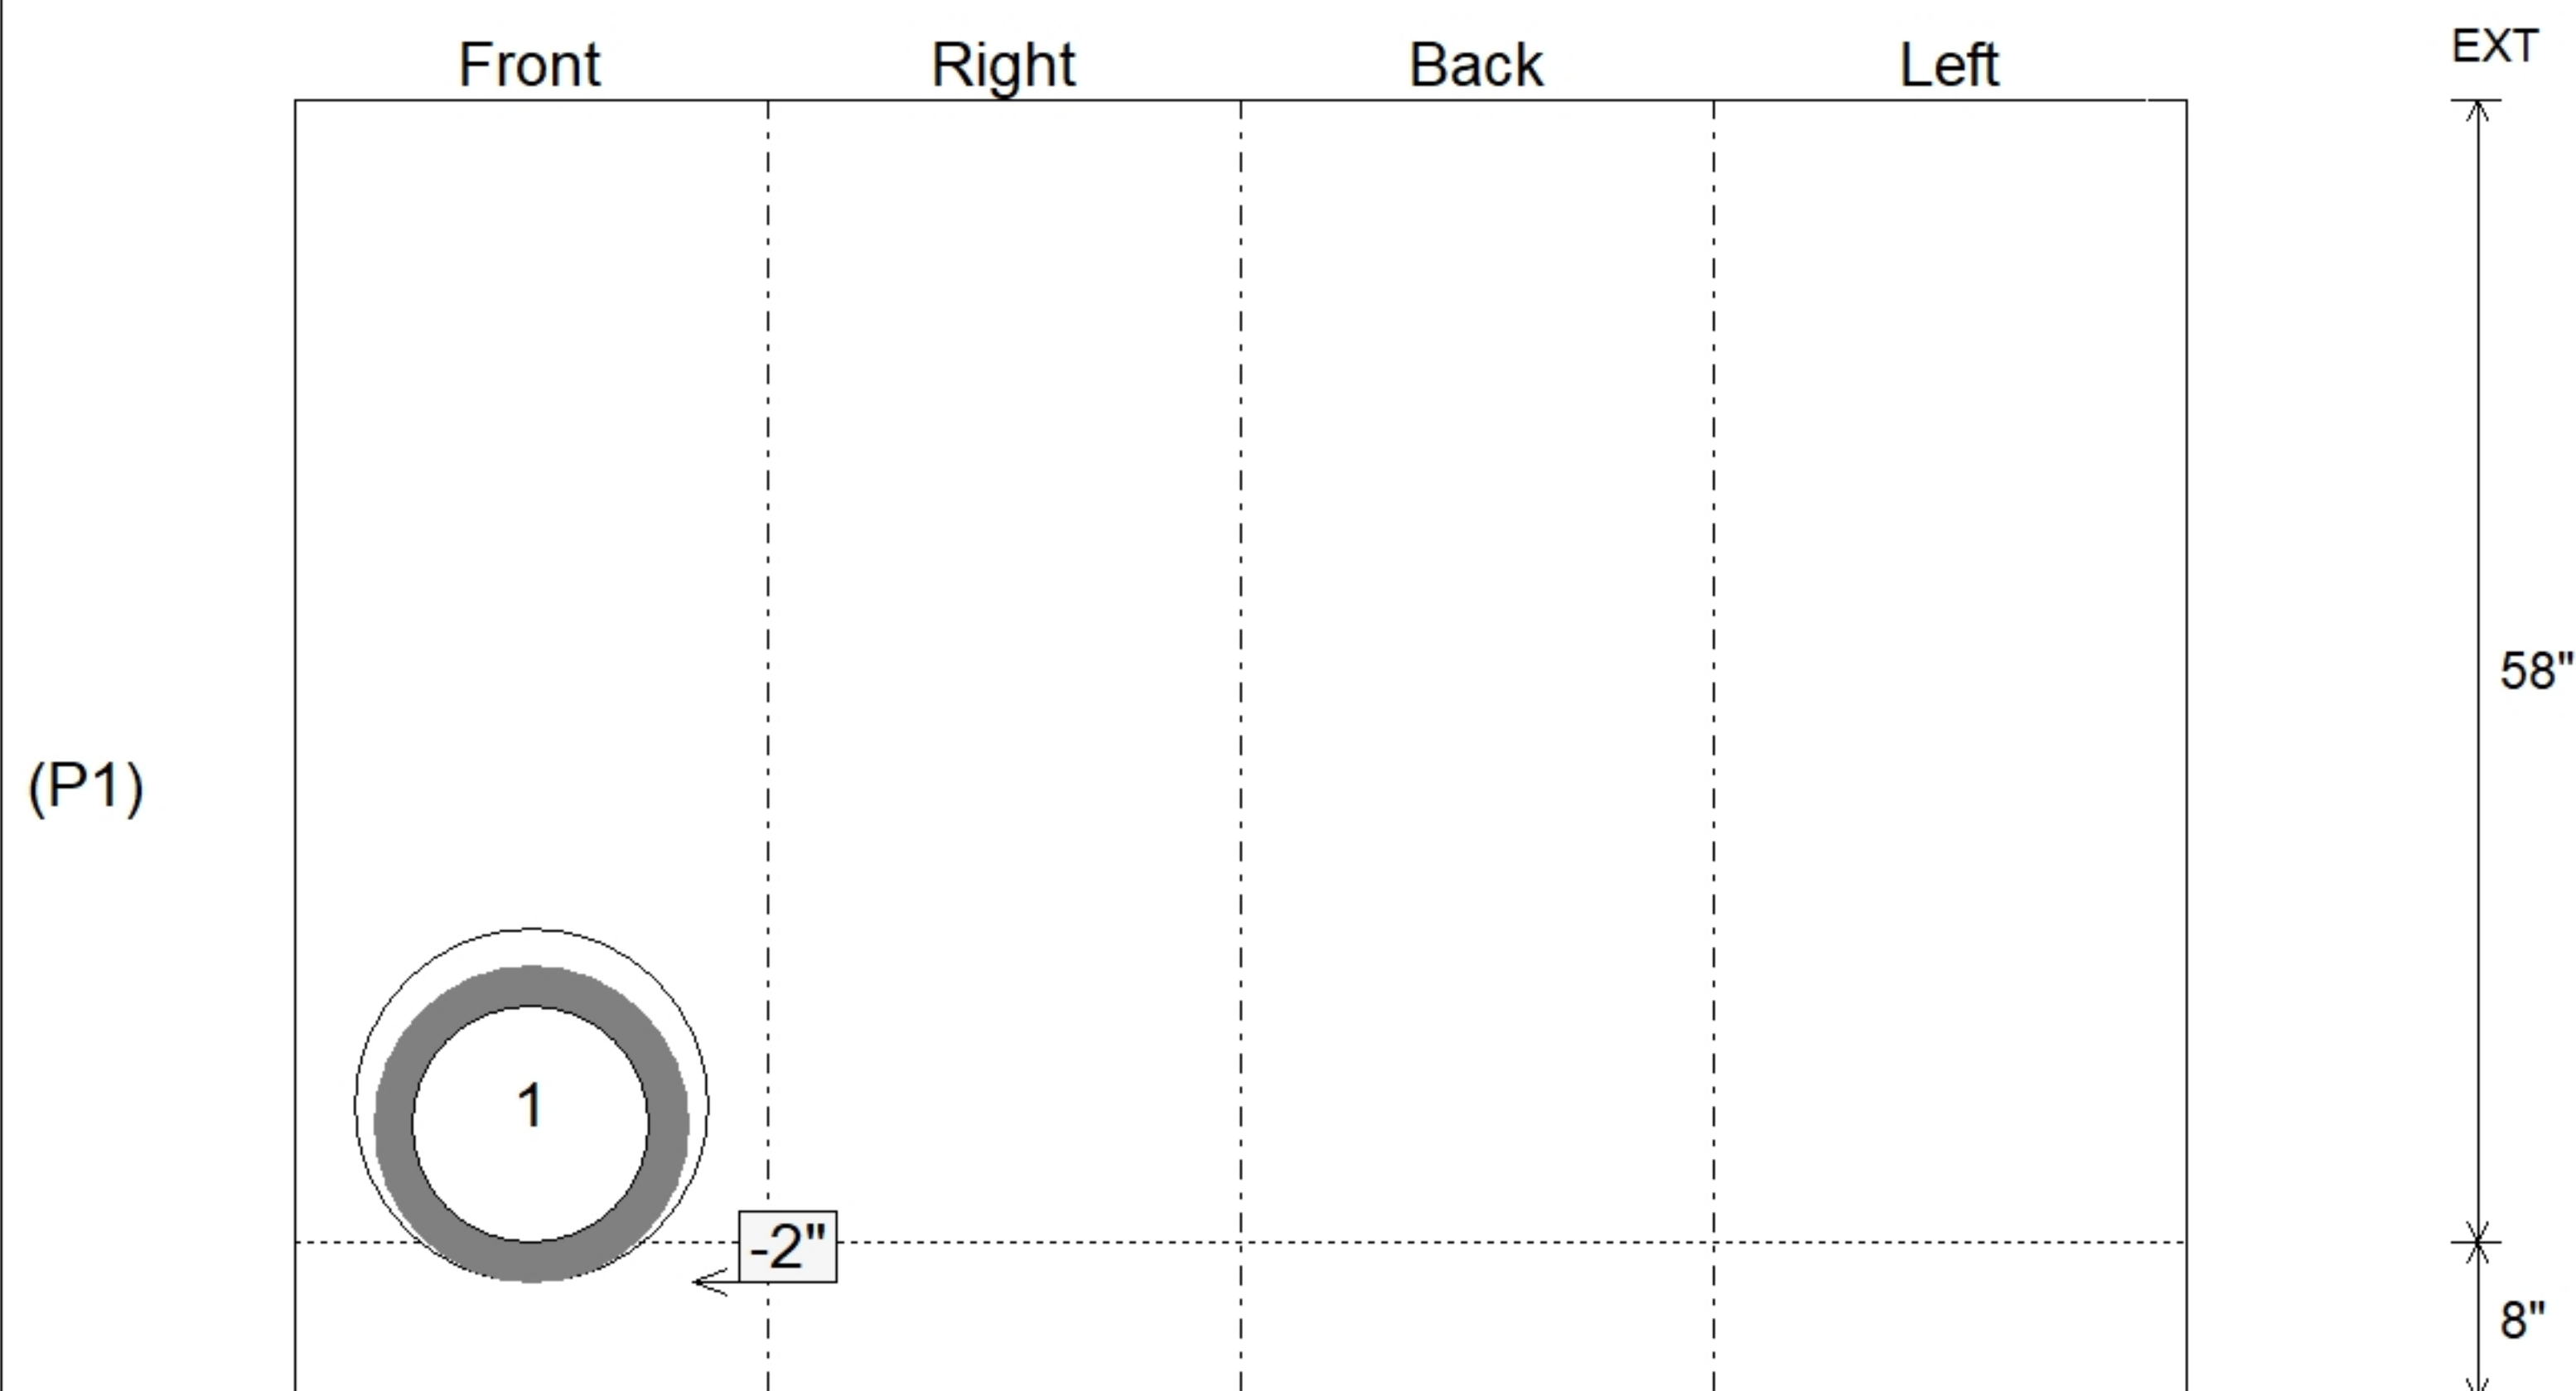

Submittal Drawing
9/18/2026 8:06:42 AM

SUBMITTAL
APPROVED BY:
