

Contractor: Mick-Murf Construction Inc.

TECH: Jared - F

Plant: 100



Size: 36" x 36"


Rim to Invert: 5.89'

Floor Height: 8"

Slack: 3.68"


0 lb

Structure Total: 14591 lb

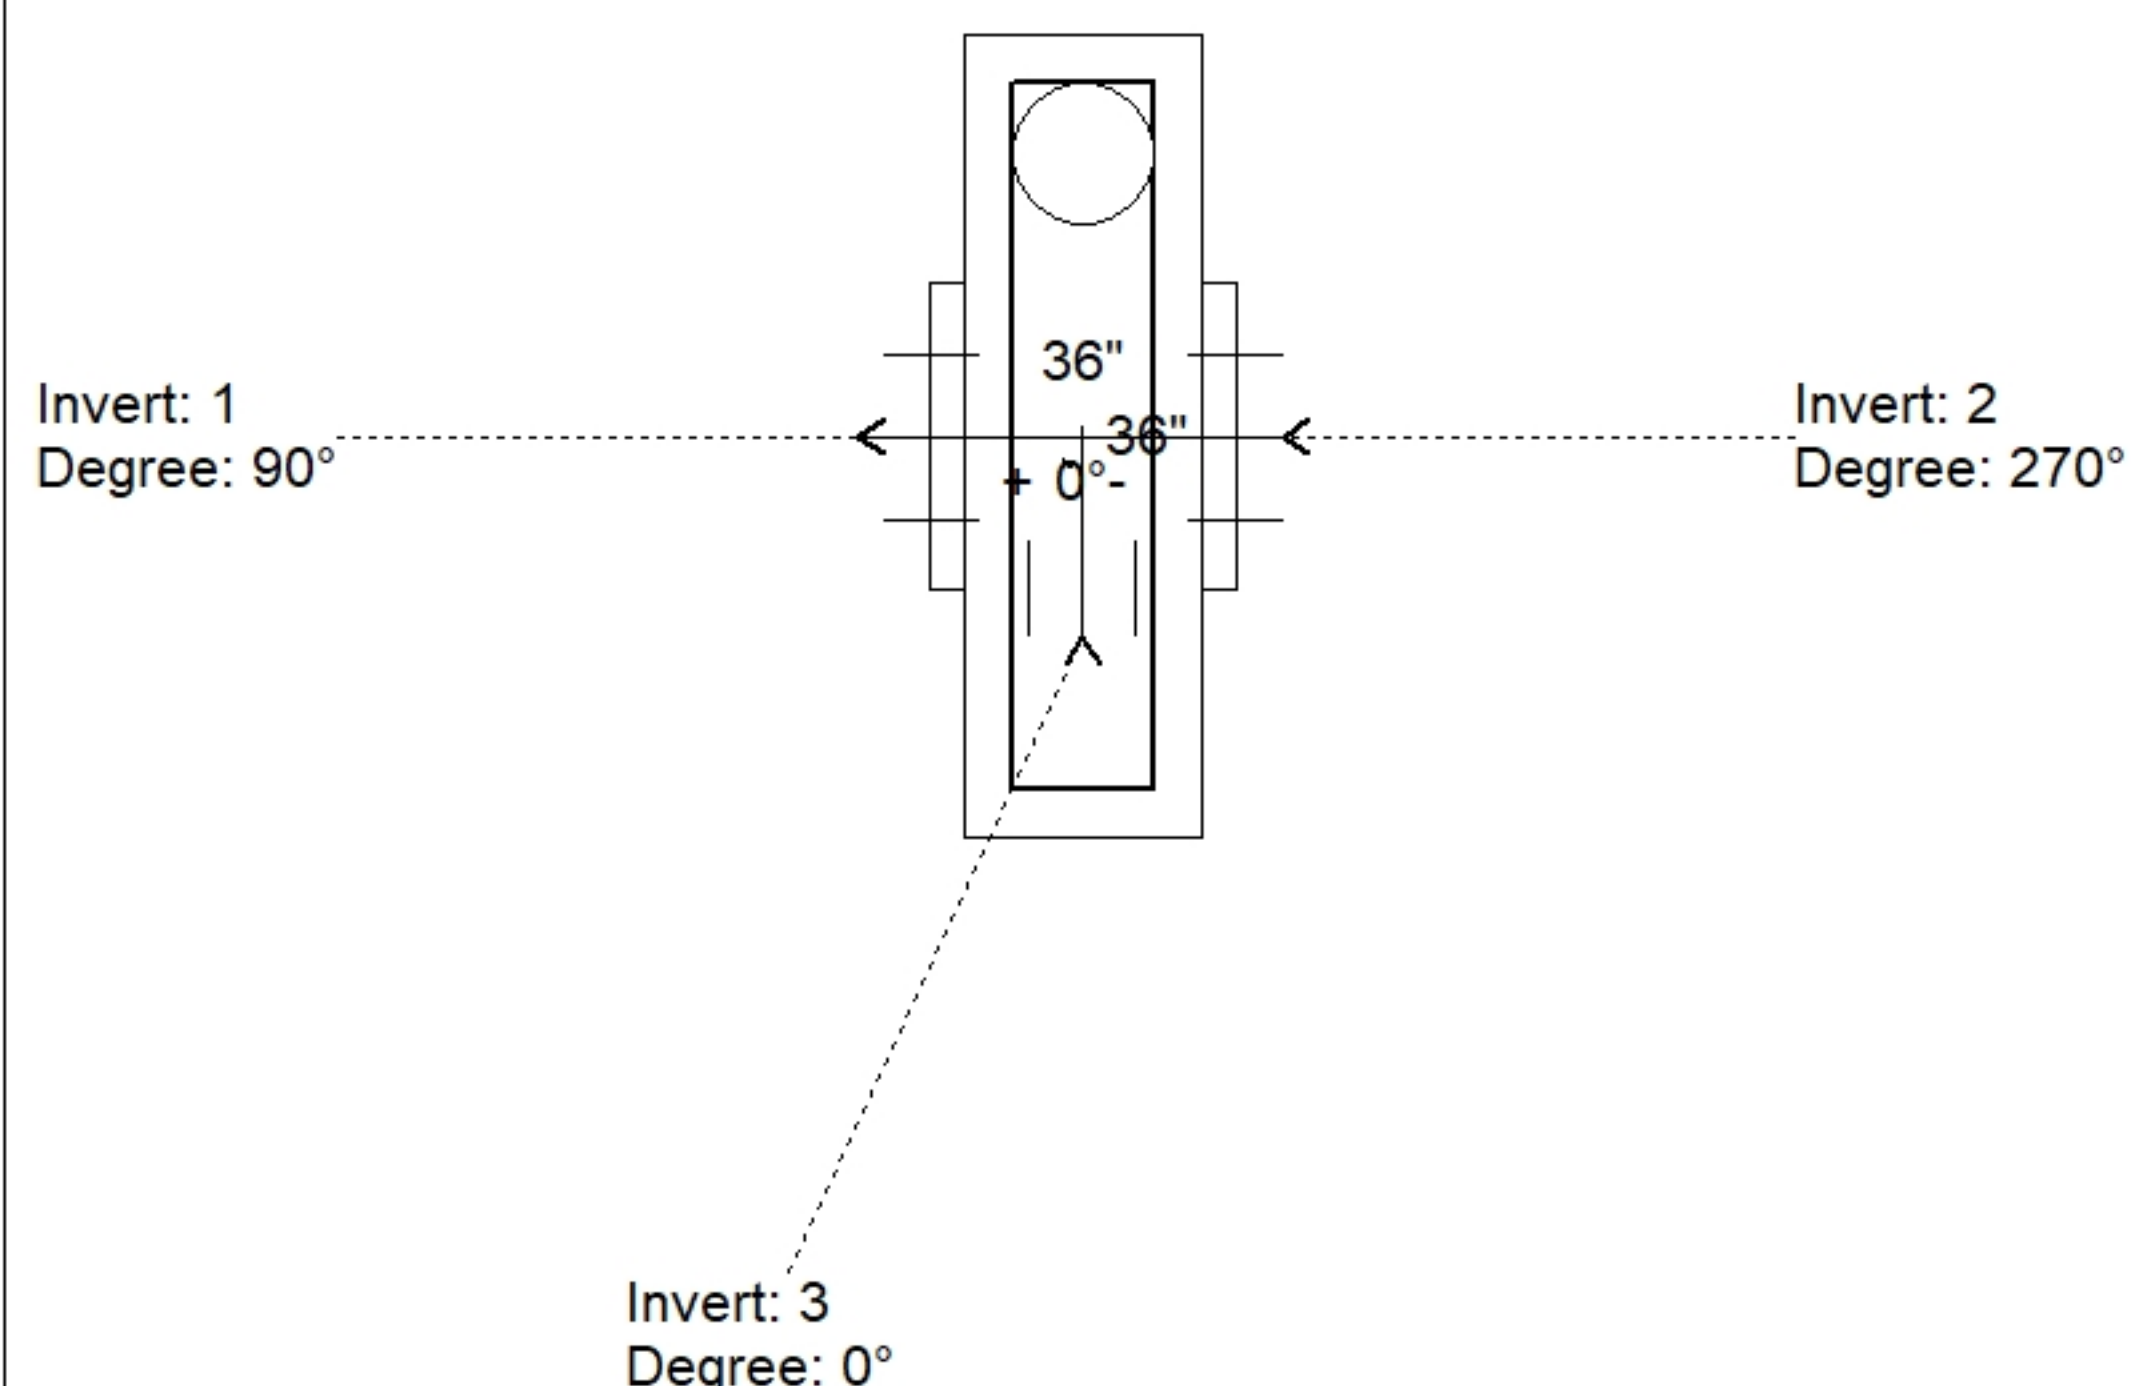

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	533.55'							
Reducer	530.243'							
Invert 1	527.66'	90°	24" CMP	25"	28"	Hole 28	-2"	P1
Invert 2	527.74'	270°	24" CMP	25"	28"	Hole 28	-1.04"	P1
Invert 3	527.74'	0°	15" CMP	16"	18"	Hole 18	-0.54"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

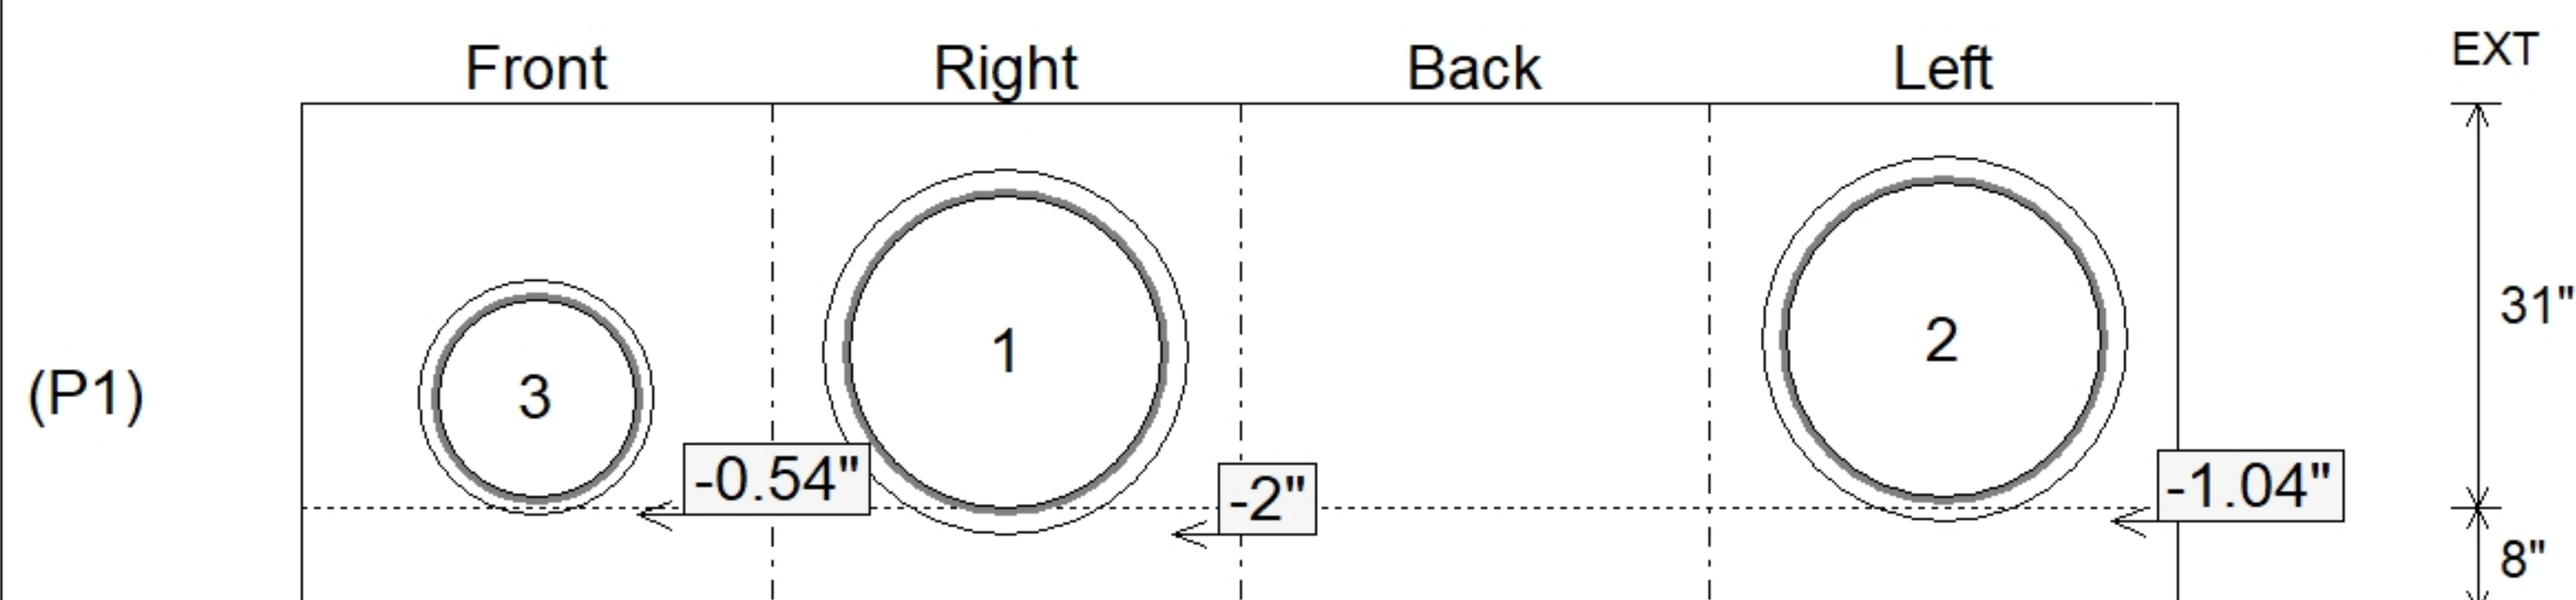

Submittal Drawing
9/8/2026 3:32:59 PM

SUBMITTAL
APPROVED BY:
