

Contractor: Mick-Murf Construction Inc.

TECH: Jared - F

Plant: 100



Size: 36" x 36"

Rim to Invert: 3.89'


Floor Height: 8"

Slack: 3.68"

1) Hole - 18



0 | b

Structure Total: 5366 lb

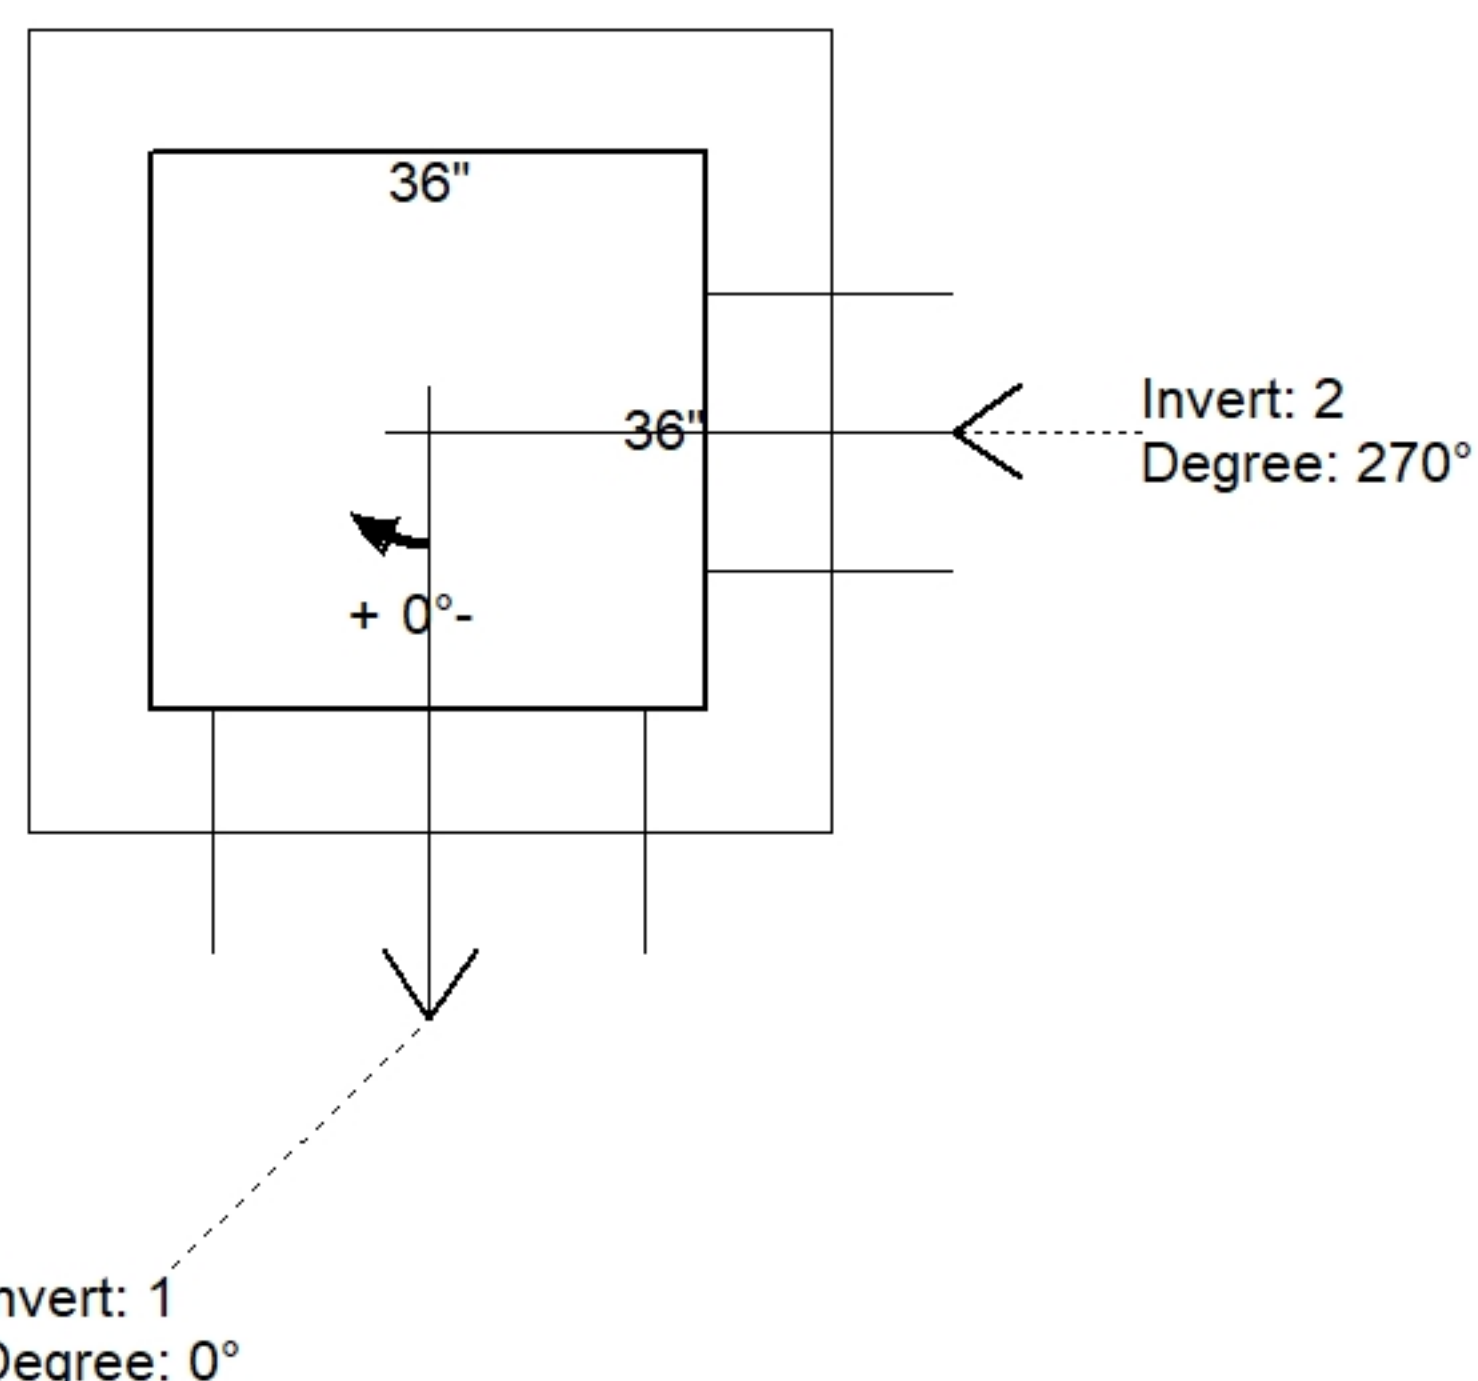

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	531.77'							
Reducer								
Invert 1	527.88'	0°	24" CMP	25"	28"	Hole 28	-2"	P1
Invert 2	527.96'	270°	15" CMP	16"	18"	Hole 18	-0.54"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

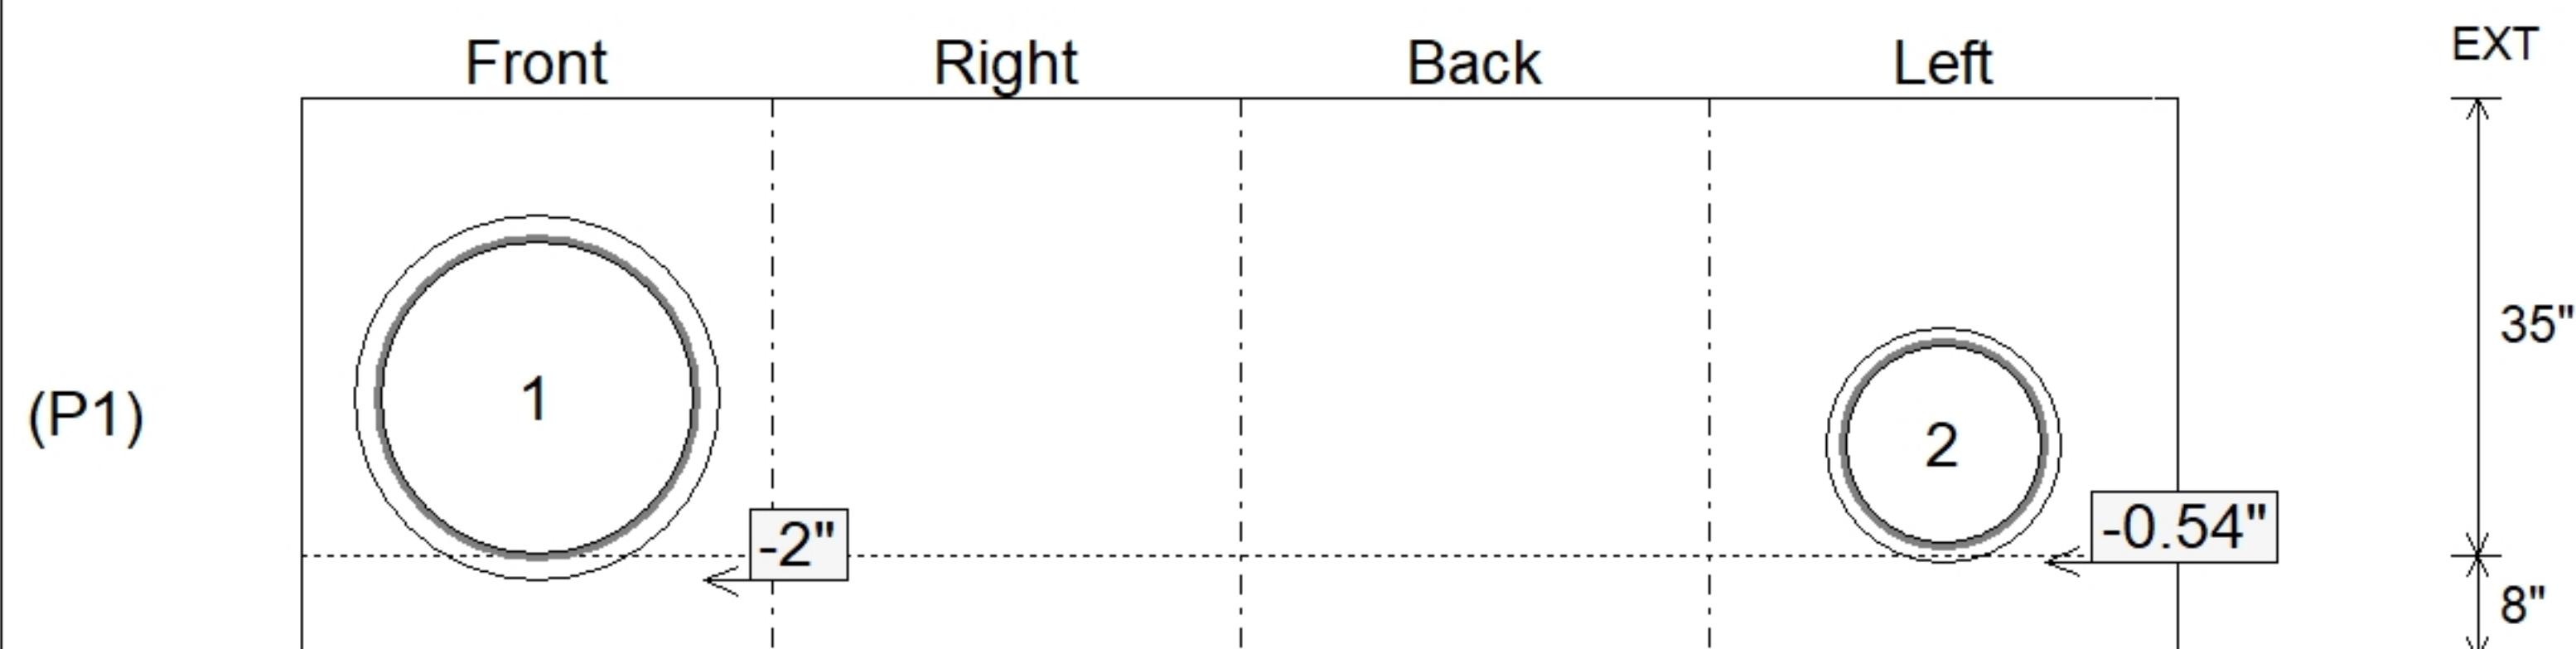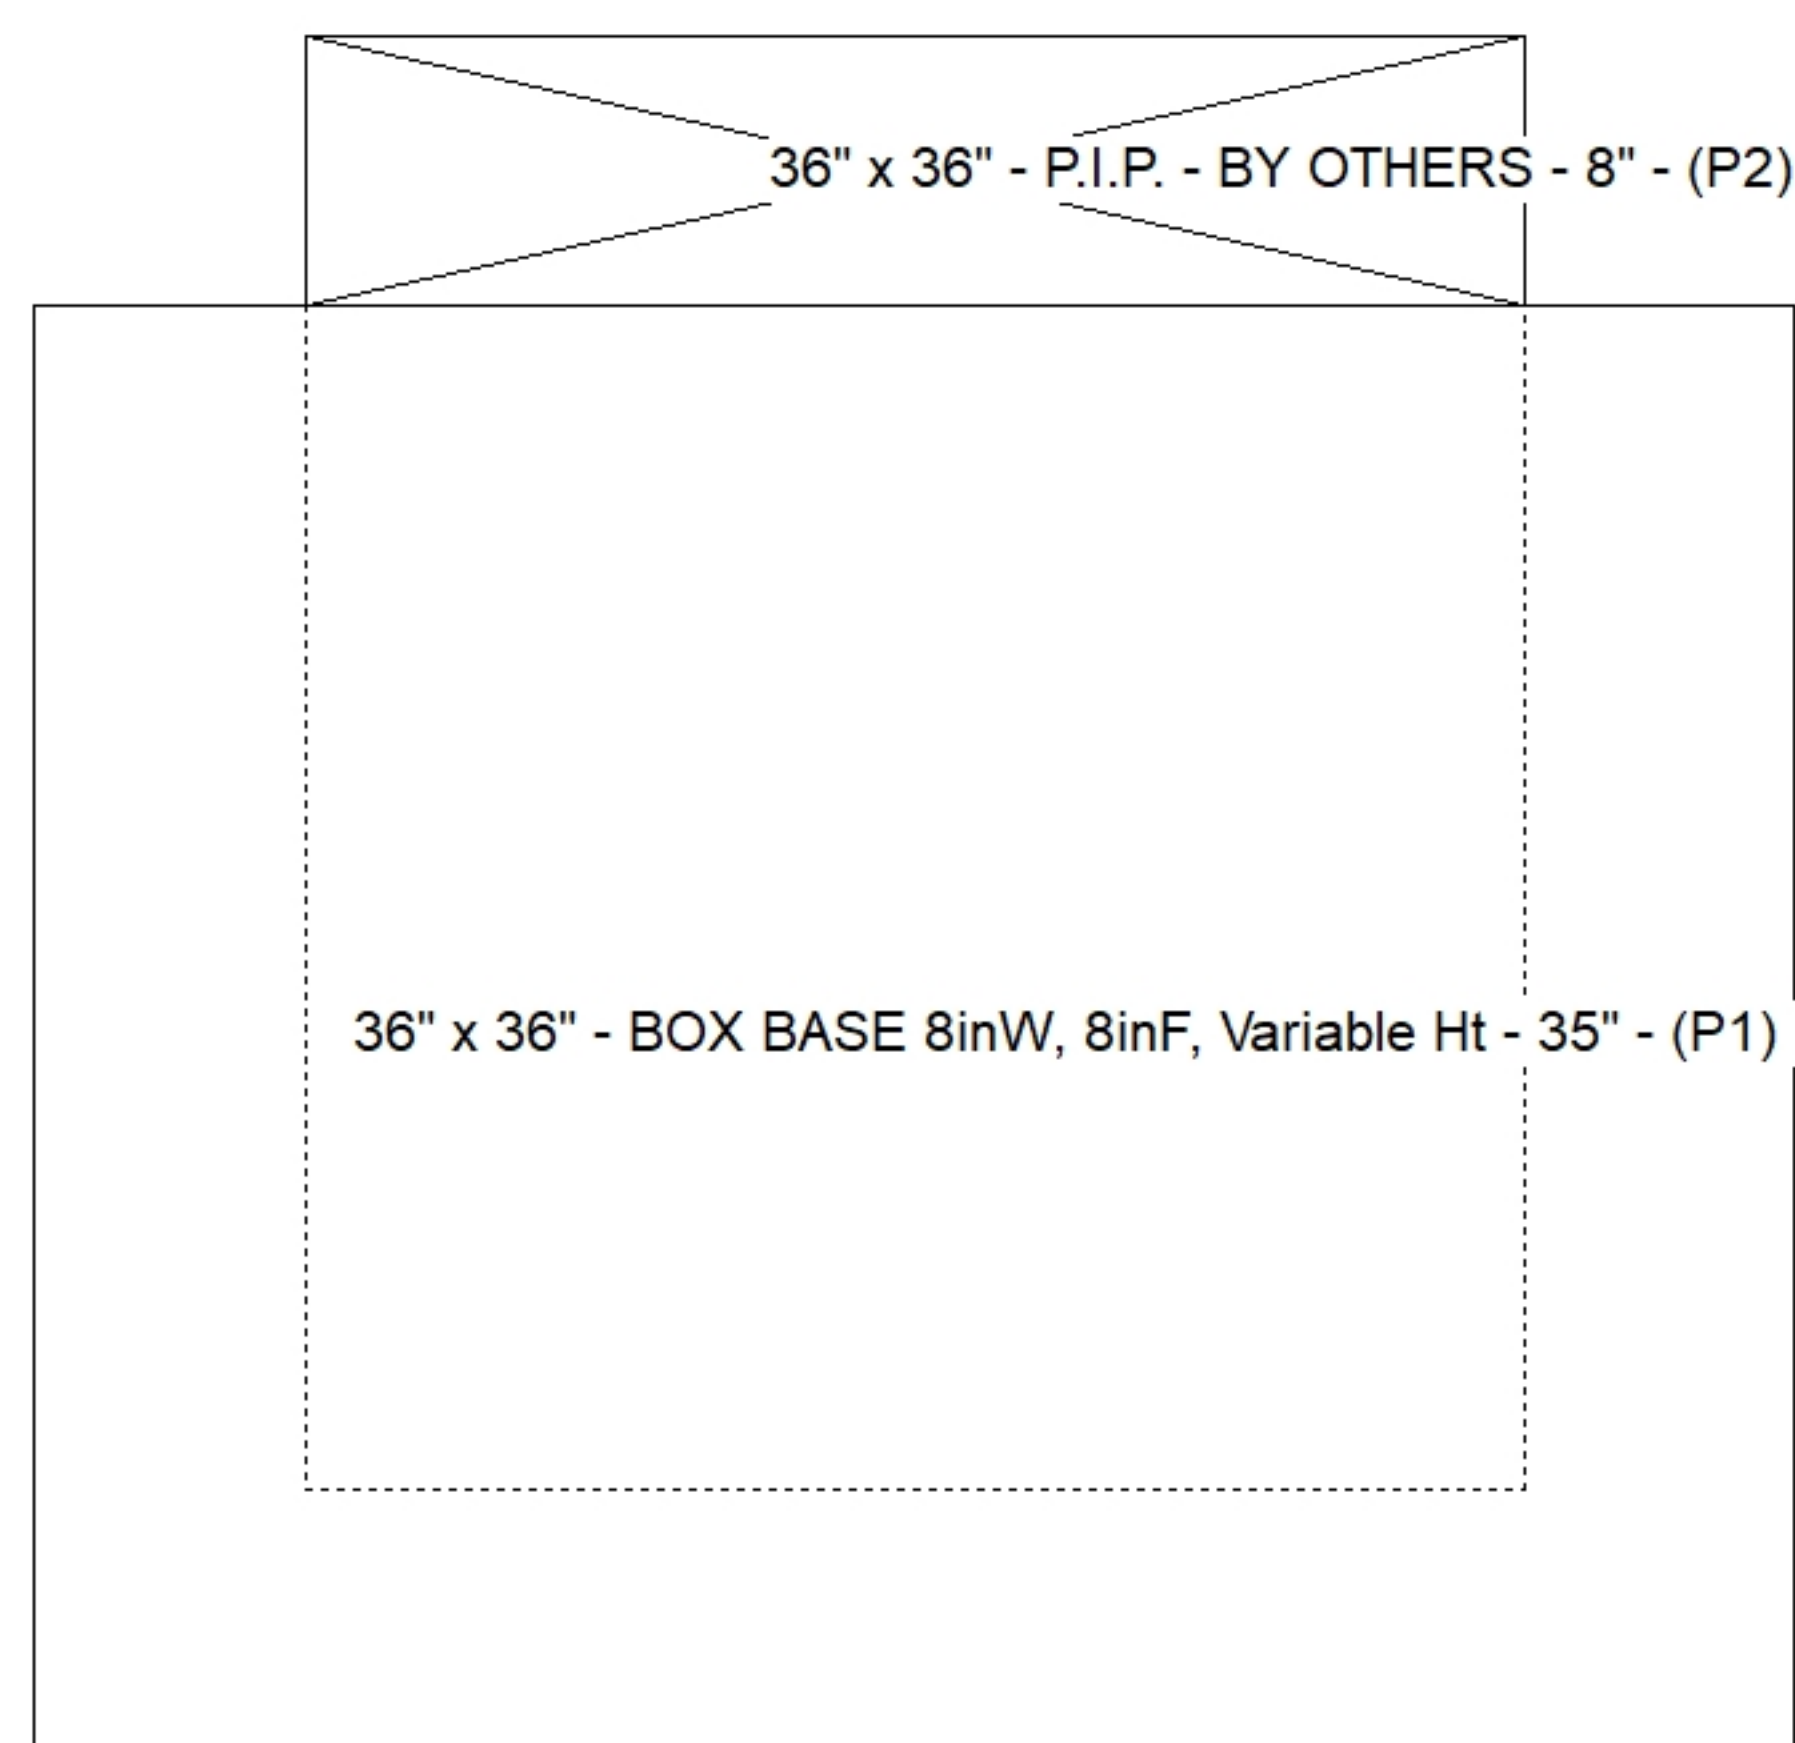

SUBMITTAL
APPROVED BY:
