

Plant: 100

6/16/2026 1:23:35 PM

P3 CUSTOM WALL

WALL PANEL 6" THICK F/F

	466 lb
	1398 lb
	1398 lb
	0 lb

Structure Total:	3261 lb

Structure Notes: .


1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28" DAYS.
3. SMOOTH FORM FINISH ON THE FRONT SURFACE.
4. 3/4" CHAMFER ON ALL LONG EDGES.

REINFORCING PER ASTM A615 (GRADE 60).
 -VERTICAL BARS = #4 BARS AT 12" C/C
 -HORIZONTAL BARS = #6 BARS EQUALLY SPACED
 (10" MAX.)

Rim: 692' Rim to Invert: 2' Slack: 0" Sump: 60" Step Position:


[illegible]

RIGHT-SIDE UP VIEW (int. dimensions)



Note:
See attached typical drawing
for reinforcing and lifting details.

INSIDE WALL DIMENSIONS






Coating (Int):	
Coating (Ext):	

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 0"
Floor Height: 0"

Height (Int): 12"
Height (Ext): 12"

Weight (Net): 466 lb
Volume (Net): 0.12cu.yd

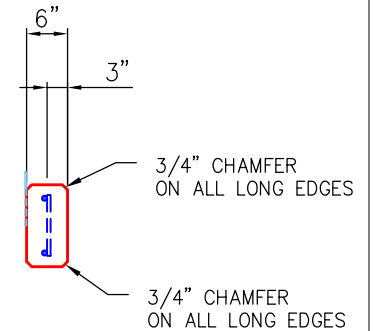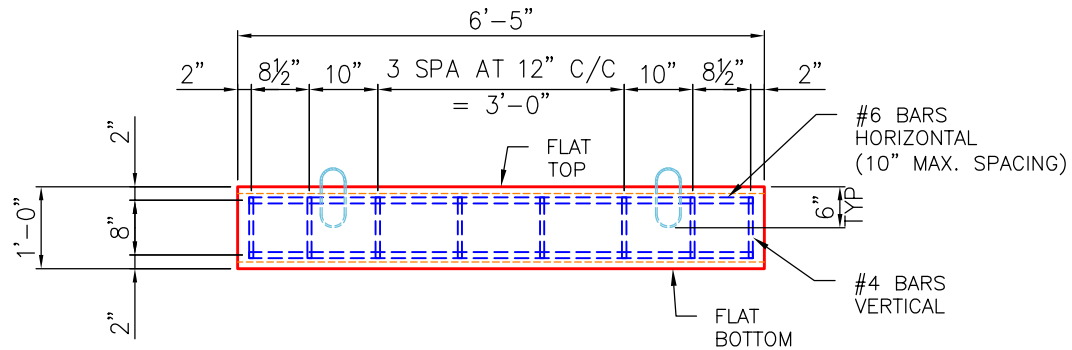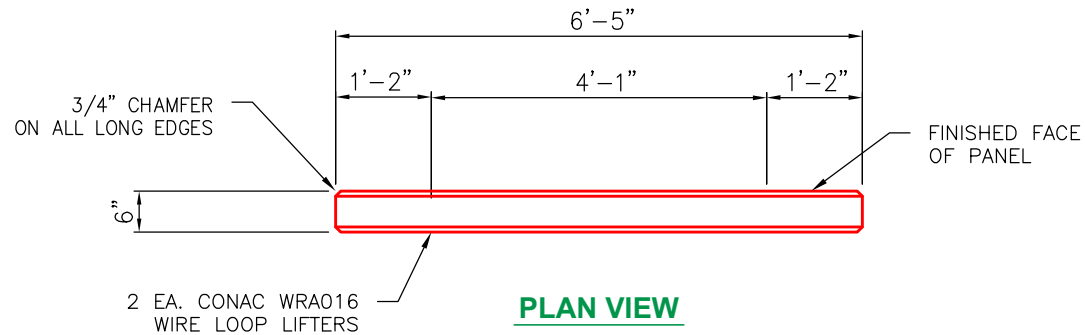

GENERAL NOTES:

1. MANUFACTURED ASTM C913 SPECIFICATIONS.
2. CONCRETE: 4,000 PSI MINIMUM AT 28 DAYS.
3. REINFORCING: AS PER PLAN DESIGN (GRADE 60).
4. CONAC 5CA14 ANCHORS CAST IN FOR HANDLING.
5. WEIGHT = 472 LBS
6. 1 REQUIRED.

REVISION INFORMATION				SUBMITTAL DESCRIPTION: WALL PANEL 6.50' LG x 6" THK.	
REV. 	DATE:	NO REVISIONS TO DATE		CUSTOMER: HALL CONTRACTING OF KY INC.	
				PROJECT: MITCHELL HILL ROAD PROJECT	
				STRUCTURE ID.: WALL PANEL 6" THK (78" LG x 12" HT)	
				SALES ORDER NO: 26-1333	
				CHECK: B. SMITH	DRAWN BY: J. HORSLEY
				DATE: 04/20/26	SCALE: NTS PG. 1 of 1
