


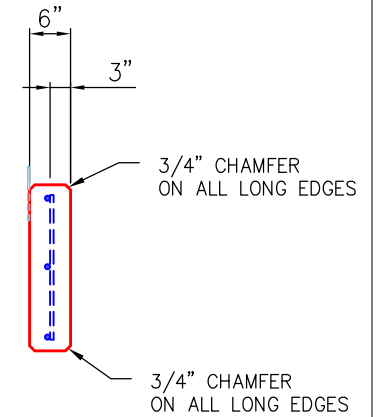
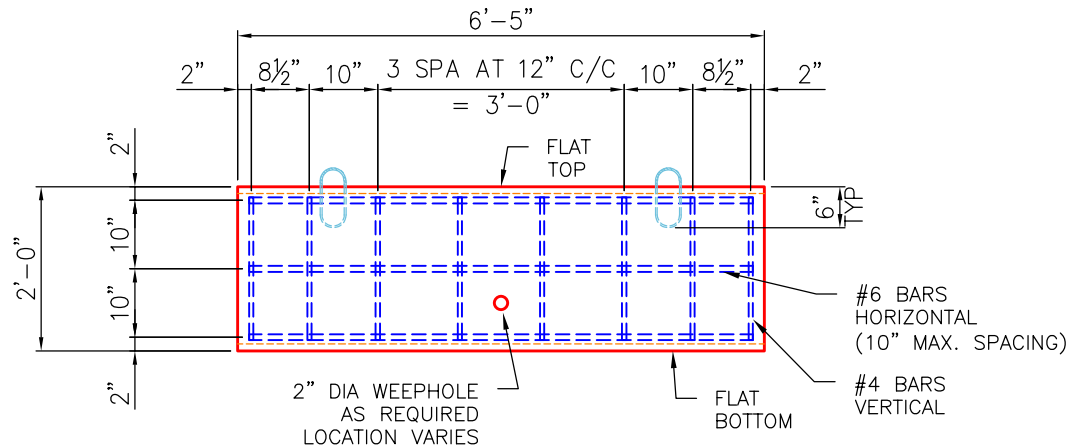


Job Name: 26-1333 - Mitchell Hill Road Project Job Location: Louisville, KY 40118 Contractor: Hall Contracting of Kentucky Inc					Plant: 100 6/16/2026 1:23:35 PM		Tech: J. Horsley PC: J. Jarvis				
Structure ID: WALL P22-P23											
P2 CUSTOM WALL				WALL PANEL 6" THICK F/F							
P3) 77" x 6" - WALL PANEL 6" THICK F/F - 3.00' HT x 6.42' LONG P2) 77" x 6" - WALL PANEL 6" THICK F/F - 2.00' HT x 6.42' LONG P1) 77" x 6" - WALL PANEL 6" THICK F/F - 2.00' HT x 6.42' LONG 1) Hole - 2						1398 lb 932 lb 932 lb 0 lb ----- Structure Total: 3261 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETER = 4,000 PSI AT 28" DAYS. 3. SMOOTH FORM FINISH ON THE FRONT SURFACE. 4. 3/4" CHAMFER ON ALL LONG EDGES. REINFORCING PER ASTM A615 (GRADE 60). -VERTICAL BARS = #4 BARS AT 12" C/C -HORIZONTAL BARS = #6 BARS EQUALLY SPACED (10" MAX.)			
Rim: 691' Rim to Invert: 1.5' Slack: 0" Sump: 66" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) (P3) (P2) << (P1)  Note: See attached typical drawing for reinforcing and lifting details. INSIDE WALL DIMENSIONS (P2) 											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: Flat		Wall Thickness: 0" Floor Height: 0"		Height (Int): 24" Height (Ext): 24"		Weight (Net): 932 lb Volume (Net): 0.24cu.yd	

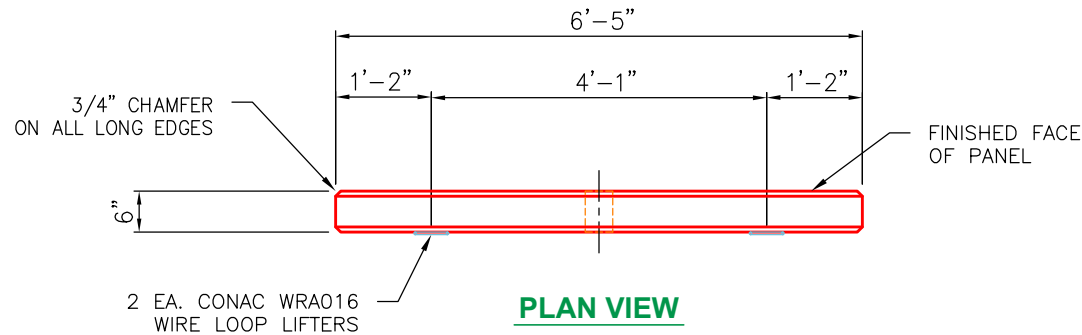

SIDE VIEW

END VIEW

GENERAL NOTES:

1. MANUFACTURED ASTM C913 SPECIFICATIONS.
2. CONCRETE: 4,000 PSI MINIMUM AT 28 DAYS.
3. REINFORCING: AS PER PLAN DESIGN (GRADE 60).
4. CONAC 5CA14 ANCHORS CAST IN FOR HANDLING.
5. WEIGHT = 914 LBS
6. 21 REQUIRED.

REVISION INFORMATION				SUBMITTAL DESCRIPTION: WALL PANEL 6.50' LG x 6" THK.	
REV. 	DATE:	NO REVISIONS TO DATE		CUSTOMER: HALL CONTRACTING OF KY INC.	
				PROJECT: MITCHELL HILL ROAD PROJECT	
				STRUCTURE ID.: WALL PANEL 6" THK (78" LG x 24" HT)	
				SALES ORDER NO: 26-1333	
				CHECK: B. SMITH	DRAWN BY: J. HORSLEY
				DATE: 04/20/26	SCALE: NTS PG. 1 of 1
