

Contractor: Hall Contracting of Kentucky Inc

TECH: J. Horsley

Plant: 100



Size: 77" x 6"


Rim to Invert: 1'

Floor Height: 0"

Slack: 0"



-HORIZONTAL BARS = #6 BARS EQUALLY SPACED (10" MAX.)

Structure Total: 2795 lb

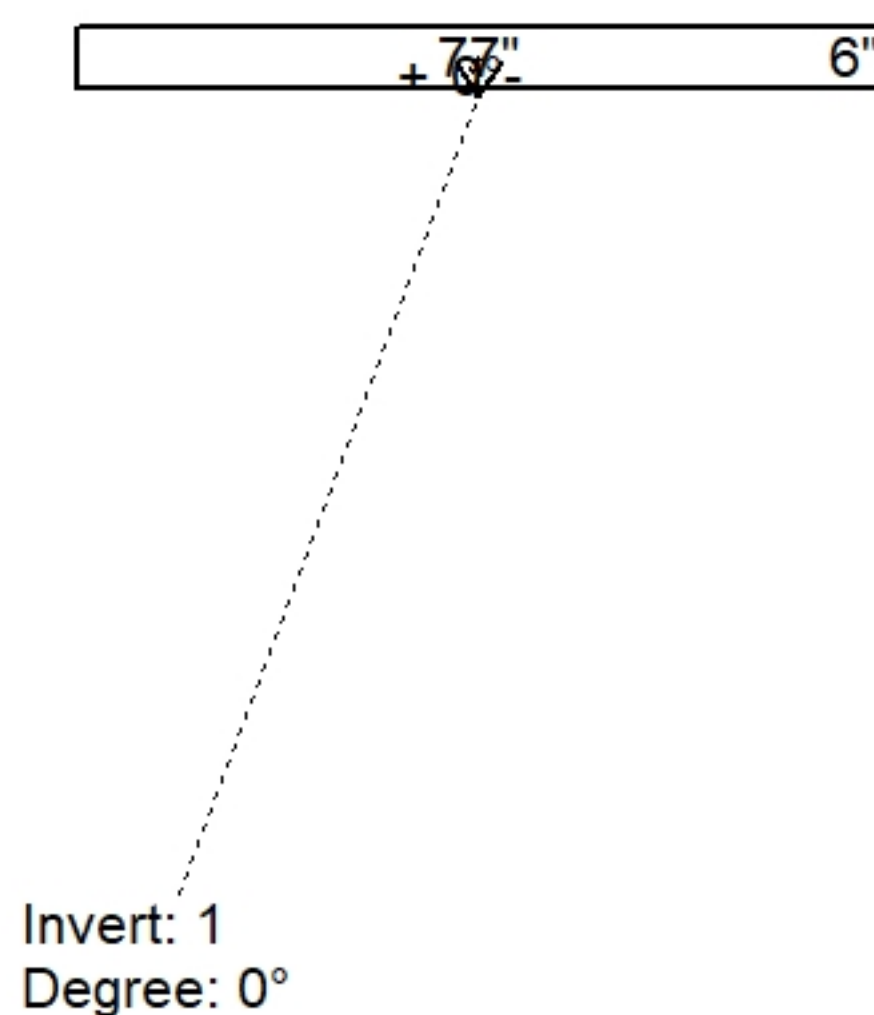

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	690'							
Reducer								
Invert 1	689'	0°	2" WEEP HOLE	2"	2"	Hole 2	24"	P2
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Cast (Int. Dim.) - Interior Dimensions

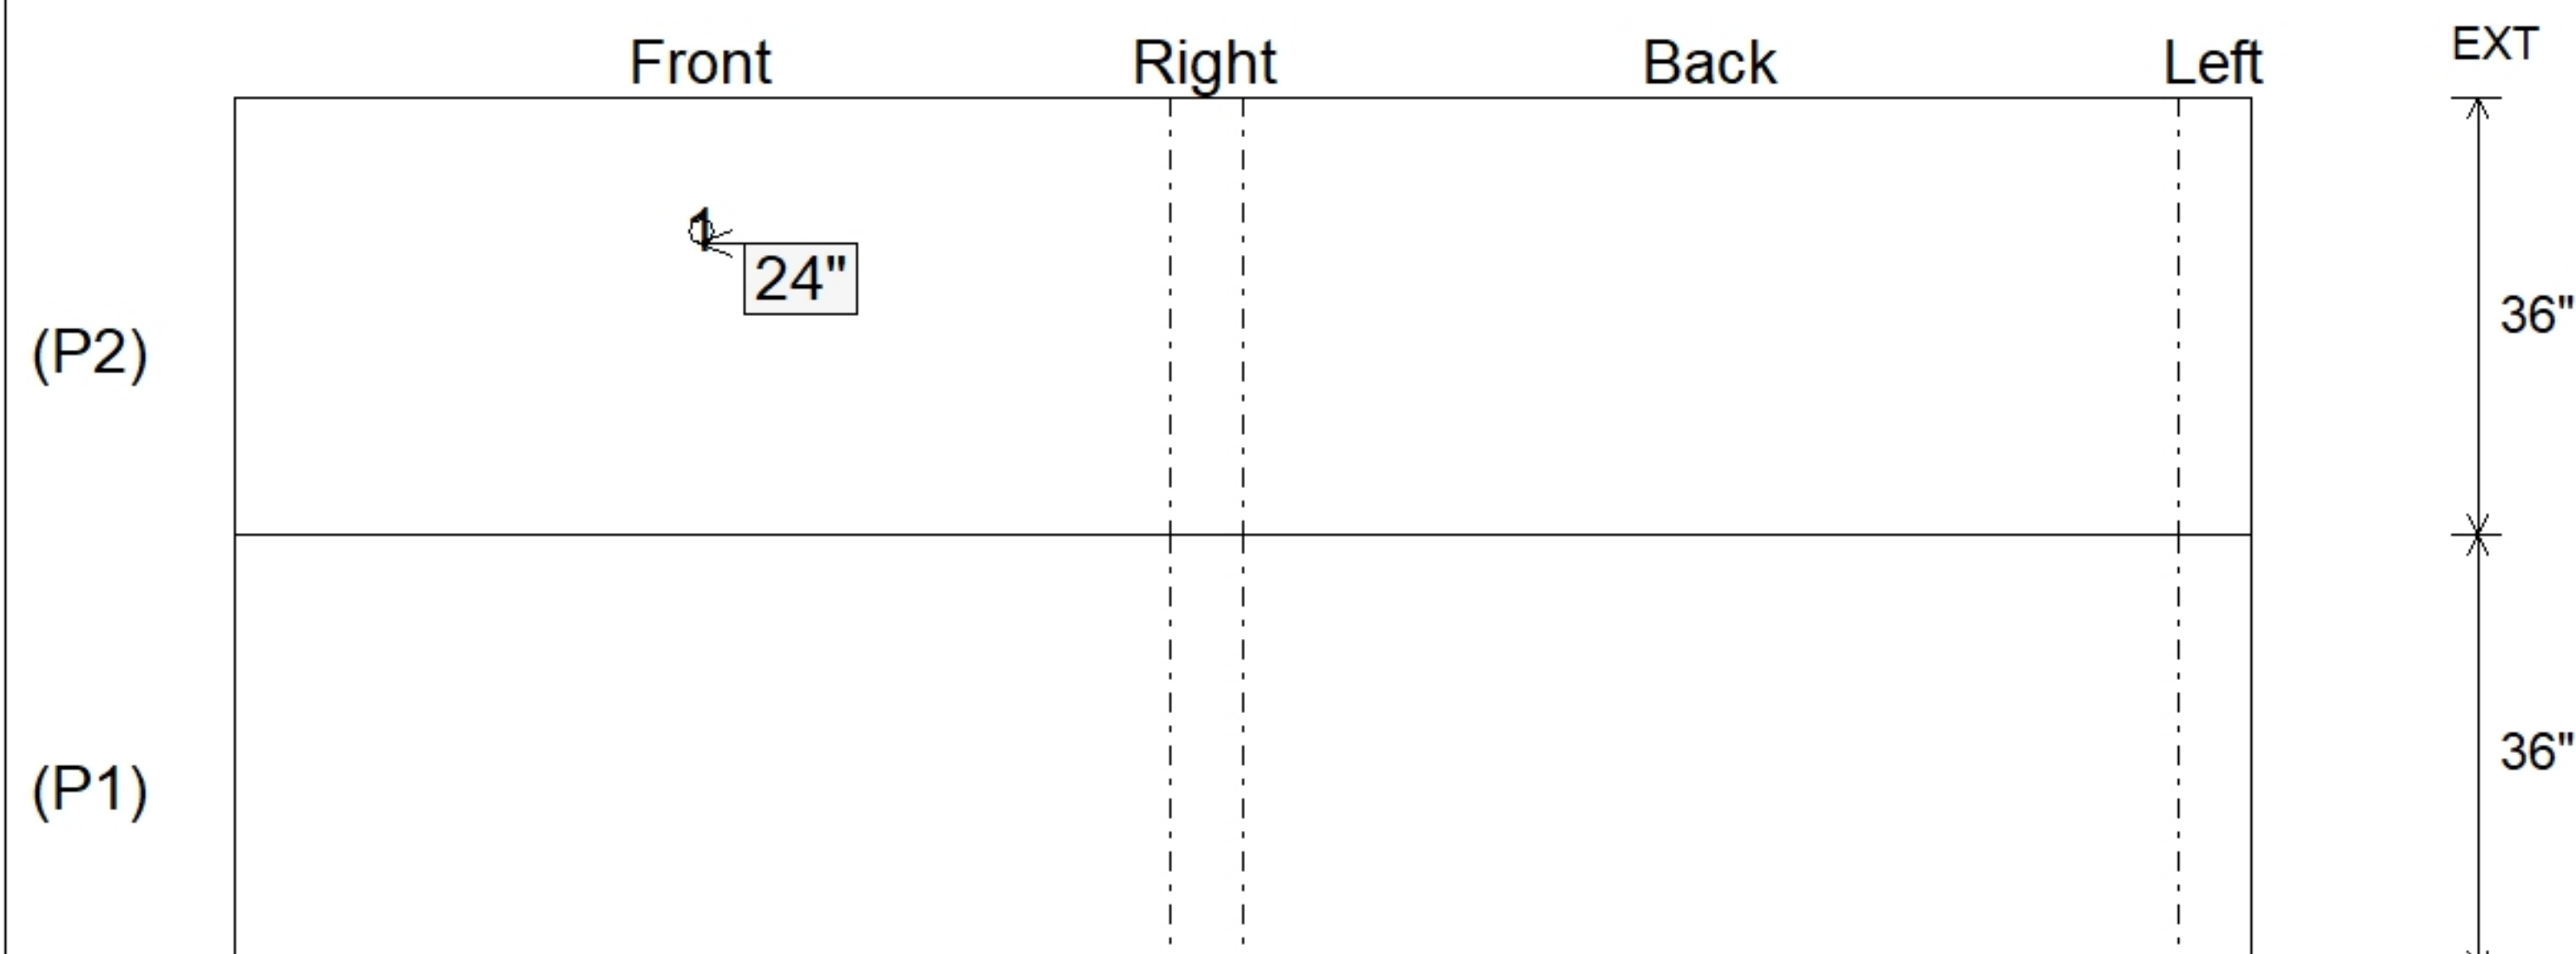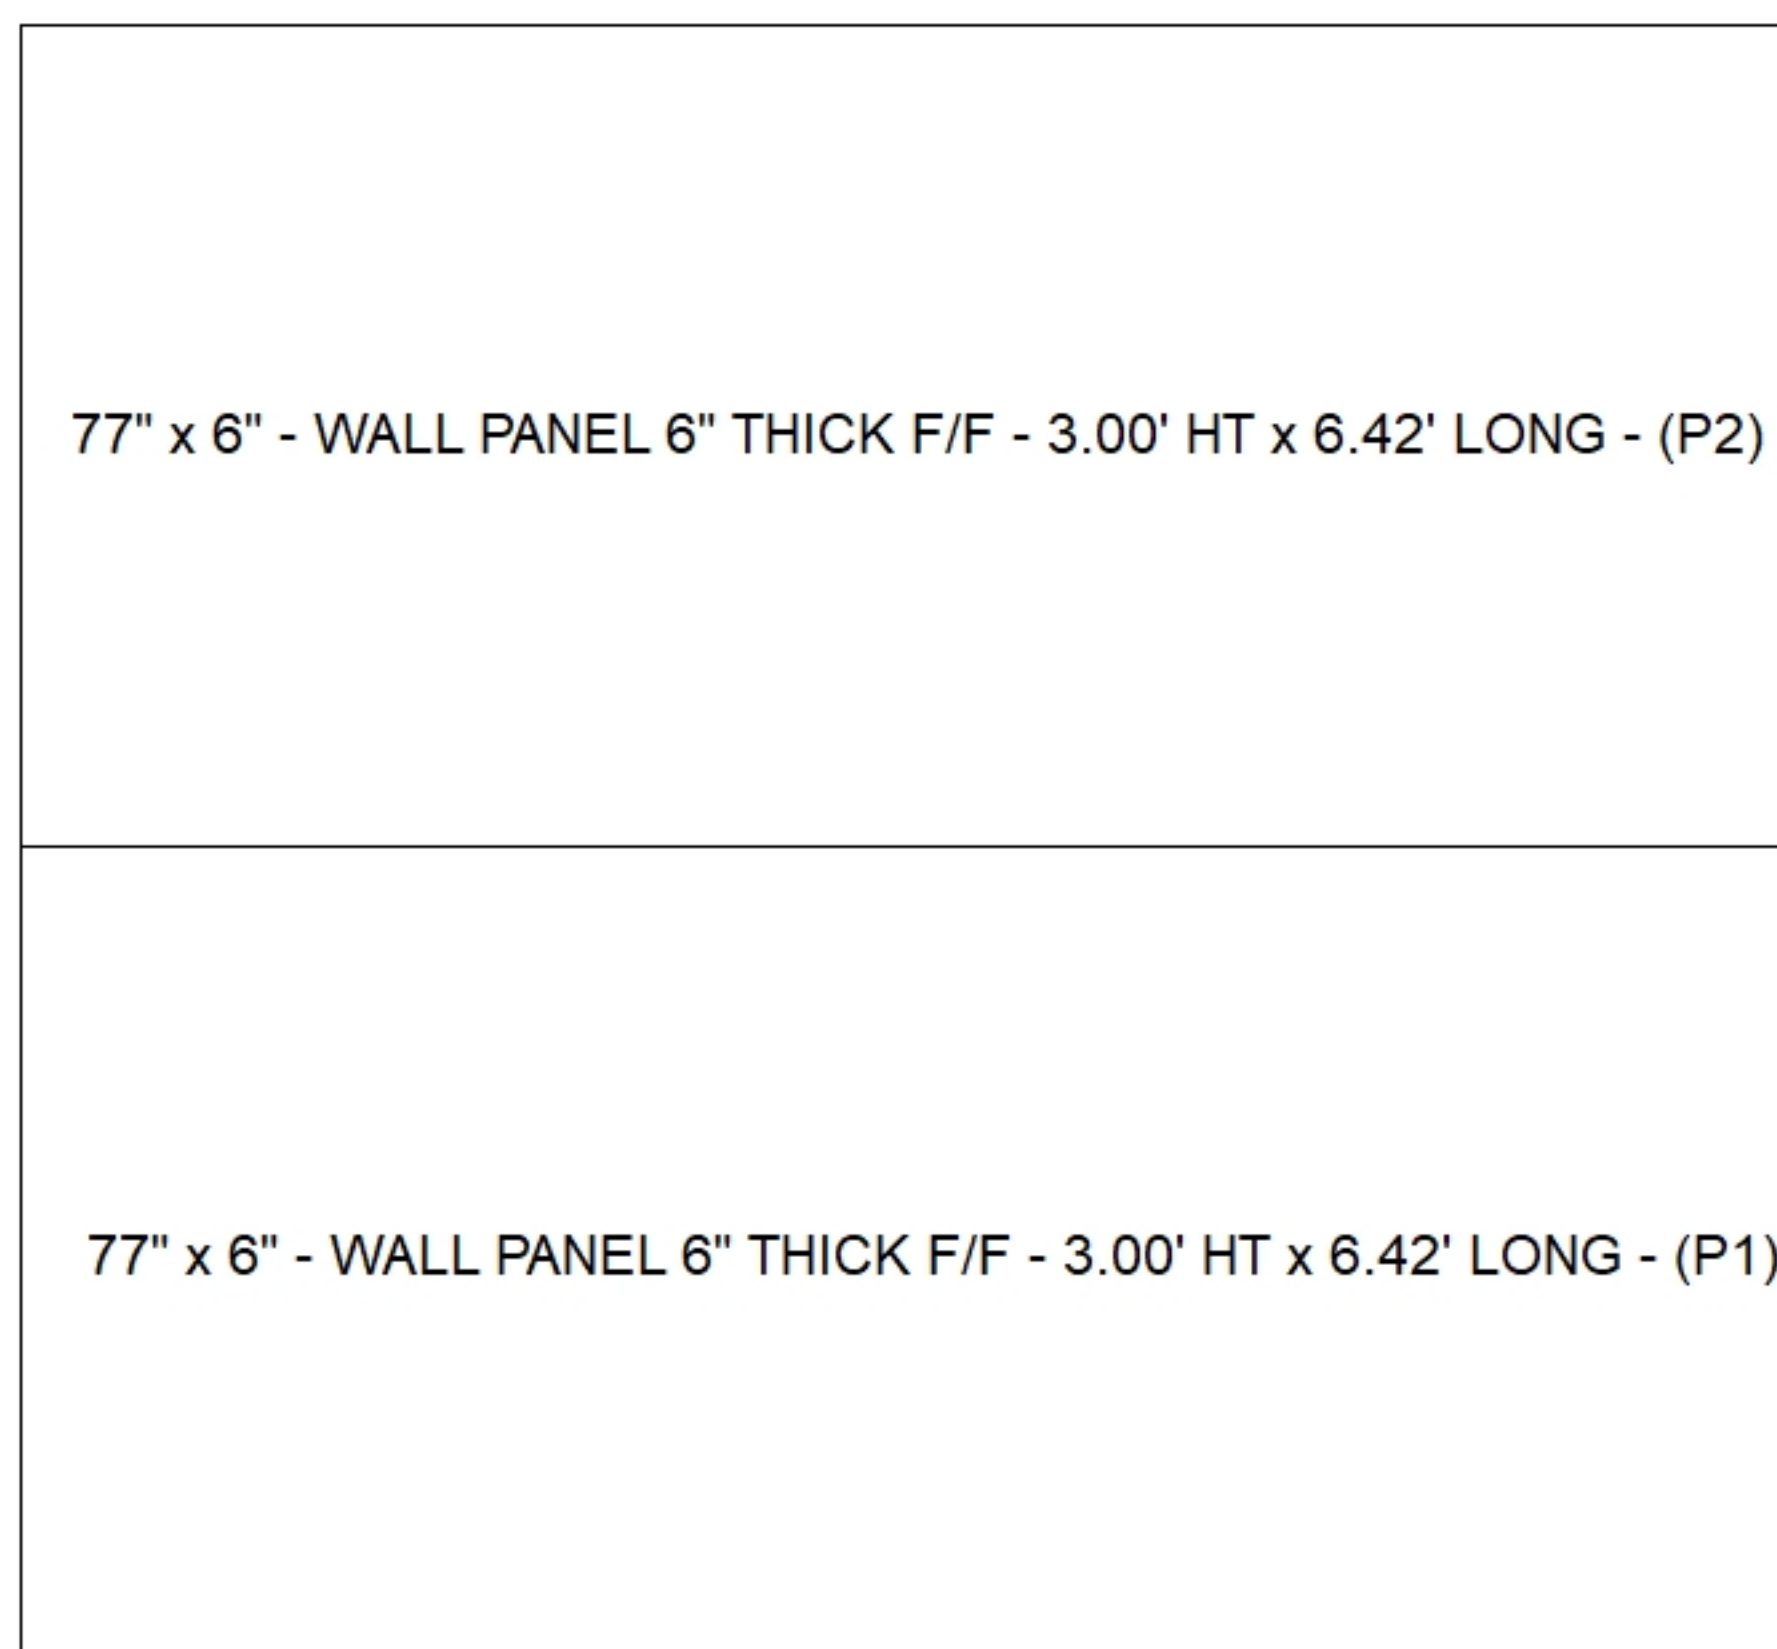

SUBMITTAL
APPROVED BY:
