

Job Name: 26-1364 - Ollie Car Wash
Job Location: Owensboro, KY
Contractor: Winwater Hartford KY Co.

Plant: 100

7/20/2026 6:51:55 PM

Tech: Jared - F

PC: A. Chambers



Structure ID: 2000-GT-TANK-3

P1 BX60126-06W06F-FTVF

BOX BASE 6inW, 6inF, Variable Ht F/n

- P4) 24" - CASTING HEIGHT - 7"
P3) 24" - GRADE RING F/F - 3"
P2) 60" x 126" - CB FLAT TOP 6"W w/(2) 24" HOLES F/F - 8"
P1) 60" x 126" - BOX BASE 6inW, 6inF, Variable Ht F/n - 72"
1) CASTING - HOE MC-315 F/C Storm
2) 24" - Con Seal CS-102 1.00"
2) Hole - 10

0 lb
202 lb
6064 lb
19278 lb
258 lb
0 lb
0 lb


Structure Total: 25803 lb

Structure Notes:

1. PER ASTM C-890-13 SPECIFICATIONS.
2. CONCRETE = 4,500 PSI AT 28 DAYS.
3. NO STEPS AND NO FLOW CHANNEL.
4. CASTING BY ICAST (HOE MC-315 F/C "STORM")


REINFORCING PER ASTM A615 (GRADE 60)
- TOP SLAB (As .47) #5 BARS AT 8" C.C.E.W.
- WALLS (As .47) #5 BARS AT 8" C.C.E.W.
- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.

Rim: 7.5' Rim to Invert: 6' Slack: 0" Sump: 18" Step Position:

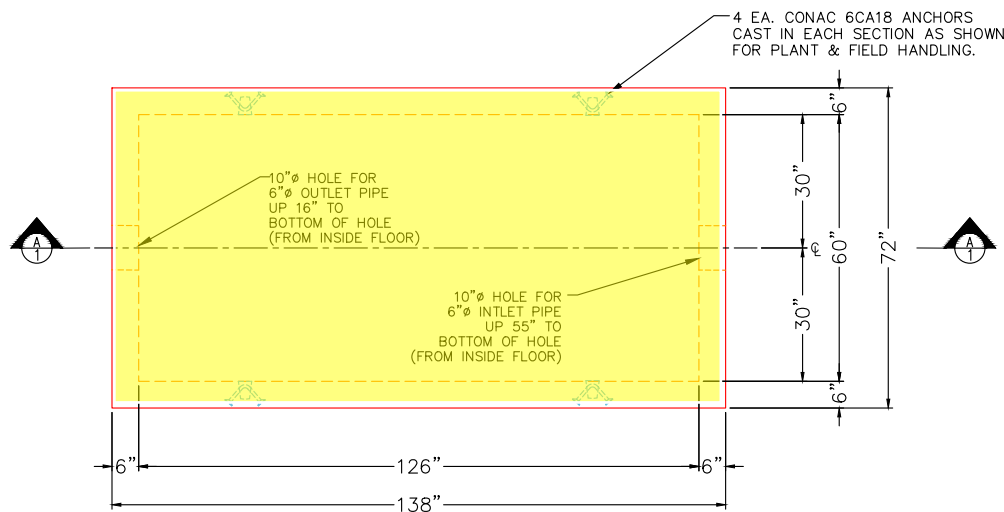

PLAN VIEW
(RIGHTSIDE-UP)

FIRST POUR DRAWING

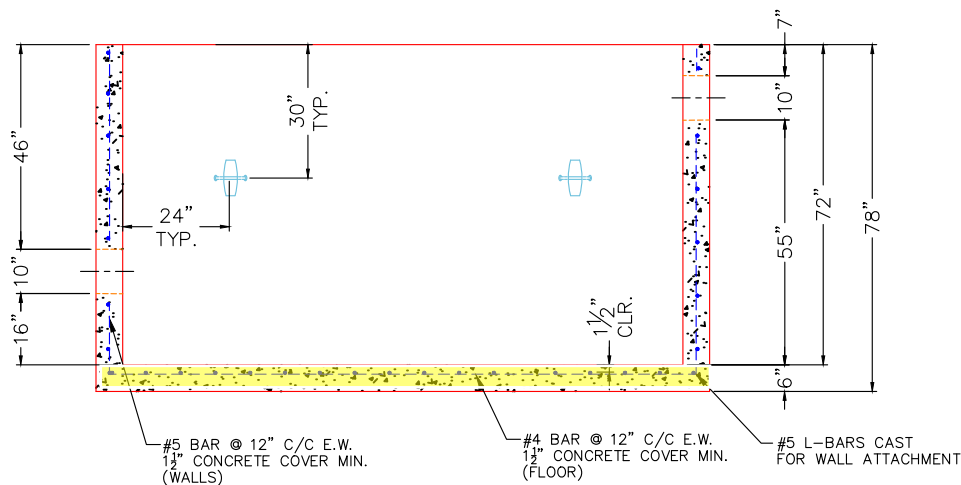

NOTES:

1. PER ASTM C-890-13 LATEST REVISION.
2. CONCRETE = 4,500 PSI AT 28 DAYS.
3. REINFORCING PER ASTM A615 (GRADE 60).
(H-20 TRAFFIC RATED DESIGN)
4. SEALED WITH 1" CS-102 BUTYL SEALANT
5. POUR BASE, THEN POUR INTERIOR BAFFLE.
6. **FIRST POUR (BASE SLAB) - 5,002 LBS**
SECOND POUR (WALLS) - 14,276 LBS

SECTION A-A
(RIGHTSIDE-UP)

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 6"
Floor Height: 6"

Height (Int): 72"
Height (Ext): 78"

Weight (Net): 19278 lb
Volume (Net): 4.92cu.yd

Job Name: 26-1364 - Ollie Car Wash
Job Location: Owensboro, KY
Contractor: Winwater Hartford KY Co.

Plant: 100

7/20/2026 6:51:55 PM

Tech: Jared - F

PC: A. Chambers



Structure ID: 2000-GT-TANK-3

P1 BX60126-06W06F-FTVF

BOX BASE 6inW, 6inF, Variable Ht F/n

- P4) 24" - CASTING HEIGHT - 7"
P3) 24" - GRADE RING F/F - 3"
P2) 60" x 126" - CB FLAT TOP 6"W w/(2) 24" HOLES F/F - 8"
P1) 60" x 126" - BOX BASE 6inW, 6inF, Variable Ht F/n - 72"
1) CASTING - HOE MC-315 F/C Storm
2) 24" - Conseal CS-102 1.00"
2) Hole - 10

0 lb
202 lb
6064 lb
19278 lb
258 lb
0 lb
0 lb

25803 lb


Structure Total:

Structure Notes:

1. PER ASTM C-890-13 SPECIFICATIONS.
2. CONCRETE = 4,500 PSI AT 28 DAYS.
3. NO STEPS AND NO FLOW CHANNEL.
4. CASTING BY ICAST (HOE MC-315 F/C "STORM")


REINFORCING PER ASTM A615 (GRADE 60)
- TOP SLAB (As .47) #5 BARS AT 8" C.C.E.W.
- WALLS (As .47) #5 BARS AT 8" C.C.E.W.
- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.

Rim: 7.5' Rim to Invert: 6' Slack: 0" Sump: 18" Step Position:

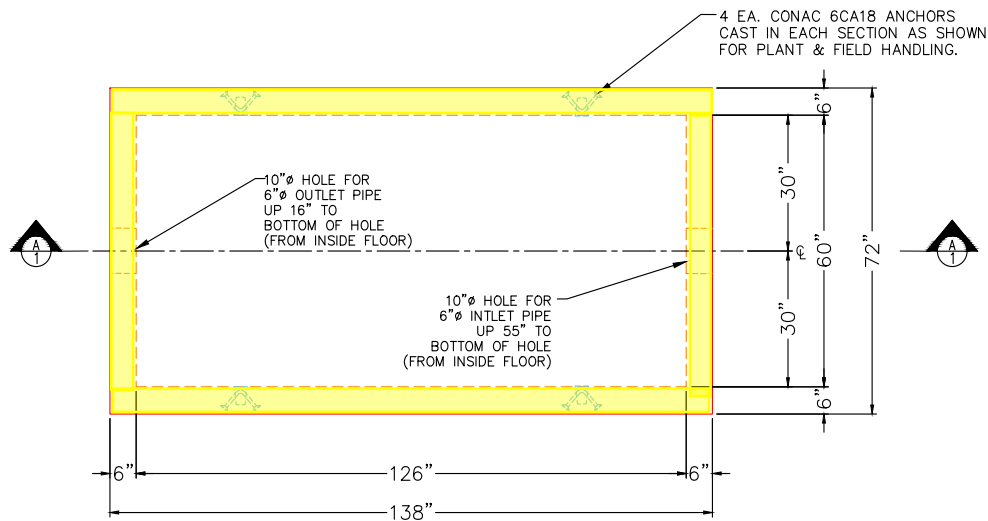

PLAN VIEW
(RIGHTSIDE-UP)

SECOND POUR DRAWING

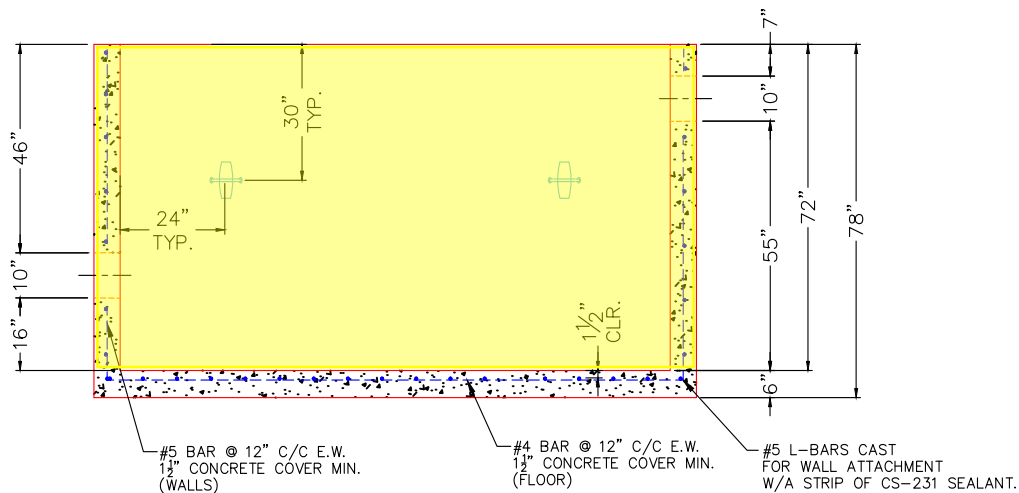

NOTES:

1. PER ASTM C-890-13 LATEST REVISION.
2. CONCRETE = 4,500 PSI AT 28 DAYS.
3. REINFORCING PER ASTM A615 (GRADE 60). (H-20 TRAFFIC RATED DESIGN)
4. SEALED WITH 1" CS-102 BUTYL SEALANT
5. POUR BASE, THEN POUR INTERIOR BAFFLE.
6. FIRST POUR (BASE SLAB) - 5,002 LBS
SECOND POUR (WALLS) - 14,276 LBS

SECTION A-A
(RIGHTSIDE-UP)

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: n/a

Wall Thickness: 6"
Floor Height: 6"

Height (Int): 72"
Height (Ext): 78"

Weight (Net): 19278 lb
Volume (Net): 4.92cu.yd
