

Contractor: Kauffeld Brothers Construction

Plant: Beaver Dam




Slack: 4"

- FLOOR (As .31) #5 BARS AT 12: C.C.E.W.

2) Hole - 24


0 lb

Structure Total: 8532 lb

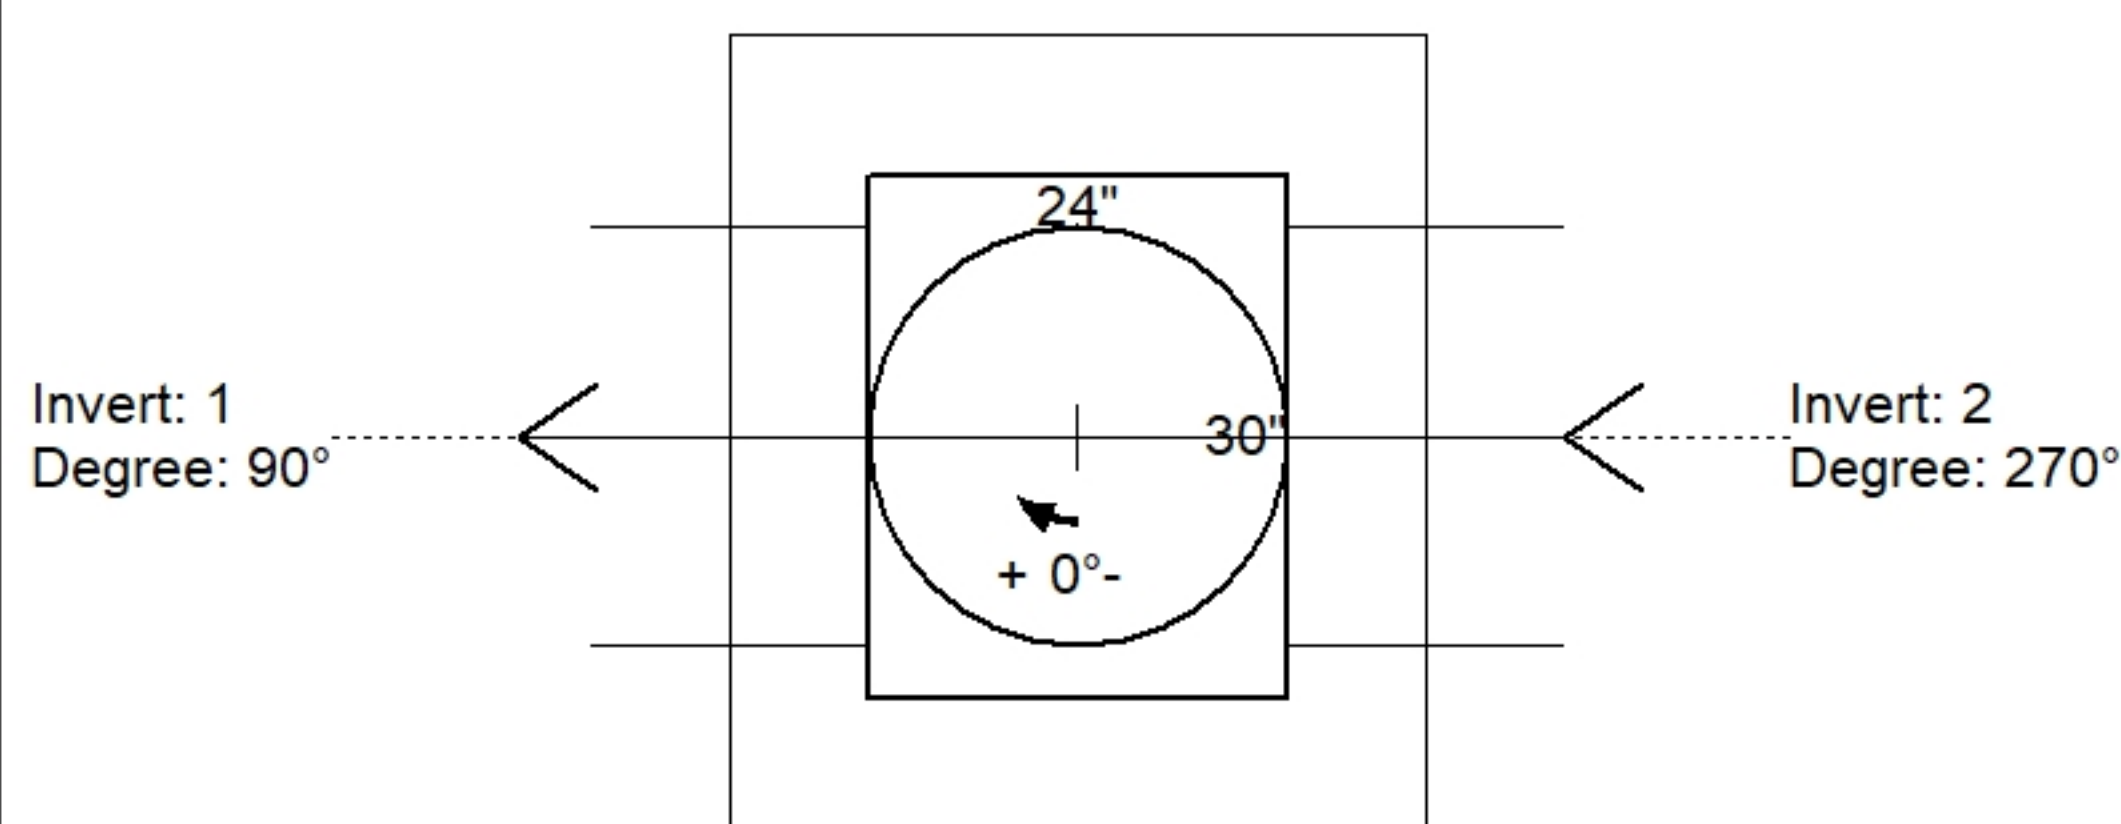

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	779'							
Reducer								
Invert 1	772'	90°	18" HDPE	21.2"	24"	Hole 24	-3"	P1
Invert 2	772'	270°	18" HDPE	21.2"	24"	Hole 24	-3"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

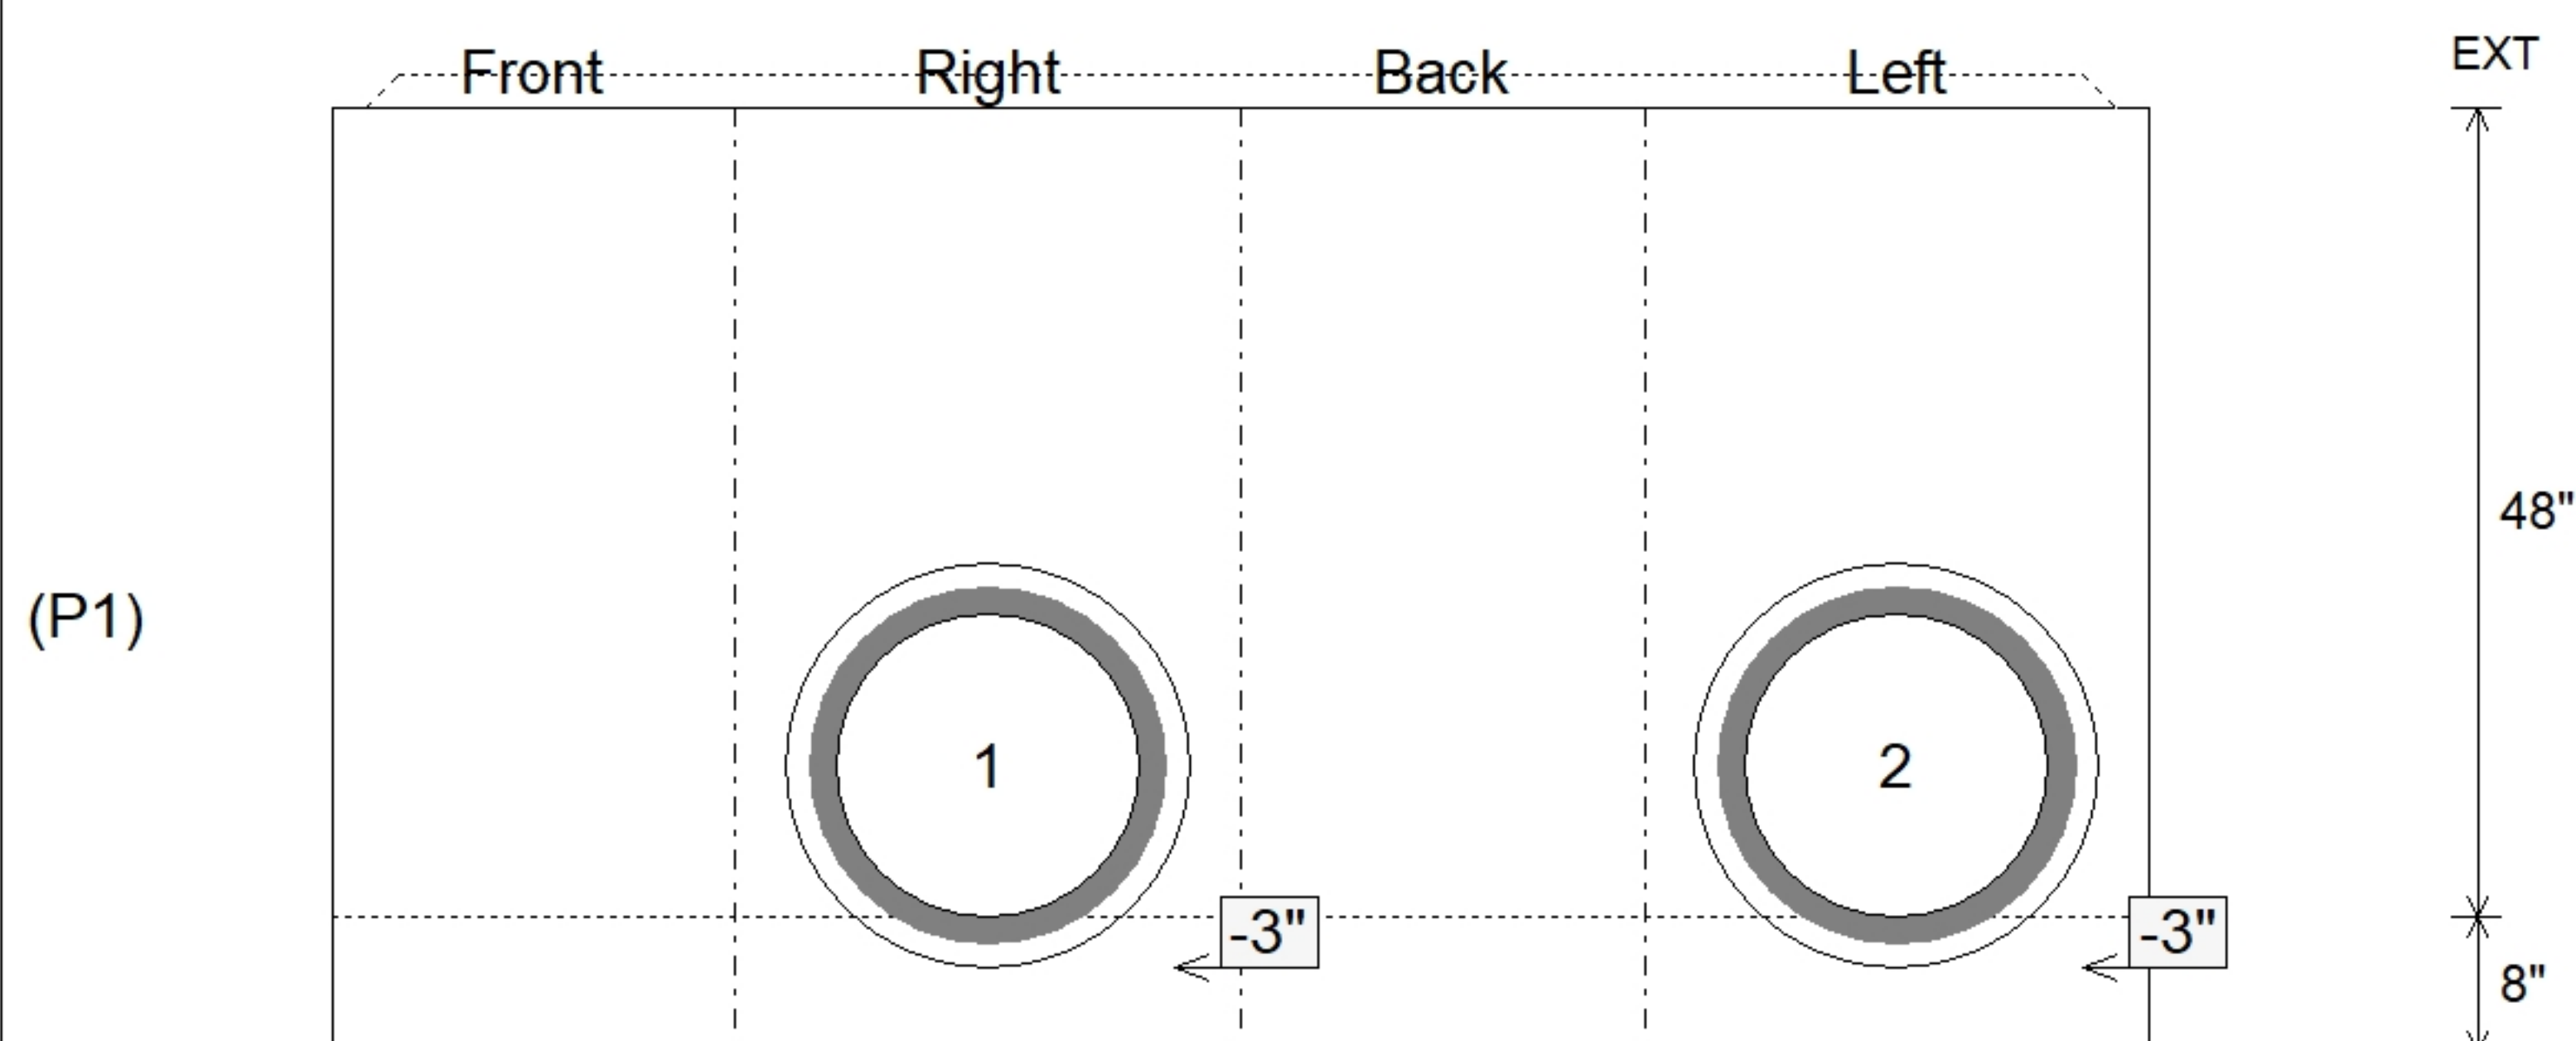

SUBMITTAL
APPROVED BY:
