

Job Name: 26-1421 855355 Camp Ground Road
 Job Location: Louisville, KY
 Contractor: Contech Engineering Solutions

Plant: Beaver Dam
 2/25/2026 3:28:13 PM

Tech: S. Felletter
 PC: T. Sekula



Structure ID: 10-CS-5

P1 MH060BA18

MH BASE T/n

- P4) 30" - CASTING HEIGHT - 4"
- P3) 60" - MH FLAT TOP SPEC. (30" ECC HOLE) F/G - 13"
- P2) 60" - MH RISER T/G - 72"
- P1) 60" - MH BASE T/n - 18"
- 1) CVSTENCILING
- 1) ASSEMBLY REQUIRED
- 2) 60" - Conseal CS-102 1.00"
- 2) Hole - 16

0 lb
 2589 lb
 7303 lb
 4612 lb
 0 lb
 0 lb
 0 lb
 0 lb
 0 lb

 Structure Total: 14504 lb

Structure Notes:
 4" CASTING BY OTHERS

 LIFTING ANCHORS TO BE INSTALLED
 ON THE OUTSIDE OF THE STRUCTURE

 ICAST TO INSTALL THE INTERNALS



 CONTECH'S LOGO AS WELL AS THE
 INLET AND OUTLET MUST BE
 STENCILED ONTO THE STRUCTURE

Rim: 444.5' Rim to Invert: 4.98' Slack: 10.84" Sump: 58.08" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimenions)

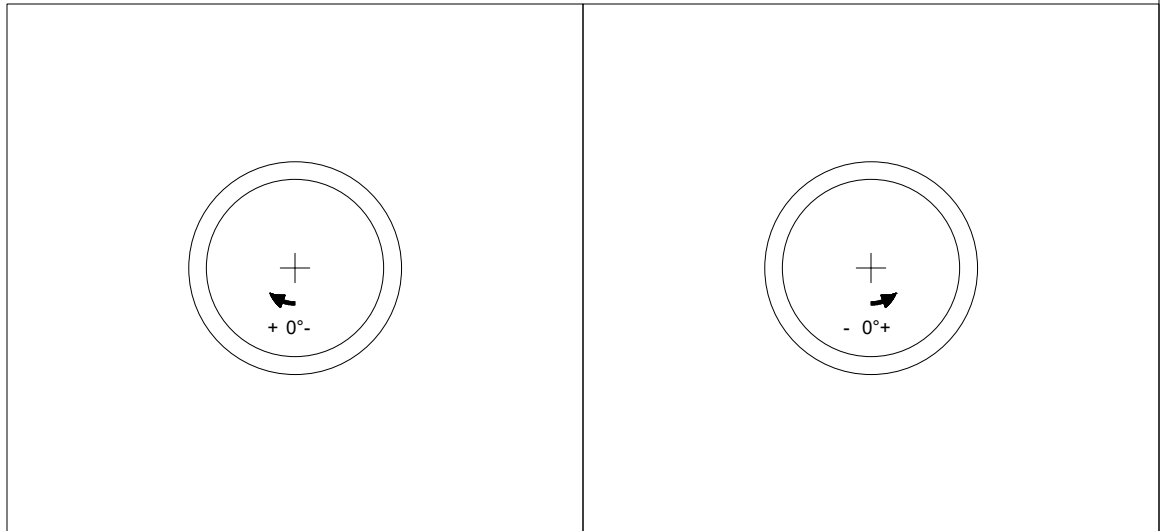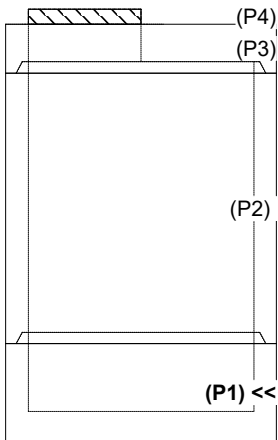

INSIDE WALL DIMENSIONS



Coating (Int):
 Coating (Ext):

Seam Up: Tongue
 Seam Dn: n/a

Wall Thickness: 6"
 Floor Height: 8"

Height (Int): 18"
 Height (Ext): 26"

Weight (Net): 4612 lb
 Volume (Net): 1.18cu.yd
